


IL 13 OVER TRIBUTARY TO RICHLAND CREEK- BELLEVILLE

NOTES

1. ALL SIGNS REQUIRED WILL BE SUPPLIED TO THE CONTRACTOR BY I.D.O.T.
2. THE CONTRACTOR SHALL FURNISH THE POSTS AND ERECT SIGNS AT THE LOCATIONS SHOWN ON THIS SHEET, AS DIRECTED BY THE R.E./R.T. THE POSTS SHALL REMAIN THE PROPERTY OF THE CONTRACTOR.
3. THE CONTRACTOR SHALL GIVE ILLINOIS DEPARTMENT OF TRANSPORTATION, BUREAU OF OPERATIONS TWO WEEKS NOTICE FOR SIGNS. THE CONTRACTOR SHALL PICK UP THE SIGNS AT THE T.M. BUILDING IN FAIRVIEW HGTS., AND RETURN THEM UPON COMPLETION OF THE CONTRACT.
4. THE ABOVE NOTED WORK SHALL BE PAID FOR AT THE CONTRACT UNIT PRICE, LUMP SUM, FOR WIDE LOAD SIGNING AND NO OTHER COMPENSATION WILL BE ALLOWED.
5. SIGN SPACING WILL BE 400' OR TO FIT FIELD CONDITIONS.
6. THE HEIGHT TO THE BOTTOM OF THE LOWEST SIGN SHALL NOT BE LESS THAN 6'.

SIGNS REQUIRED

- | | |
|---------------------------------------------|-----|
| MAX WIDTH
8 FT 6 IN
1/2 MILE
AHEAD | (1) |
| MAX WIDTH
8 FT 6 IN
2 MILES
AHEAD | (3) |
| MAX WIDTH
8 FT 6 IN
1 MILE
AHEAD | (1) |
| ILLINOIS
13 | (3) |
| EAST | (3) |

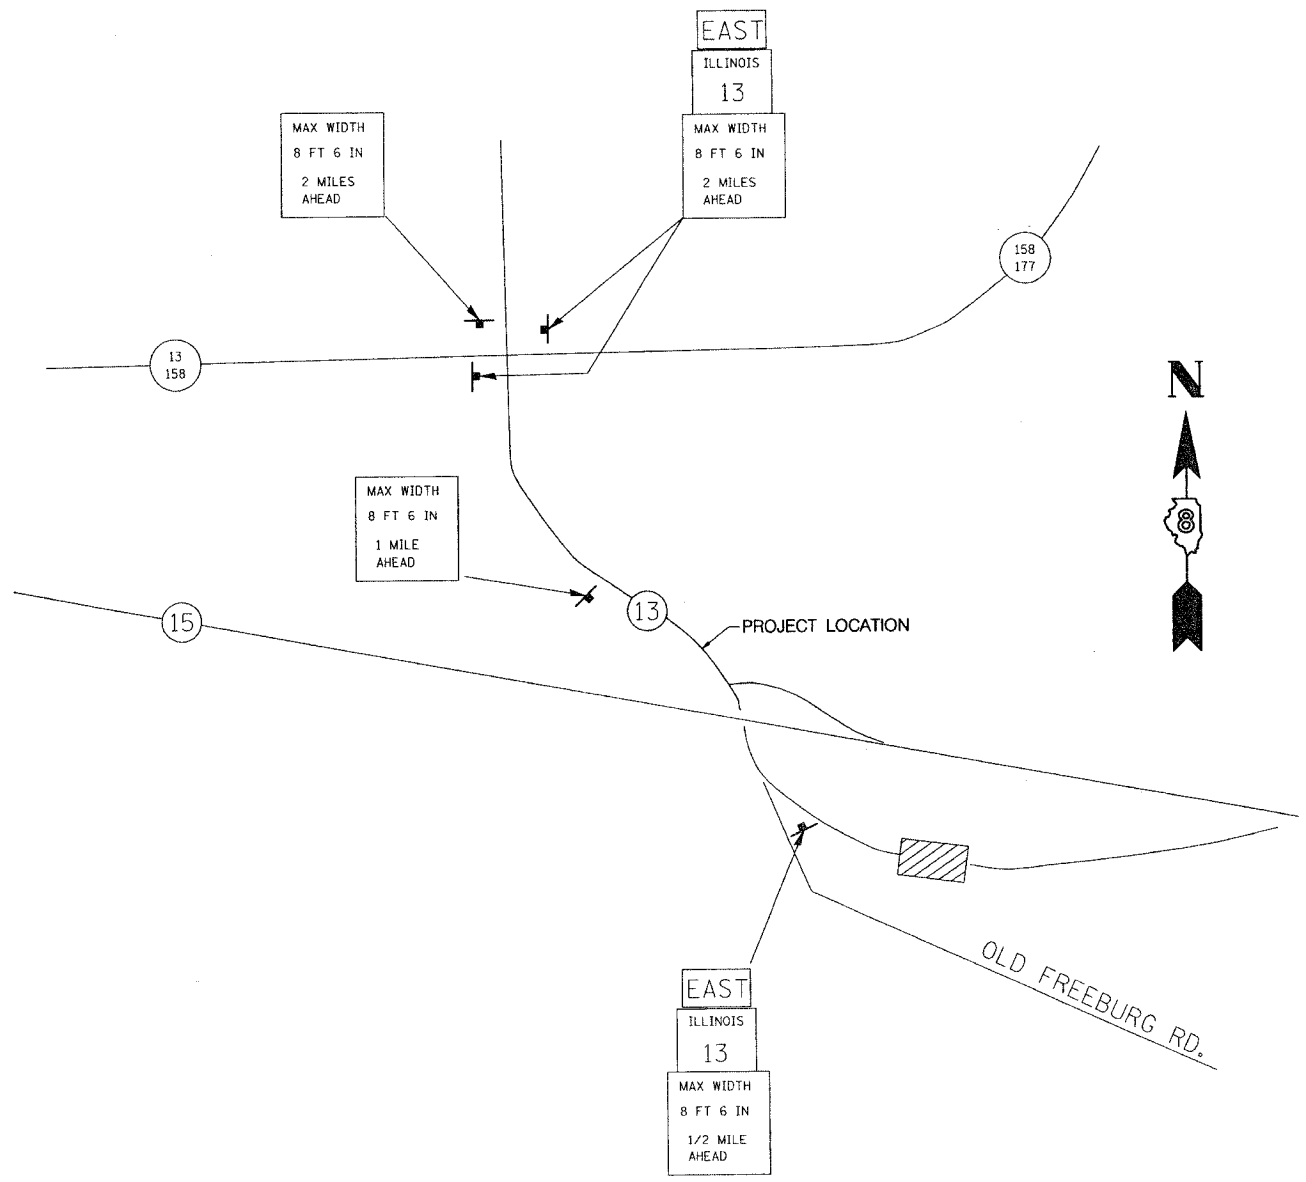

WIDTH RESTRICTION SIGNING LOCATIONS
(NOT TO SCALE)

STAGE CONSTRUCTION TRAFFIC DETAILS
 F.A.P. ROUTE 103 (OLD IL. ROUTE 13)
 OVER TRIBUTARY OF RICHLAND CREEK
 SECTION 27-3BR
 ST. CLAIR COUNTY
 STA. 85+70.00
 S.N. 082-2042
