


MODEL: SHT_PLAN
 FILE NAME: C:\Bentley\CONNECT1011\Organization\Chil\DOT_Standards\Civil\DOT_Sheets.dwg

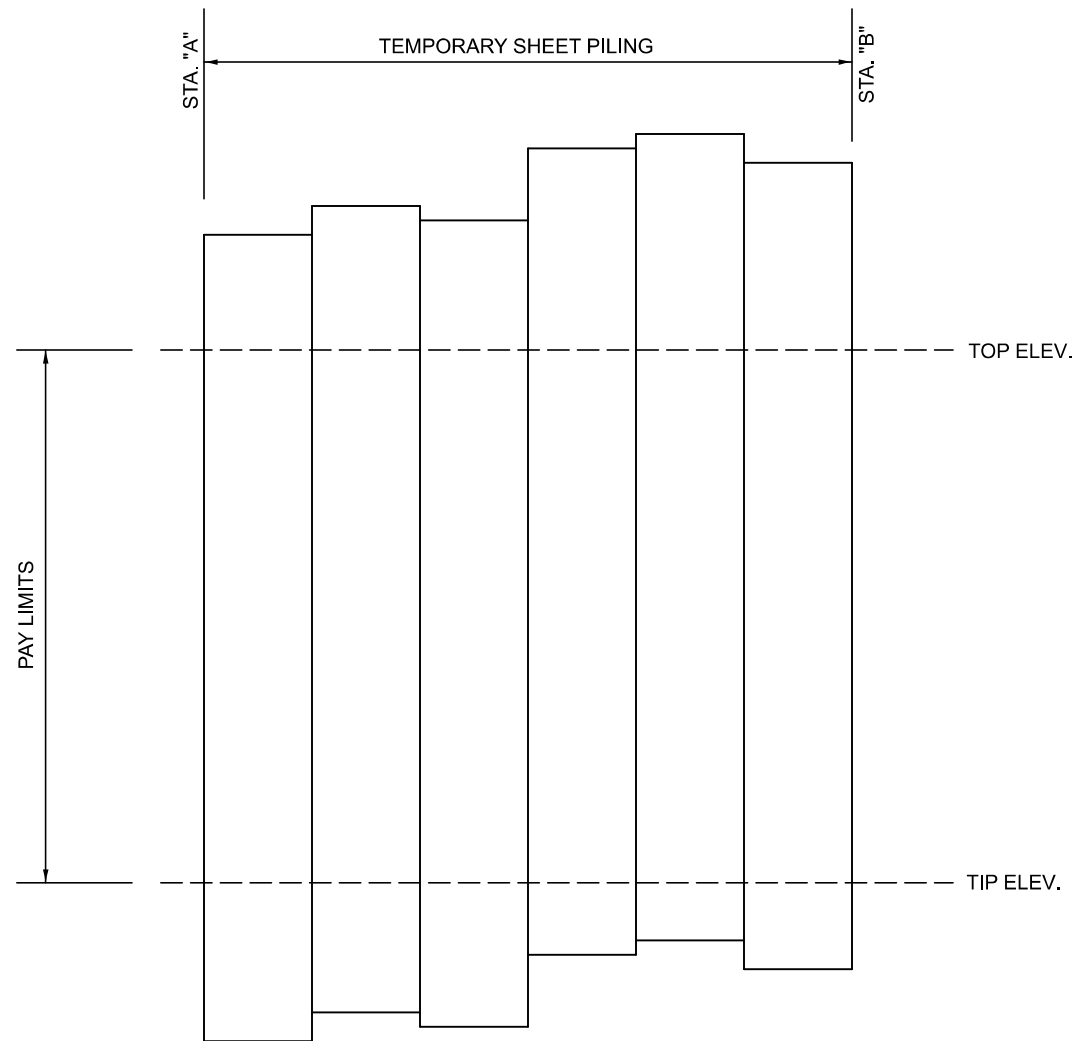

TABULATION OF PAY LIMITS

STA "A"	OFFSET FT. (m)	STA "B"	OFFSET FT. (m)	TOP ELEV.	TIP ELEV.	QUANTITY SQ. FT. (m ²)

NOTES:

PAYMENT WILL BE MADE ONLY FOR TEMPORARY SHEET PILING WITHIN THE LIMITS SHOWN ABOVE.

THE TOP ELEV. IS BASED ON THE GROUND LEVEL TO BE MAINTAINED BEHIND THE TEMPORARY SHEET PILING.

THE TIP ELEV. IS BASED ON THE SOIL BORINGS AND THE RECOMMENDATIONS OF THE DISTRICT MATERIALS ENGINEER.

THE TOP ELEV., TIP ELEV., AND LIMITS OF SHEET PILING ARE SUBJECT TO CHANGES BASED ON APPROVED SHOP DRAWINGS.

IF THE CONTRACTOR CHOOSES TO ALTER THE TEMPORARY CANTILEVERED SHEET PILING DESIGN REQUIREMENTS, THEN FULL DESING SUBMITTALS WITH THE REQUIRED SEALS WILL BE EXPECTED BY THE DEPARTMENT, FOR REVIEW AND APPROVAL.

Note: All dimensions are in INCHES (millimeters) unless otherwise shown.

DISTRICT 5 DETAIL NO. 51205200

USER NAME = Eric.Thomas	DESIGNED -	REVISED - 12/06
	DRAWN -	REVISED -
PLOT SCALE = \$\$SCALE\$	CHECKED -	REVISED -
PLOT DATE = 12/7/2022	DATE -	REVISED -

**STATE OF ILLINOIS
 DEPARTMENT OF TRANSPORTATION**

TEMPORARY SHEET PILING

SCALE: SHEET 1 OF 1 SHEETS STA. TO STA.

F.A. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
CONTRACT NO.				
ILLINOIS		FED. AID PROJECT		
