











LEGEND



-  Drum with steady burning bi-directional light
-  Temporary concrete barrier
-  Work area
-  Sign
-  Type III barricade
-  Impact attenuator
-  Arrow board
-  Flagger with traffic control sign.

PI STA 20+03.568 LINCOLN =
STA 13+75.551 MADISON

STA 17+99.39 LINCOLN =
STA 208+44.94 JEFFERSON

NOTES:

1. DURING HYDROSCARIFICATION OPERATIONS, THE CONTRACTOR SHALL CLOSE JEFFERSON STREET AT LINCOLN STREET AS SHOWN. CLOSURE OF JEFFERSON STREET SHALL ONLY BE PERMITTED FROM 7:00 PM TO 6:00 AM
2. DETOUR SIGNING FOR THE CLOSURE OF JEFFERSON STREET WILL BE PROVIDED BY DISTRICT 6 BUREAU OF OPERATIONS. BUREAU OF OPERATIONS SHALL BE CONTACTED 14 DAYS PRIOR TO THE START OF CONSTRUCTION. THE CONTACT PERSON SHALL BE MARSHALL METCALF, PHONE (217) 785-5312.
3. "ROAD CLOSED 500 FT" AND "ROAD CLOSED AHEAD" SIGNS SHALL BE COVERED UP WHEN THERE IS NO ROAD CLOSURE ON JEFFERSON STREET.
4. THE FLAGGER SHOWN SHALL DIRECT THRU TRAFFIC FROM ADJACENT SIDE ROADS AND DRIVEWAYS BETWEEN LINCOLN STREET AND SN 084-0190 DURING HYDROSCARIFICATION OPERATIONS. THE FLAGGER SHALL ALLOW TRAFFIC THROUGH THE CLOSURE IN AREAS THAT ARE NOT BENEATH THE HYDROSCARIFICATION OPERATION. IT MAY BE NECESSARY TO SUSPEND HYDROSCARIFICATION OPERATIONS AT TIMES TO ALLOW TRAFFIC TO PASS. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE SAFETY OF TRAFFIC DRIVING THROUGH THE CLOSURE. THE CONTRACTOR SHALL ALSO BE RESPONSIBLE TO KEEP JEFFERSON STREET FREE OF DEBRIS TO FACILITATE THRU TRAFFIC. THE COST OF THE FLAGGER AND DEBRIS REMOVAL SHALL BE INCLUDED IN THE BID PRICE FOR TRAFFIC CONTROL AND PROTECTION, STANDARD BLR 21 (SPECIAL).
5. FOR FULL DEPTH PATCHING OPERATIONS, THE CONTRACTOR WILL BE PERMITTED TO SET UP LANE CLOSURES ON JEFFERSON STREET PER STANDARD 701601. THESE LANE CLOSURES WILL NOT BE PERMITTED BETWEEN 3:00 PM AND 6:00 PM ON WEEKDAYS. THE COST OF THESE CLOSURES AND ANY OTHER DAY ONLY LANE CLOSURES SHALL BE INCLUDED IN THE BID PRICE FOR TRAFFIC CONTROL & PROTECTION, STANDARD 701601.

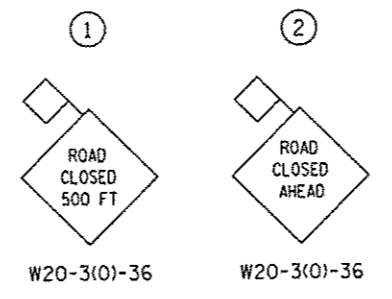

SN 084-0190
WORK ZONE

ROAD
CLOSED

FILE NAME *	USER NAME * audleybm	DESIGNED - DMS	REVISED -
D:\OPERATIONS\Bridges\plans\CAD\72685 - 848198 overlay\Complete Plans and IC.dgn		DRAWN - DMS	REVISED -
	PLOT SCALE * 48,0000 / 1 in.	CHECKED -	REVISED -
Default	PLOT DATE * Apr-09-2014 02:03:57PM	DATE	REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**ROAD CLOSURE STAGE I & STAGE II
TRAFFIC CONTROL DETAIL**

SCALE: SHEET 2 OF 2 SHEETS STA. TO STA.

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
67	(1072) BDR	SANGAMON	23	13
CONTRACT NO. 72685			ILLINOIS FED. AID PROJECT	
