SIGN DETAIL

1:75

WB-TR-08
STA. 12+40

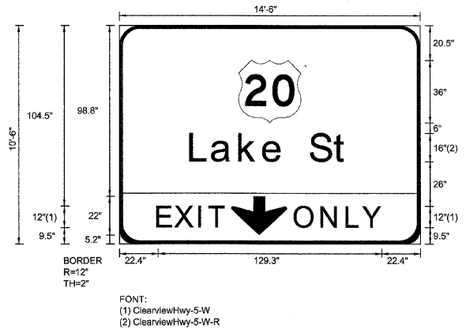

FONT:
(1) ClearviewHwy-5-W
(2) ClearviewHwy-5-W-R

SIGN NUMBER	name
WIDTH x HGHT.	14'-6" x 10'-6"
BORDER WIDTH	2"
CORNER RADIUS	12"
MOUNTING	Overhead
BACKGROUND	TYPE: Reflective
	COLOR: Green
LEGEND/BORDER	TYPE: Reflective
	COLOR: White,Black/White

SYMBOL	ROT	X	Y	WID	HT
M1_4	0	69	69.5	36	36
ARDOWN	0	64.8	5.2	32	22

Panel Style: sign_default.ssi
Dimensions are in inches.tenths

Letter locations are panel edge to lower left corner

LETTER POSITIONS (X)

																																			LENGTH	SERIES/SIZE
L	a	k	e		S	t																															ClearviewHwy-5-W-R
41.4	53.8	69.8	83.6	95.4	110.7	124.7																														91.2	16/13
E	X	I	T																																		ClearviewHwy-5-W
22.4	32.6	46.3	52.2																																	38.5	12
O	N	L	Y																																		ClearviewHwy-5-W
101.8	117.3	131.9	141.2																																	49.8	12

FILE NAME =	DESIGNED - SEW	REVISED -	LIN ENGINEERING,LTD. Consulting Engineers Chatham, Illinois Westmont, Illinois
$FILEL$	DRAWN - SEW	REVISED -	**STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION**
USER NAME = $USER$	CHECKED - FML	REVISED -	**SIGNING DETAILS**
PLOT DATE = $DATE$	DATE - 12/2009	REVISED -	SCALE: N.T.S. SHEET NO. 47 OF 71 SHEETS STA. TO STA.

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
*	22(), 1-1, 2&3)RS-7	DUPAGE	661	629
* 290,355		CONTRACT NO. 60G51		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		
