HORIZONTAL CONTROL POINTS

POINT	NORTH	EAST	ELEVATION	CHAIN	STATION	OFFSET	DESCRIPTION
1	2046136.2713	2562517.5295	800.0242	EBBUS20	62+45.8968	56.8951′ LT	GPS CONTROL POINT, PERM. SURVEY MARKER
2	2046008.9860	2563238.3509	788.0057	EBBUS20	69+73.6867	21.2512′ RT	TOPO SURVEY POINT, PIN
3	2046058.0424	2563713.9818	787.5937	EBBUS20	74+44.9000	59.9236′ LT	TOPO SURVEY POINT, PIN
4	2045923.9354	2564485.5133	789.4543	EBBUS20	82+23.7457	21.5924′ RT	TOPO SURVEY POINT, PIN
5	2046172.9246	2563802.4680	793.0022	EBBUS20	75+25.3978	180.538′ LT	TOPO SURVEY POINT, PIN
6	2046060.4087	2563747.8046	786.8814	EBBUS20	74+78.4847	64.5764′ LT	GPS CONTROL POINT, PERM. SURVEY MARKER
90202	2045999.4306	2564011.1144	788.1152	EBBUS20	77+45.3214	21.5817′ LT	PHOTO CONTROL H. & V., PIN
90220	2045937.0230	2565657.3338	779.8197	EBBUS20	93+92.0366	70.591′ LT	PHOTO CONTROL H. & V., PIN

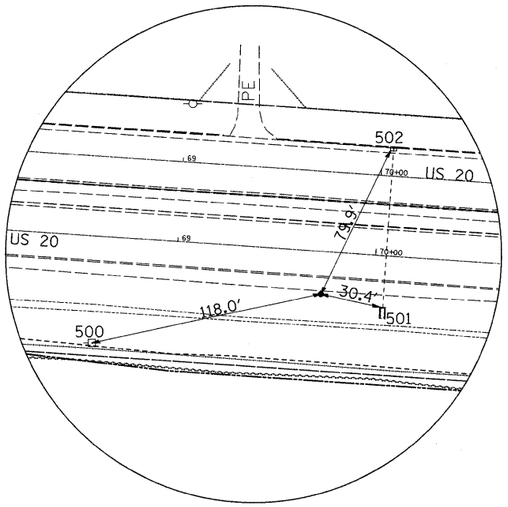

HORIZONTAL CONTROL
POINT No. 2

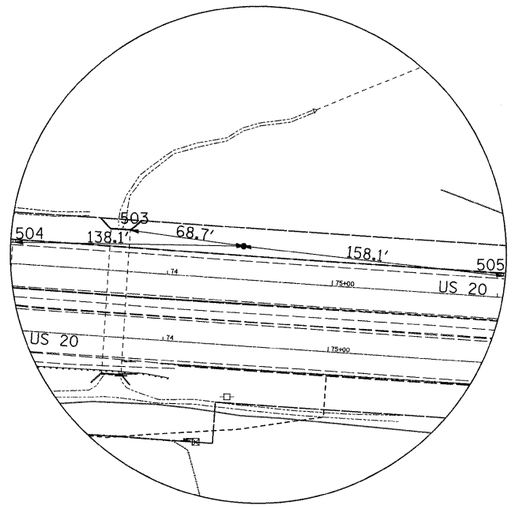

HORIZONTAL CONTROL
POINT No. 3

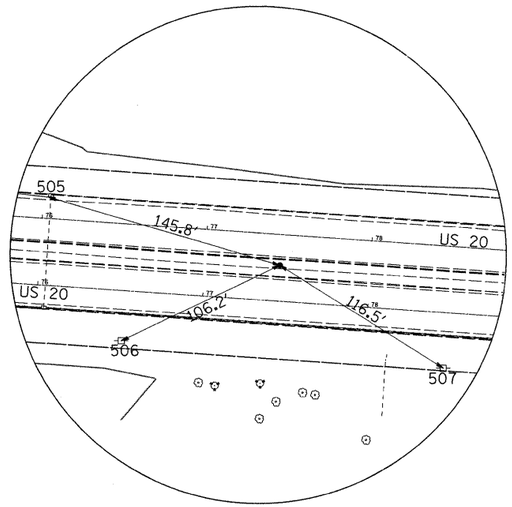

HORIZONTAL CONTROL
POINT No. 90202

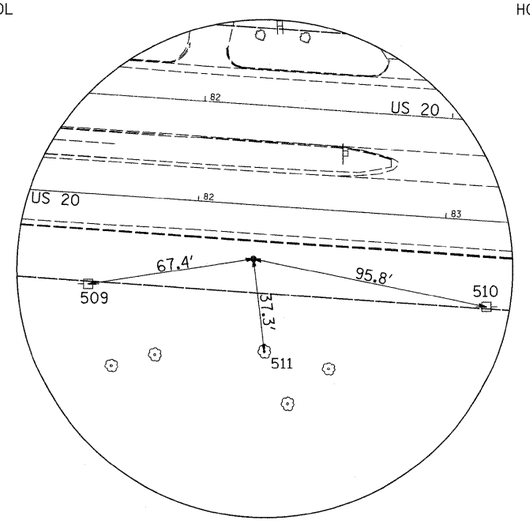

HORIZONTAL CONTROL
POINT No. 4

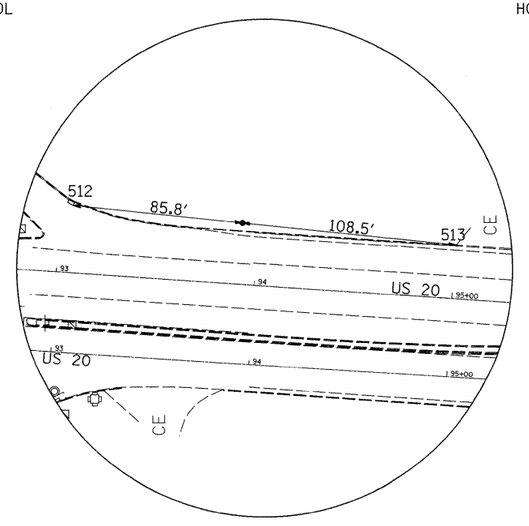

HORIZONTAL CONTROL
POINT No. 90220

FILE NAME = c:\projects\p211406\d11406hvc.dgn	USER NAME = polzinej	DESIGNED -	REVISED -	**STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION**	**HORIZONTAL & VERTICAL CONTROL**				
		DRAWN -	REVISED -						
	PLOT SCALE = 150.0000 ′ / IN.	CHECKED -	REVISED -						
	PLOT DATE = Mon Aug 04 13:24:24 2008	DATE -	REVISED -		SCALE:	SHEET NO. OF SHEETS	STA.	TO STA.	

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
303	(4OR)T	WINNEBAGO	67	15
		CONTRACT NO. 64C65		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		
