DESIGN		
INT.	DATE	REASON

PLOTS & CHECKS		
INT.	DATE	NO. REASON

FILE NAME = $FILE$
PLOT SCALE = $PLOTSCALE$ DRV = $PLOTTER$
PLOT DATE = $DATE$
PLOT TIME = $TIME$
OPERATOR = $USER$

CHECKS		
INT.	DATE	REASON

F.A.U RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
6108	***	LA SALLE	679	181
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	

*** (70X,71X)RS-1, (71X-VBR)DM
CONTRACT NO. 66225

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 7 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete
N/A in. Other N/A
Soil/Type CLAY Conditions DRY
Utility: GAS Size: 2" Material: STL Cond: GOOD
Was it found? YES At the requested location? YES
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76
Bench Mark: NameNo. Elev.=
As shown on sheet 4 of 10 on the plans
dated 5/21/03 and called IL RT 351

Client: IDOT
Contract # 66225
Project # C9300602
Name: RT 351
City: LA SALLE
County: LA SALLE
State: ILLINOIS

Geotrack Job # 73805
Truck # 121
Crew Chief M.M.
Drawn By M.M.
Checked By G.L.
Date 5/01/03

SKETCH PLAN:
* NOT TO SCALE *
HORIZONTAL SURVEY
ACCURACY = +/- 0.16mm

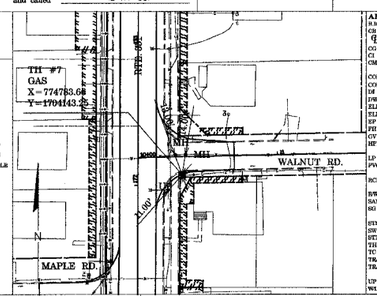

SYMBOL LEGEND
- TEST HOLE HUBPK
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark
CB – Catch Basin
℄ – Centerline
CG – Curb & Gutter
CI – Cast Iron
CMP – Corrugated Metal Pipe
CONC – Concrete
COND – Conduit
DI – Ductile Iron
DW – Driveway
ELEC – Electric
ELEV – Elevation
EP – Edge of Pavement
FH – Fire Hydrant
GV – Gas Valve
HPP – High Pressure Plastic
LP – Light Pole
PVC – Polyvinyl Chloride
RCP – Reinforced Concrete Pipe
R/W – Right-of-Way
SAN – Sanitary Sewer
SG – Storm Sewer Grate
STM – Storm Sewer
SW – Sidewalk
STL – Steel
TH – Test Hole
TC – Terra Cotta
TRAN – Transformer
TRAV – Survey Traverse Point
UP – Utility Pole
WL – Water Line

UTILITY OWNER: NICOR GAS
REPRESENTATIVE: SCOTT STOGSDILL
PHONE No: 630-983-8676 X2362
FAX No:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING EAST
VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR YELLOW
P.K. NAIL / HUB STAKE / CHISLED X



STA. 172+07.54, 31.75' RT. (IL RTE. 351)

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 8 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete
N/A in. Other N/A
Soil/Type CLAY Conditions DAMP
Utility: TELE Size: DUCT Material: CONC Cond: GOOD
Was it found? YES At the requested location? YES
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76
Bench Mark: NameNo. Elev.=
As shown on sheet 4 of 10 on the plans
dated 5/21/03 and called IL RT 351

Client: IDOT
Contract # 66225
Project # C9300602
Name: RT 351
City: LA SALLE
County: LA SALLE
State: ILLINOIS

Geotrack Job # 73805
Truck # 121
Crew Chief M.M.
Drawn By M.M.
Checked By G.L.
Date 5/02/03

SKETCH PLAN:
* NOT TO SCALE *
HORIZONTAL SURVEY
ACCURACY = +/- 0.16mm

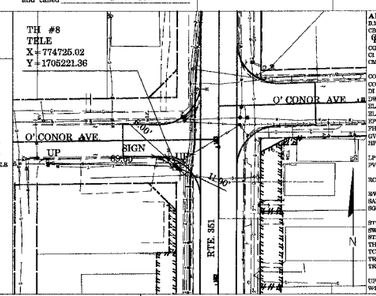

SYMBOL LEGEND
- TEST HOLE HUBPK
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark
CB – Catch Basin
℄ – Centerline
CG – Curb & Gutter
CI – Cast Iron
CMP – Corrugated Metal Pipe
CONC – Concrete
COND – Conduit
DI – Ductile Iron
DW – Driveway
ELEC – Electric
ELEV – Elevation
EP – Edge of Pavement
FH – Fire Hydrant
GV – Gas Valve
HPP – High Pressure Plastic
LP – Light Pole
PVC – Polyvinyl Chloride
RCP – Reinforced Concrete Pipe
R/W – Right-of-Way
SAN – Sanitary Sewer
SG – Storm Sewer Grate
STM – Storm Sewer
SW – Sidewalk
STL – Steel
TH – Test Hole
TC – Terra Cotta
TRAN – Transformer
TRAV – Survey Traverse Point
UP – Utility Pole
WL – Water Line

UTILITY OWNER: AMERITECH
REPRESENTATIVE:
PHONE No:
FAX No:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING EAST
VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR ORANGE
P.K. NAIL / HUB STAKE / CHISLED X



STA. 182+85.47, 30.13' LT. (IL RTE. 351)

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 9 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete
N/A in. Other N/A
Soil/Type CLAY Conditions WET
Utility: WATER Size: 4" Material: C.I. Cond: GOOD
Was it found? YES At the requested location? YES
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76
Bench Mark: NameNo. Elev.=
As shown on sheet 4 of 10 on the plans
dated 5/21/03 and called IL RT 351

Client: IDOT
Contract # 66225
Project # C9300602
Name: RT 351
City: LA SALLE
County: LA SALLE
State: ILLINOIS

Geotrack Job # 73805
Truck # 121
Crew Chief M.M.
Drawn By M.M.
Checked By G.L.
Date 5/5/03

SKETCH PLAN:
* NOT TO SCALE *
HORIZONTAL SURVEY
ACCURACY = +/- 0.16mm

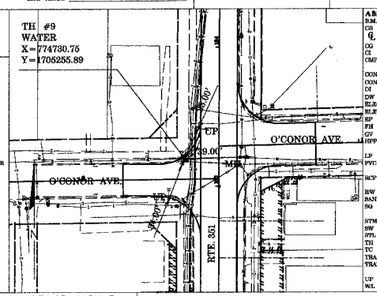

SYMBOL LEGEND
- TEST HOLE HUBPK
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark
CB – Catch Basin
℄ – Centerline
CG – Curb & Gutter
CI – Cast Iron
CMP – Corrugated Metal Pipe
CONC – Concrete
COND – Conduit
DI – Ductile Iron
DW – Driveway
ELEC – Electric
ELEV – Elevation
EP – Edge of Pavement
FH – Fire Hydrant
GV – Gas Valve
HPP – High Pressure Plastic
LP – Light Pole
PVC – Polyvinyl Chloride
RCP – Reinforced Concrete Pipe
R/W – Right-of-Way
SAN – Sanitary Sewer
SG – Storm Sewer Grate
STM – Storm Sewer
SW – Sidewalk
STL – Steel
TH – Test Hole
TC – Terra Cotta
TRAN – Transformer
TRAV – Survey Traverse Point
UP – Utility Pole
WL – Water Line

UTILITY OWNER: CITY OF LA SALLE
REPRESENTATIVE: WATER DEPT.
PHONE No:
FAX No:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING EAST
VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR BLUE
P.K. NAIL / HUB STAKE / CHISLED X



STA. 183+20.03, 24.49' LT. (IL RTE. 351)

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

TESTHOLES

FAU ROUTE 6108 (IL. RTE. 351)
SEC. (70X, 71X)RS-1, (71X-VBR)DM
LASALLE COUNTY

SCALE: VERT.
HORIZ.
DATE: 12/02/03

DRAWN BY: MABUS
DESIGNED BY: BOTT
CHECKED BY: COLBROOK

GREENE & BRADFORD, INC.
OF SPRINGFIELD
CONSULTING ENGINEERS
3600 CONSTITUTION DRIVE,
SPRINGFIELD, ILLINOIS 62707
REGISTERED PROFESSIONAL ENGINEERS AND LAND SURVEYORS
PROFESSIONAL SERVICE INDUSTRIES, INCORPORATED
(217) 793-2040, (217) 793-2427 (FAX), <email>GBSPRINGFIELD@PSIEMAIL.COM</email>

COMPUTER FILE NO.
TESTHOLES_C

PROJECT 01194_B_S
08/06/04-RPB

IDOTPL-20 1"=20' 8/07/00

FAU RTE. 6108 (IL. RTE. 351) LASALLE CO.

...\south part\testholes_c.dgn 12/2/2004 6:31:21 PM User = greg
