DESIGN		
INT.	DATE	REASON

PLOTS & CHECKS			
INT.	DATE	NO.	REASON

CHECKS		
INT.	DATE	REASON

F.A.U RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
6108	***	LA SALLE	679	193
STA.		TO STA.		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

*** (70X,71X)RS-1, (71X-VBR)DM
CONTRACT NO. 66225

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 43 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete; N/A in. Other N/A
Soil/Type CLAY Conditions WET
Utility: GAS Size: 4" Material: STL. Cond: GOOD
Was it found? YES At the requested location? YES
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76
Bench Mark: Name/No. Elev.=
As shown on sheet 6 of 10 on the plans
dated 5/21/03 and called IL RT 351

Client: IDOT
Geotrack Job # 73805
Truck # 121
Crew Chief M.M.
Drawn By M.M.
Checked By G.L.
Date 5/9/03
Contract # 66225
Project # C9300602
Name: RT 351
City: LA SALLE
County: LA SALLE
State: ILLINOIS

SKETCH PLAN: * NOT TO SCALE * HORIZONTAL SURVEY ACCURACY = +/- 0.16mm

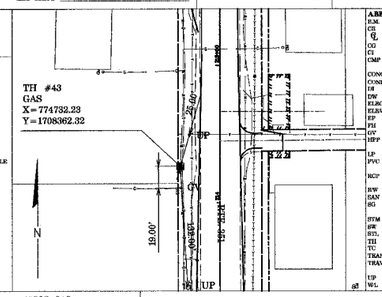

SYMBOL LEGEND
- TEST HOLE NUMBER
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark; CB – Catch Basin; ℄ – Centerline; CO – Curb & Gutter; CI – Cast Iron; CMP – Corrugated Metal Pipe; CONC – Concrete; COND – Conduit; DI – Ductile Iron; DW – Driveway; ELEC – Electric; ELEV – Elevation; EP – Edge of Pavement; FH – Fire Hydrant; GV – Gas Valve; HPP – High Pressure Plastic; LP – Light Pole; PVC – Polyvinyl Chloride; RCP – Reinforced Concrete Pipe; RW – Right-of-Way; SAN – Sanitary Sewer; SG – Storm Sewer Grate; STM – Storm Sewer; SW – Sidewalk; STL. – Steel; TH – Test Hole; TC – Terra Cotta; TRAN – Transformer; TRAV – Survey Traverse Point; UP – Utility Pole; WL – Water Line

UTILITY OWNER: NICOR GAS
REPRESENTATIVE: SCOTT STOGSDILL
PHONE No: 630-983-8676 X2362
FAX No:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING NORTH

VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR YELLOW
P.K. NAIL / HUB STAKE / CHISLED X



STA. 214+26.52, 27.30' LT. (IL RTE. 351)

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 44 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete; N/A in. Other N/A
Soil/Type CLAY Conditions WET
Utility: WATER Size: 8" Material: CI Cond: GOOD
Was it found? YES At the requested location? YES
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76
Bench Mark: Name/No. Elev.=
As shown on sheet 6 of 10 on the plans
dated 5/21/03 and called IL RT 351

Client: IDOT
Geotrack Job # 73805
Truck # 121
Crew Chief M.M.
Drawn By M.M.
Checked By G.L.
Date 5/9/03
Contract # 66225
Project # C9300602
Name: RT 351
City: LA SALLE
County: LA SALLE
State: ILLINOIS

SKETCH PLAN: * NOT TO SCALE * HORIZONTAL SURVEY ACCURACY = +/- 0.16mm

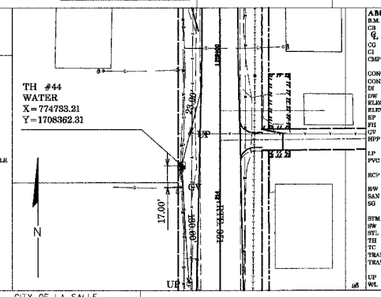

SYMBOL LEGEND
- TEST HOLE NUMBER
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark; CB – Catch Basin; ℄ – Centerline; CO – Curb & Gutter; CI – Cast Iron; CMP – Corrugated Metal Pipe; CONC – Concrete; COND – Conduit; DI – Ductile Iron; DW – Driveway; ELEC – Electric; ELEV – Elevation; EP – Edge of Pavement; FH – Fire Hydrant; GV – Gas Valve; HPP – High Pressure Plastic; LP – Light Pole; PVC – Polyvinyl Chloride; RCP – Reinforced Concrete Pipe; RW – Right-of-Way; SAN – Sanitary Sewer; SG – Storm Sewer Grate; STM – Storm Sewer; SW – Sidewalk; STL. – Steel; TH – Test Hole; TC – Terra Cotta; TRAN – Transformer; TRAV – Survey Traverse Point; UP – Utility Pole; WL – Water Line

UTILITY OWNER: CITY OF LA SALLE
REPRESENTATIVE: WATER DEPT.
PHONE No:
FAX No:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING NORTH

VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR BLUE
P.K. NAIL / HUB STAKE / CHISLED X



STA. 214+26.54, 28.28' LT. (IL RTE. 351)

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 45 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete; N/A in. Other N/A
Soil/Type CLAY Conditions DRY
Utility: GAS Size: 2" Material: STL. Cond: GOOD
Was it found? YES At the requested location? YES
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76
Bench Mark: Name/No. Elev.=
As shown on sheet 7 of 10 on the plans
dated 5/21/03 and called IL RT 351

Client: IDOT
Geotrack Job # 73805
Truck # 121
Crew Chief M.M.
Drawn By K.W.
Checked By G.L.
Date 5/12/03
Contract # 66225
Project # C9300602
Name: RT 351
City: LA SALLE
County: LA SALLE
State: ILLINOIS

SKETCH PLAN: * NOT TO SCALE * HORIZONTAL SURVEY ACCURACY = +/- 0.16mm

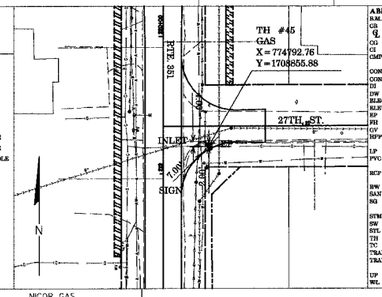

SYMBOL LEGEND
- TEST HOLE NUMBER
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLES
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark; CB – Catch Basin; ℄ – Centerline; CO – Curb & Gutter; CI – Cast Iron; CMP – Corrugated Metal Pipe; COND – Conduit; DI – Ductile Iron; DW – Driveway; ELEC – Electric; ELEV – Elevation; EP – Edge of Pavement; FH – Fire Hydrant; GV – Gas Valve; HPP – High Pressure Plastic; LP – Light Pole; PVC – Polyvinyl Chloride; RCP – Reinforced Concrete Pipe; RW – Right-of-Way; SAN – Sanitary Sewer; SG – Storm Sewer Grate; STM – Storm Sewer; SW – Sidewalk; STL. – Steel; TH – Test Hole; TC – Terra Cotta; TRAN – Transformer; TRAV – Survey Traverse Point; UP – Utility Pole; WL – Water Line

UTILITY OWNER: NICOR GAS
REPRESENTATIVE: SCOTT STOGSDILL
PHONE No: 630-983-8676 X2362
FAX No:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING EAST

VERTICAL SURVEY ACCURACY = +/- 0.15mm
FLAGGING COLOR YELLOW
P.K. NAIL / HUB STAKE / CHISLED X



STA. 219+20.06, 32.53' RT. (IL RTE. 351)

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

TESTHOLES

FAU ROUTE 6108 (IL. RTE. 351)
SEC. (70X, 71X)RS-1, (71X-VBR)DM
LASALLE COUNTY

SCALE: VERT.
HORIZ.
DATE: 12/02/03

DRAWN BY: MABUS
DESIGNED BY: BOTT
CHECKED BY: COLBROOK

GREENE & BRADFORD, INC. OF SPRINGFIELD
CONSULTING ENGINEERS
1500 CONSTITUTION DRIVE
POST OFFICE BOX 19247
PROFESSIONAL DESIGN FIRM NO. 184-001219
PROFESSIONAL & STRUCTURAL ENGINEERING CORPORATION
(217) 793-0045, (217) 793-3237 (FAX) E-MAIL: gbinfo@greenebradford.com

COMPUTER FILE NO.
TESTHOLES_0

PROJECT 01194_B_S
08/06/04-RPB

IDOTPL-20 1"=20' 8/07/00

FAU RTE. 6108 (IL. RTE. 351) LASALLE CO.

FILE NAME = $FILE$
PLOT SCALE = $pltscale$ DRV = $PLOTTER$
PLOT DATE = $DATE$
PLOT TIME = $TIME$
OPERATOR = $USER$

...\south part\testholes_0.dgn 12/2/2004 6:32:03 PM User = greg
