F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(530 & 531) RS-4	Cook	31	20G
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	

CONTRACT # 62079

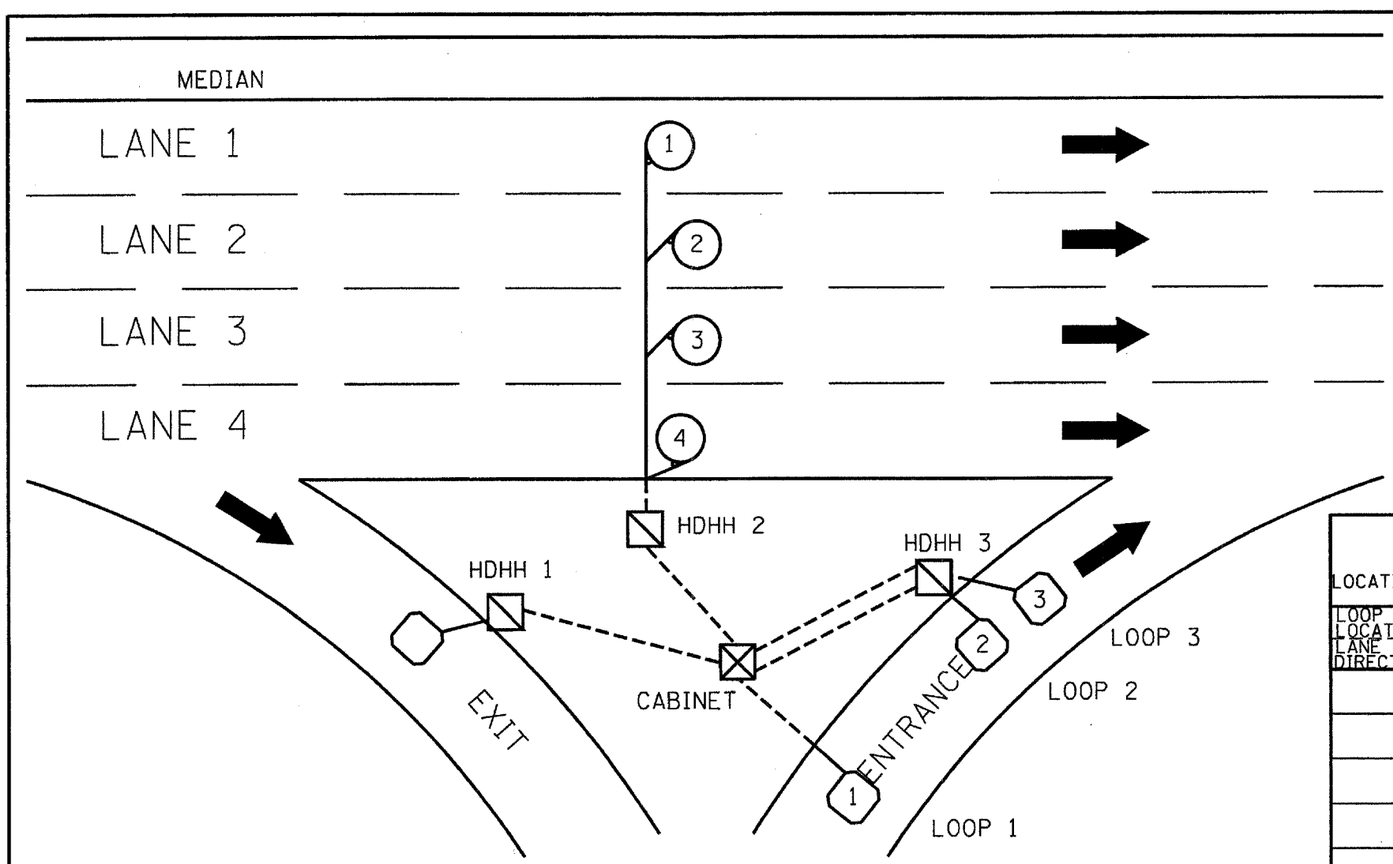



SUGGESTED TAG
PANDUIT
#MP250W175-C
OR EQUIVALENT

LOOP ANALYZER

LOCATION_____ DATE_____

LOOP LOCATION LANE DIRECTION	LOOP WIRE MARKED AND CODED	LOOP SIZE	FREQ. INDUCTANCE	INSULATION	LOOP RESISTANCE

HDHH 1 EXAMPLE

IB-EB EXIT
CCW IN/
TO CABINET #____

HDHH 2 EXAMPLE

IB (OB) LANE #__
CCW /OUT
TO CABINET #____

HDHH 3 EXAMPLE

IB-EB ENT.
LOOP #2
CW IN/

NOTE:
EACH LOOP WIRE SHALL BE TAGGED AS "IN" OR "OUT" AND "CW" OR "CCW". SHIELDED CABLE WILL BE TAGGED IN EACH HANDHOLE AND CABINET TO MATCH THE CABLE LOG.

REVISIONS	
NAME	DATE
R.L.	6/94
T.C.	10/96

ILLINOIS DEPARTMENT OF TRANSPORTATION
TRAFFIC SYSTEMS CENTER

LOOP STATUS REPORT

SCALE: VERT. HORIZ. NONE
DATE 6-27-94
DRAWN BY G.M.
CHECKED BY R.L.

RD=TYPMET.DGN
RF=
VI=4187

TRAFFIC SYSTEMS CENTER (TY-1TSC-418#7)
