CONTRACT NO. 88804

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
669	11W-3,RS-8,*	TAZEWELL	442	94
STA.		TO STA.		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

* 11BR-1, 11BR-2

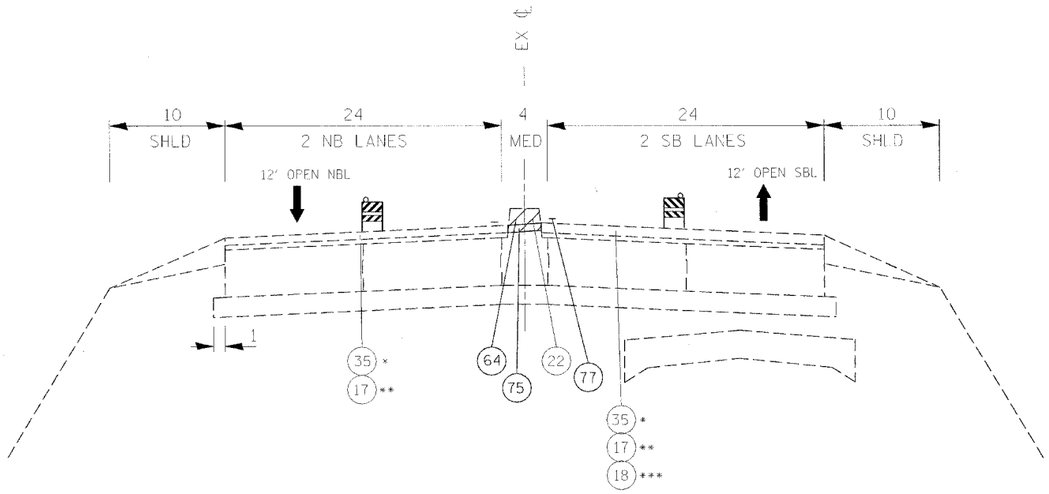

S1-1 SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL TYPICAL SECTION
STAGE 1
IL RTE 29
STA 257+30 TO STA 275+47
EXISTING BRIDGE OMMISSION STA 275+47 TO STA 276+07.5
STA 276+07.5 TO STA 276+50.36
STA 283+00 TO STA 301+30
EXISTING BRIDGE OMMISSION STA 301+30 TO STA 302+84
STA 302+84 TO STA 307+16

* FROM STA 257+30 TO STA 258+00
** FROM LT STA 258+00 TO LT STA 307+16
FROM RT STA 267+83 TO RT STA 275+47
FROM RT STA 286+05 TO RT STA 307+16
*** FROM RT STA 258+00 TO RT STA 267+83
FROM RT STA 276+07.5 TO RT STA 286+05

**** PR PCC BASE CSE WIDENING (VARIABLE DEPTH)
STA 277+31 TO 277+58,
STA 278+24 TO 278+45
STA 279+09 TO 283+00

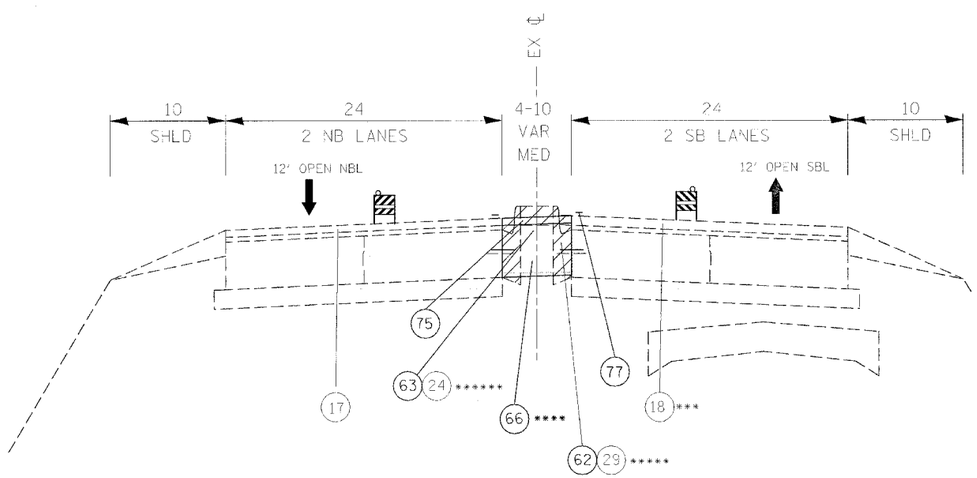

S1-2 SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL TYPICAL SECTION
STAGE 1
IL RTE 29
STA 276+50.36 TO 283+00

***** EX 10" PCC PAVEMENT & 2½" BIT CONC SURF W NO C&G
STA 276+64 TO 277+31,
STA 277+58 TO 278+24,
STA 278+45 TO 279+09
EX ABANDONED RR CROSSING W 5¼" INC BIT SURF
STA 279+64 TO 280+05
EX GRASS MED W COMB CONC C&G TYPE 3 MOD
STA 282+09 TO STA 282+95

****** STA 277+31 TO 277+58
STA 278+24 TO 278+45
STA 279+09 TO 283+00

SYMBOLS

REMOVAL ITEM

(1) EX AGG SHLD
(2) EX ANCHOR BOLT ⅝" DIA
(3) EX AREA REFLECTIVE CRACK CONTROL TREATMENT SYSTEM A
(4) EX BIT CONC BASE CSE, TY B 3"
(5) EX BIT CONC BIND & SURF CSE FINE DENSE - GRADED AGG TY, SUB CLASS I-11 (3")
(6) EX BIT CONC BIND CSE 1½"
(7) EX BIT CONC BIND CSE 2"
(8) EX BIT CONC BIND CSE, TY 2 (1½")
(9) EX BIT CONC PAVEMENT 4"
(10) EX BIT CONC SHLD 10"
(11) EX BIT CONC SHLD 2"
(12) EX BIT CONC SHLD 8"
(13) EX BIT CONC SURF CSE 2"
(14) EX BIT CONC SURF CSE CL I 1½"
(15) EX BIT CONC PAVEMENT 6" (ASSUMED)
(16) EX BIT CONC SURF CSE 1½"
(17) EX BIT CONC SURF CSE MIX E, CL 1, TY 2, 1½"
(18) EX BIT CONC SURF CSE, MIX E, CL 1, TY 2, 2"
(19) EX BIT SURF 2" DENSE-GRADED AGG TY SUBCLASS B-2
(20) EX CCC&G TY B-6.24
(21) EX CONC MED TY SM (MODIFIED)
(22) EX CONC MED TY 4
(23) EX CONC MED TY 4A
(24) EX INC BIT CONC SURF 4" W COMB CC&G TY 3 MOD
(25) EX LEVELING BIND (MACH METH), TY 2, 1"
(26) EX LEVELING BIND VAR THICKNESS
(27) EX LEVLEING BIND VAR THICKNESS (MACH METH), (0"-2")
(28) EX LEVLEING BIND VAR THICKNESS (MACH METH), (0"-4")
(29) EX MED
(30) EX PCC BASE CSE 8"
(31) EX PCC BASE CSE 9"
(32) EX PCC BASE CSE WIDENING 8"
(33) EX PCC PVMT 10"
(34) EX PCC PVMT 9-6-9
(35) EX POLYMERIZED BIT CONC SURF CSE, SUPER E, N70, 1½"
(36) EX SOIL CEMENT BASE 6½"
(37) EX STABILIZED SHLD 8"
(38) EX STABILIZED SUB-BASE 4" (BAM)
(39) EX SUB-BASE GRAN MATL 4"
(40) EX GRASS MED W/COMB CC&G TY 10
(41) EX BIT CONC 3½"
(42) EX BIT CONC 4½"

(50) PR AGG SHLD, TY B
(51) PR BIT CONC BIND CSE 2¼"
(52) PR BIT BASE CSE SUPERPAVE 6½"
(53) PR POLY BIT CONC BIND CSE, SP, IL-19.0, N70 (VAR DEPTH)
(54) PR BIT CONC LEVELING BIND 0-1"
(55) PR BIT CONC SHLD SP 6½"
(56) PR POLY BIT CONC SURF CSE, SP, MIX "E", N70 (1½")
(57) PR BIT CONC SHLD SP 1½"
(58) PR BIT SHLD REM
(59) PR BIT SURF REM, 1½"
(60) PR BIT SURF REM, 2"
(61) PR COMB CONC C&G, TY B-6.24
(62) PR COMB C&G REM
(63) PR MED REM
(64) PR MED REM PARTIAL DEPTH
(65) PR CONC MED, TY SM 4.06
(66) PR PCC BASE CSE WIDENING VARIABLE DEPTH
(68) PR PVMT REM (SPECIAL)
(69) PR PVMT REM
(70) PR SLOPED PARKWAY W GRASS
(71) PR STORM SEWER 18" TO 24" DIA
(72) PR SUBBASE GRAN MATL, TY C 4"
(73) PR TOPSOIL 4"
(74) PR BIT CONC BASE CSE SP 6"
(75) PR BIT CONC BIND CSE 3"
(76) PR BIT CONC SURF CSE, SP, MIX "C", N50 (2")
(77) PR TEMP PVMT MARKING - LINE 4"

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
IL RTE 29
WESLEY RD TO IL RTE 98
SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL
STAGE 1A & 1B TYPICAL SECTIONS

SCALE: VERT. HORIZ. NOT TO SCALE
DRAWN BY
DATE
CHECKED BY

PLOT DATE = 4/10/2006
FILE NAME = c:\projects\29peiun\phase_II\typical_staging.dgn
PLOT SCALE = 1988.5000 ' / M.
REFERENCE = REF
