F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
1517	03-00247-00-BR	KANE	121	22
STA.		TO STA.		
FED. ROAD DIST. NO. 1		ILLINOIS	HIGHWAY PROJECT	

CONTRACT #: 83867

ROAD CLOSURE GENERAL NOTES

1. THE CONTRACTOR WILL BE ALLOWED TO CLOSE ILLINOIS AVENUE FOR TWO (2) SEPARATE DURATIONS AS DETAILED IN THE SPECIFICATIONS. EACH DURATION SHALL BE A MAXIMUM OF FIVE (5) CONTINUOUS WORKING DAYS. CLOSURES WILL NOT BE ALLOWED DURING HOLIDAYS OR WEEKENDS. ALL DETOUR SIGNS SHALL BE REMOVED WHEN DETOUR IS NOT IN PLACE.
2. THE DETOUR ROUTE SHALL BE POSTED PRIOR TO CLOSING THE ROAD.
3. ALL TRAFFIC CONTROL WORK ASSOCIATED WITH BOTH THE ROAD CLOSURES, SIGNING, AND BARRICADING, SHALL BE INCLUDED IN THE PAY ITEM FOR 'TRAFFIC CONTROL AND PROTECTION FOR TEMPORARY DETOUR'.
4. THE CONTRACTOR SHALL GIVE THE ENGINEER, CITY AND IDOT A 72 HOUR NOTICE PRIOR TO PLACING THE ADVANCE NOTICE SIGNS.
5. ADVANCE NOTICE SIGNS " (17) " SHALL BE PLACED TWO WEEKS PRIOR TO CLOSING THE ROADWAY.
6. CHANGEABLE MESSAGE SIGNS SHALL BE PLACED ON THE NORTH AND SOUTH LEGS OF IL ROUTE 31, NORTH AND SOUTH LEGS OF IL ROUTE 25, AND THE EAST AND WEST LEGS OF ILLINOIS AVENUE ONE WEEK IN ADVANCE OF ROAD CLOSURES.

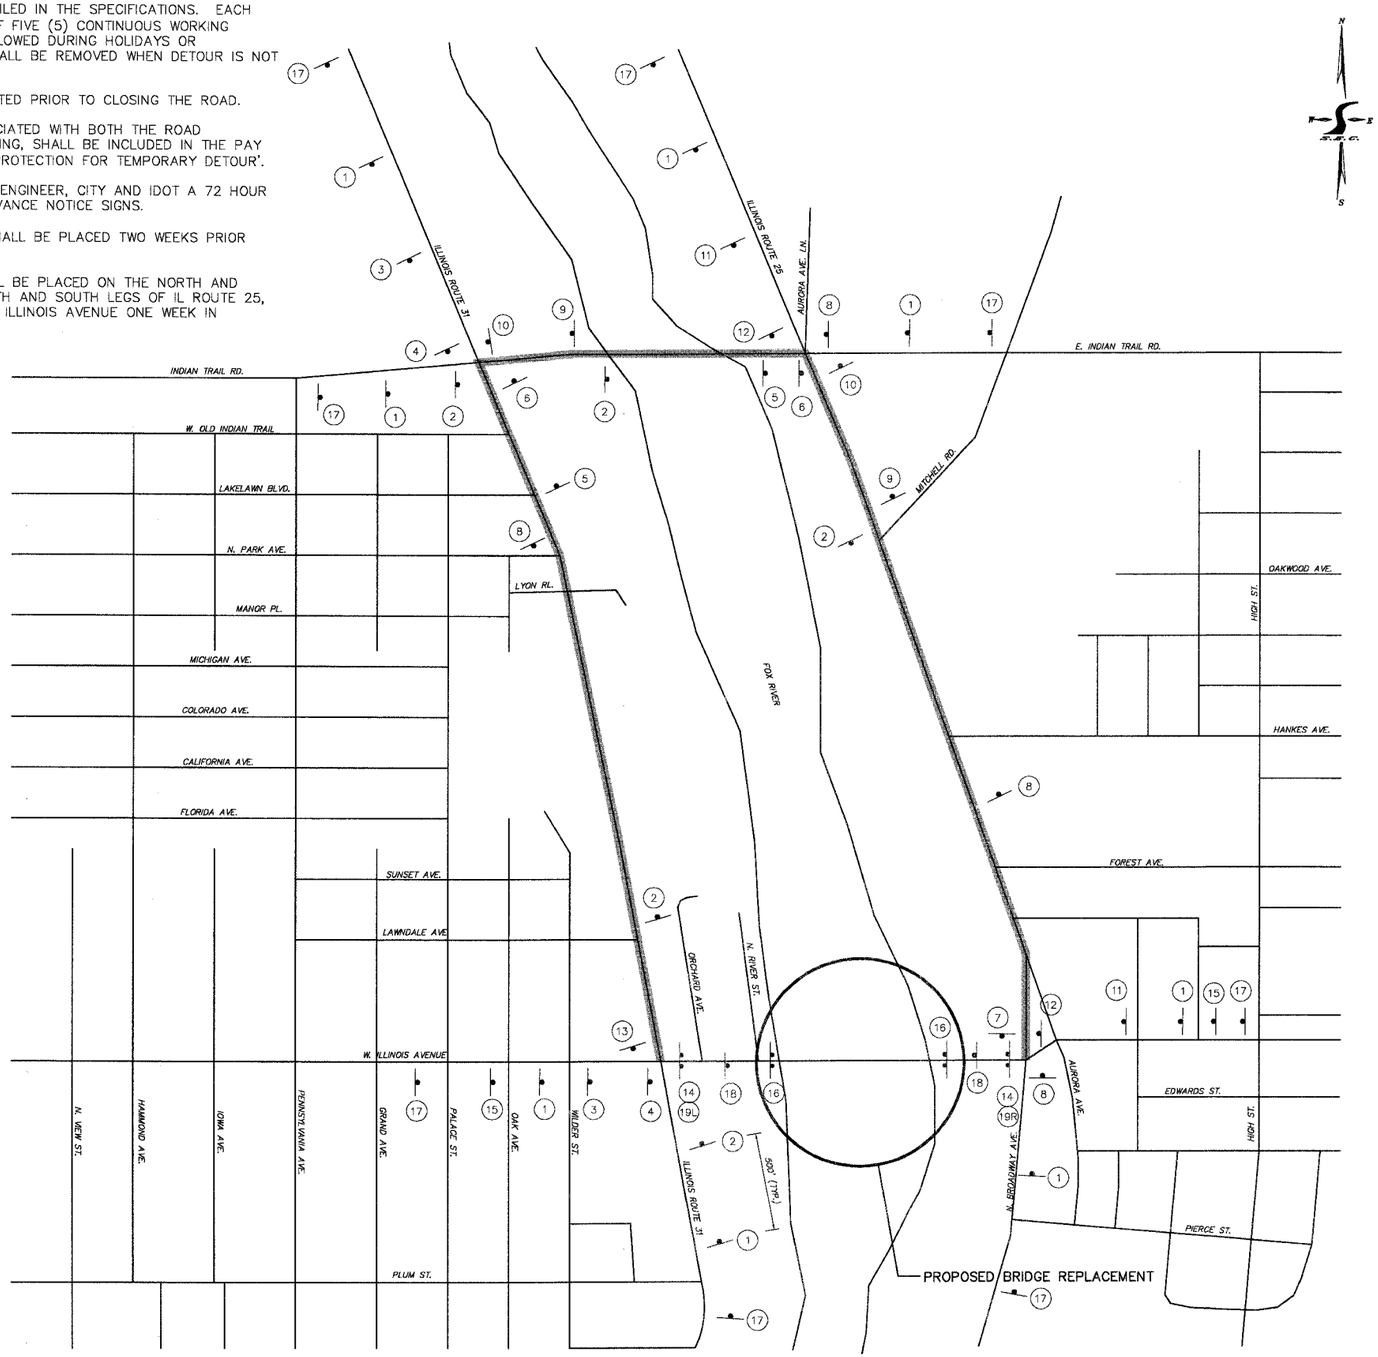

SIGN LEGEND

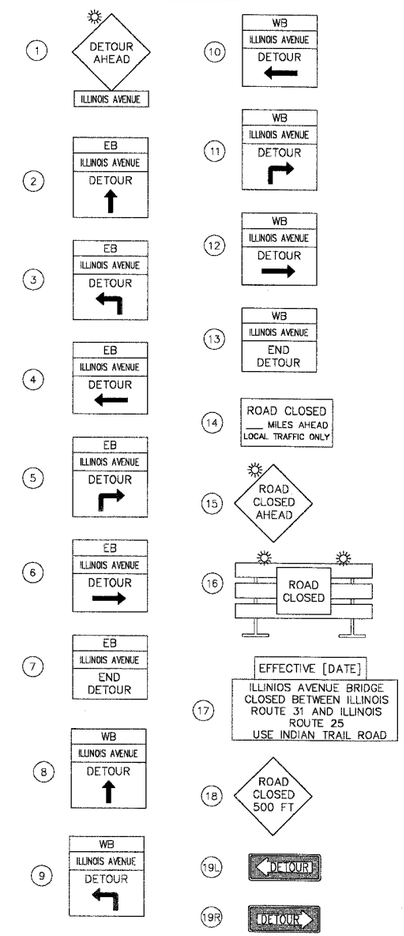

LEGEND

PROPOSED DETOUR ROUTE

NOTE:
SIGN SPACING SHALL BE 500' TYPICAL UNLESS OTHERWISE DIRECTED BY THE ENGINEER.

REVISIONS		
	NAME	DATE
7.		
6.		
5.		
4.		
3.		
2.		
1.		

SMITH ENGINEERING CONSULTANTS, INC.
CIVIL/STRUCTURAL ENGINEERS AND SURVEYORS
4500 PRIME PARKWAY, SUITE 201
McHENRY, ILLINOIS 60050
PH: 815-385-1778 FAX: 815-385-1781
www.smithengineering.com E-MAIL: sec@smithengineering.com
McHENRY HUNTLEY YORKVILLE
ILLINOIS PROFESSIONAL DESIGN FIRM # 184-000108

ILLINOIS DEPARTMENT OF TRANSPORTATION

CITY OF AURORA
ILLINOIS AVENUE OVER THE FOX RIVER
DETOUR PLAN

SCALE: "NTS"
DATE 07-28-2006
DRAWN BY CFR
CHECKED BY JLP

PLOT FILE: STANDARD
VIEW: CE-22
COMP. FILE: 050181-627.dwg

SMITH ENGINEERING CONSULTANTS INC.
