DESIGN		
INT.	DATE	REASON

PLOTS & CHECKS			
INT.	DATE	NO.	REASON

CHECKS		
INT.	DATE	REASON

F.A.U RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
6108	***	LA SALLE	679	191
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	

*** (70X,71X)RS-1, (71X-VBR)DM
CONTRACT NO. 66225

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 37 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete		Client: IDOT	Geotrack Job # 73805
N/A in. Other N/A			Truck # 121
Soil/Type CLAY Conditions WET		Contract # 66225	Crew Chief M.M.
Utility: TELE Size: 1" Material: CABLE Cond: GOOD		Project # C9300602	Drawn By M.M.
Was it found? YES At the requested location? YES		Name: RT 351	Checked By G.L.
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76		City: LA SALLE	Date 5/8/03
Bench Mark: Name No. Elev.=		County: LA SALLE	
As shown on sheet 6 of 10 on the plans		State: ILLINOIS	
dated 5/2/03 and called IL RT 351			

SKETCH PLAN:
* NOT TO SCALE *
HORIZONTAL SURVEY
ACCURACY = +/- 0.16mm

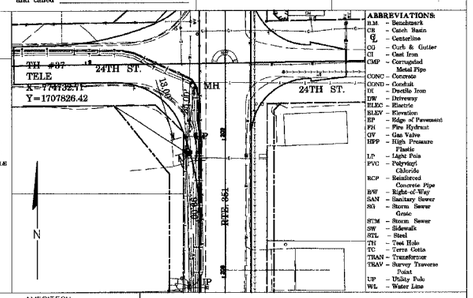

SYMBOL LEGEND
- TEST HOLE BURIED
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark
CB – Catch Basin
℄ – Centerline
CO – Curb & Gutter
CI – Cast Iron
CMP – Corrugated Metal Pipe
CONC – Concrete
COND – Conduit
DI – Ductile Iron
DW – Driveway
ELEC – Electric
ELEV – Elevation
EP – Edge of Pavement
FH – Fire Hydrant
GV – Gas Valve
HPP – High Pressure Plastic
LP – Light Pole
PVC – Polyvinyl Chloride
RCP – Reinforced Concrete Pipe
R/W – Right-of-Way
SAN – Sanitary Sewer
SG – Storm Sewer Grate
STM – Storm Sewer
SW – Sidewalk
STL – Steel
TH – Test Hole
TC – Terra Cotta
TRAN – Transformer
TRAV – Survey Traverse Point
UP – Utility Pole
WL – Water Line

UTILITY OWNER: AMERITECH
REPRESENTATIVE:
PHONE No.:
FAX No.:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING NORTH
VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR ORANGE
P.K. NAIL / HUB STAKE / CHISLED X

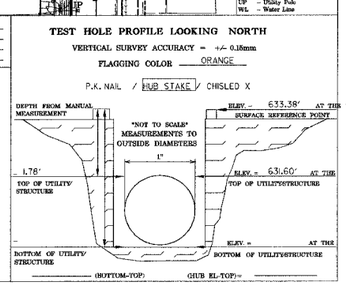

STA. 208+90.58, 27.97' LT. (IL RTE. 351)

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 38 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete		Client: IDOT	Geotrack Job # 73805
N/A in. Other N/A			Truck # 121
Soil/Type CLAY Conditions DAMP		Contract # 66225	Crew Chief M.M.
Utility: GAS Size: 4" Material: STL. Cond: GOOD		Project # C9300602	Drawn By M.M.
Was it found? YES At the requested location? YES		Name: RT 351	Checked By G.L.
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76		City: LA SALLE	Date 5/8/03
Bench Mark: Name No. Elev.=		County: LA SALLE	
As shown on sheet 6 of 10 on the plans		State: ILLINOIS	
dated 5/2/03 and called IL RT 351			

SKETCH PLAN:
* NOT TO SCALE *
HORIZONTAL SURVEY
ACCURACY = +/- 0.16mm

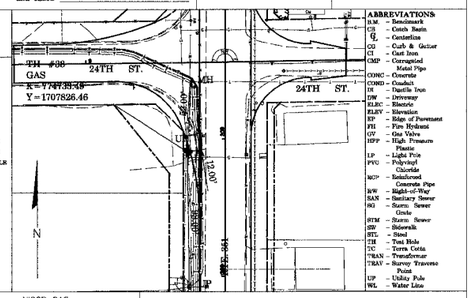

SYMBOL LEGEND
- TEST HOLE BURIED
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark
CB – Catch Basin
℄ – Centerline
CO – Curb & Gutter
CI – Cast Iron
CMP – Corrugated Metal Pipe
CONC – Concrete
COND – Conduit
DI – Ductile Iron
DW – Driveway
ELEC – Electric
ELEV – Elevation
EP – Edge of Pavement
FH – Fire Hydrant
GV – Gas Valve
HPP – High Pressure Plastic
LP – Light Pole
PVC – Polyvinyl Chloride
RCP – Reinforced Concrete Pipe
R/W – Right-of-Way
SAN – Sanitary Sewer
SG – Storm Sewer Grate
STM – Storm Sewer
SW – Sidewalk
STL – Steel
TH – Test Hole
TC – Terra Cotta
TRAN – Transformer
TRAV – Survey Traverse Point
UP – Utility Pole
WL – Water Line

UTILITY OWNER: NICOR GAS
REPRESENTATIVE: SCOTT STOSSDALL
PHONE No.: 630-983-8676 X2362
FAX No.:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING NORTH
VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR YELLOW
P.K. NAIL / HUB STAKE / CHISLED X

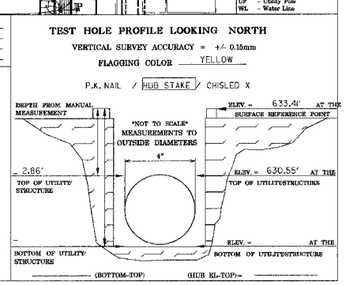

STA. 208+90.62, 27.20' LT. (IL RTE. 351)

735 N. Harvard
Villa Park, IL 60181
VOICE: (630)530-7609
FAX: (630)530-8167

GEOTRACK, INC.

Utility Location Report for Test Hole 39 **of** 53 **in U.S. Survey Feet.**

Pavement: N/A in. Asphalt N/A in. Concrete		Client: IDOT	Geotrack Job # 73805
N/A in. Other N/A			Truck # 121
Soil/Type CLAY Conditions WET		Contract # 66225	Crew Chief M.M.
Utility: WATER Size: 8" Material: C.I. Cond: FAIR		Project # C9300602	Drawn By M.M.
Was it found? YES At the requested location? YES		Name: RT 351	Checked By G.L.
Bench Mark: PK@STA.147+50 (IDOT) Elev.= 583.76		City: LA SALLE	Date 5/8/03
Bench Mark: Name No. Elev.=		County: LA SALLE	
As shown on sheet 6 of 10 on the plans		State: ILLINOIS	
dated 5/2/03 and called IL RT 351			

SKETCH PLAN:
* NOT TO SCALE *
HORIZONTAL SURVEY
ACCURACY = +/- 0.16mm

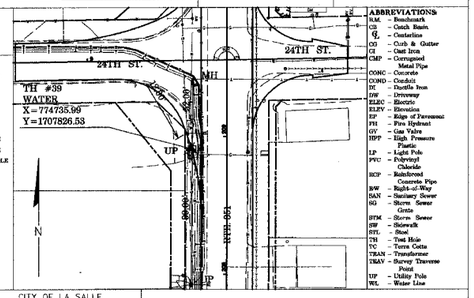

SYMBOL LEGEND
- TEST HOLE BURIED
- UTILITY POLE
- FIRE HYDRANT
- WATER VALVE
- GAS VALVE
- STORM MANHOLE
- SANITARY MANHOLE
- ELECTRIC MANHOLE
- TELEPHONE MANHOLE
- CATCH BASIN
- ELECTRIC TRANSFORMER
- CABLE TELEVISION PEDESTAL
- TELEPHONE PEDESTAL
- SURVEY TRAVERSE POINT
- STORM GRATE
- INLET

ABBREVIATIONS
B.M. – Benchmark
CB – Catch Basin
℄ – Centerline
CO – Curb & Gutter
CI – Cast Iron
CMP – Corrugated Metal Pipe
CONC – Concrete
COND – Conduit
DI – Ductile Iron
DW – Driveway
ELEC – Electric
ELEV – Elevation
EP – Edge of Pavement
FH – Fire Hydrant
GV – Gas Valve
HPP – High Pressure Plastic
LP – Light Pole
PVC – Polyvinyl Chloride
RCP – Reinforced Concrete Pipe
R/W – Right-of-Way
SAN – Sanitary Sewer
SG – Storm Sewer Grate
STM – Storm Sewer
SW – Sidewalk
STL – Steel
TH – Test Hole
TC – Terra Cotta
TRAN – Transformer
TRAV – Survey Traverse Point
UP – Utility Pole
WL – Water Line

UTILITY OWNER: CITY OF LA SALLE
REPRESENTATIVE: WATER DEPT.
PHONE No.:
FAX No.:

CERTIFICATION:
I hereby certify that the information shown hereon is correct to the best of my knowledge and belief.

TEST HOLE PROFILE LOOKING NORTH
VERTICAL SURVEY ACCURACY = +/- 0.16mm
FLAGGING COLOR BLUE
P.K. NAIL / HUB STAKE / CHISLED X

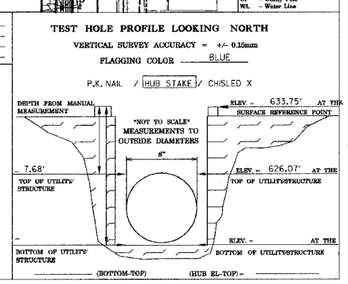

STA. 208+90.70, 24.70' LT. (IL RTE. 351)

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

TESTHOLES

FAU ROUTE 6108 (IL. RTE. 351)
SEC. (70X, 71X)RS-1, (71X-VBR)DM
LASALLE COUNTY

SCALE: VERT.
HORIZ.
DATE: 12/02/03

DRAWN BY: MABUS
DESIGNED BY: BOTT
CHECKED BY: COLBROOK

GREENE & BRADFORD, INC.
OF SPRINGFIELD
CONSULTING ENGINEERS
350 CONSTITUTION DRIVE
SPRINGFIELD, ILLINOIS 62707
PROFESSIONAL DESIGN FIRM NO. 84-0015
PROFESSIONAL & STRUCTURAL ENGINEERS CORPORATION
(217) 793-2674, (217) 793-3227 (FAX), e-mail: - ecobg-springfield@ecbg-ecbg.com

COMPUTER FILE NO.
TESTHOLES_M

PROJECT 01194_B_S
08/06/04-RPB

FILE NAME = $FILE$
PLOT SCALE = $PLOTSCALE$
PLOT DATE = $DATE$
PLOT TIME = $TIME$
OPERATOR = $USER$

IDOTPL-20 1"=20' 8/07/00

FAU RTE. 6108 (IL. RTE. 351) LASALLE CO.

...\route part\testholes_m.dgn 12/2/2004 5:31:55 PM User = greg
