F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90/94	2004-068L	COOK	37	6
STA.		TO STA.		
FED. ROAD DIST. NO. 1	ILLINOIS	FED. AID PROJECT		

62807

ACTIVITY ID	ACTIVITY DESCRIPTION	EARLY START	EARLY FINISH	ORIG DUR
CONTRACT 9C (62693) - WENTWORTH AVENUE				
PRE-STAGE - SEWER RELOCATION				
1	INSTALL TRAFFIC CONTROL	02-May-05	06-May-05	
2	SEWER RELOCATION (STA. 112+88 TO STA. 126+58)	06-May-05	03-Jun-05	
STAGE 1 - RETAINING WALLS & PAVE INSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	01-Jun-05	06-Jun-05	
2	CONSTRUCT PROPOSED RETAINING WALLS			
a.	S.N. 016-W882	06-Jun-05	05-Aug-05	
b.	S.N. 016-W886	06-Jun-05	09-Sep-05	
c.	S.N. 016-W901	06-Jun-05	19-Aug-05	
d.	S.N. 016-W887/W965	06-Jun-05	02-Sep-05	
e.	S.N. 016-WWRR	06-Jun-05	19-Aug-05	
3	COMED RELOCATION (60TH STREET)	18-July-05	05-Aug-05	
4	SEWER RELOCATION (STA. 126+58 TO STA. 131+12)	06-Jun-05	22-Jun-05	
5	CONSTRUCT PROPOSED FRONTAGE ROAD	03-Aug-05	10-Oct-05	
6	CONSTRUCT 14" TEMPORARY PAVEMENT & CONCRETE RAMPS	05-Aug-05	14-Oct-05	
STAGE 2 - PAVE OUTSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	17-Oct-05	24-Oct-05	
2	CONSTRUCT PROPOSED FRONTAGE ROAD	24-Oct-05	23-Nov-05	
CONTRACT 9C (62693) - WELLS STREET				
STAGE 1 - RETAINING WALLS & PAVE INSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	02-May-05	09-May-05	
2	CONSTRUCT PROPOSED RETAINING WALLS			
a.	S.N. 016-W894/964	09-May-05	22-Jul-05	
b.	S.N. 016-W903/W906	09-May-05	05-Aug-05	
c.	S.N. 016-W907	09-May-05	05-Aug-05	
4	CONSTRUCT PROPOSED FRONTAGE ROAD	20-Jun-05	23-Sep-05	
5	CONSTRUCT 14" TEMPORARY PAVEMENT & CONCRETE RAMPS	20-Jun-05	23-Aug-05	
STAGE 2 - PAVE OUTSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	23-Sep-05	29-Sep-05	
2	CONSTRUCT PROPOSED FRONTAGE ROAD	30-Sep-05	11-Nov-05	
CONTRACT 9C1 (62835) - SIDEWALKS & DRIVEWAYS				
WENTWORTH AVENUE				
1	CONSTRUCT PROPOSED SIDEWALKS & DRIVEWAYS	14-Nov-05	16-Dec-05	
WELLS STREET				
1	CONSTRUCT PROPOSED SIDEWALKS & DRIVEWAYS	31-Oct-05	02-Dec-05	
CONTRACT 9C4 (62836) - FRONTAGE ROAD SIGNING				
WENTWORTH AVENUE				
1	REMOVE EXISTING SIGNING	01-Jun-05	10-Jun-05	
2	INSTALL NEW SIGNAGE / REINSTALL SIGNAGE	28-Nov-05	09-Dec-05	
WELLS STREET				
1	REMOVE EXISTING SIGNING	02-May-05	13-May-05	
2	INSTALL NEW SIGNAGE / REINSTALL SIGNAGE	14-Nov-05	23-Nov-05	
CONTRACT 9C5 (62837) - FRONTAGE ROAD PAVEMENT MARKING				
STAGE 2 - WENTWORTH AVENUE				
1	INSTALL PERMANENT PAVEMENT MARKINGS	28-Nov-05	09-Dec-05	
STAGE 2 - WELLS STREET				
1	INSTALL PERMANENT PAVEMENT MARKINGS	14-Nov-05	23-Nov-05	
CONTRACT 9C6 (62838) - TREE REMOVAL				
WENTWORTH AVENUE				
1	REMOVE EMBANKMENT TREES	02-May-05	13-May-05	
WELLS STREET				
1	REMOVE EMBANKMENT TREES	25-Apr-05	06-May-05	
CONTRACT 9C7 (62839) - 59TH STREET TRAFFIC SIGNALS				
59TH STREET & WENTWORTH AVENUE				
1	INSTALL AND MAINTAIN TEMPORARY TRAFFIC SIGNALS, REMOVE EXISTING AND INSTALL NEW LIGHTING AND TRAFFIC SIGNALS	02-May-05	23-Nov-05	
59TH STREET & WELLS STREET				
1	INSTALL AND MAINTAIN TEMPORARY TRAFFIC SIGNALS, REMOVE EXISTING AND INSTALL NEW LIGHTING AND TRAFFIC SIGNALS	02-May-05	11-Nov-05	

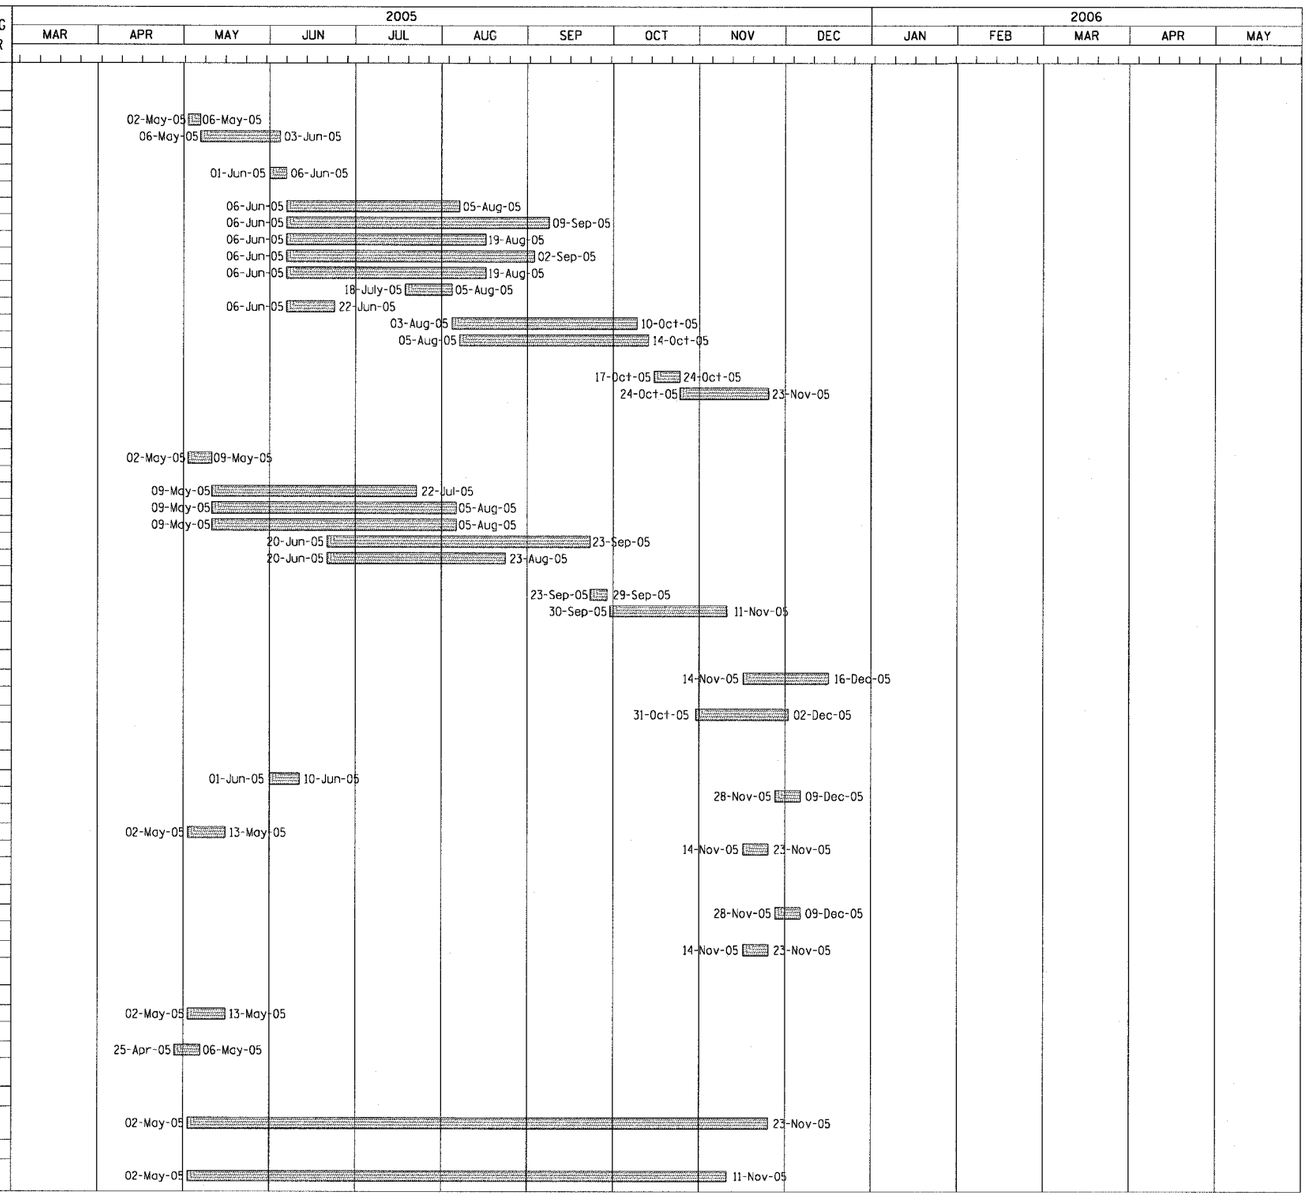

NOTE: DATES ASSOCIATED WITH WORK ITEMS MAY CHANGE BASED ON OTHER CONTRACTS AND/OR THE ENGINEER. NO ADDITIONAL COMPENSATION WILL BE CONSIDERED DUE TO CHANGES OR EXTENSIONS IN THE SCHEDULE.

LEGEND:

WORK PERFORMED IN CONTRACTS BY OTHERS

WORK PERFORMED AS PART OF THIS CONTRACT

CTE ENGINEERS
CONSOER TOWNSEND ENVIRODYNE ENGINEERS, INC.
303 EAST WACKER DRIVE, SUITE 600
CHICAGO ILLINOIS 60601-5212, PHONE: (312) 938-0300

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 90/94 (DAN RYAN EXPRESSWAY)
59th ST TO 47th ST (FRONTAGE ROAD)
CITY OF CHICAGO LIGHTING CONDUIT & FOUNDATIONS
WENTWORTH AVENUE

SUGGESTED CONSTRUCTION SCHEDULE

SCALE: NONE DRAWN BY: AMM
DATE: February 11, 2005 CHECKED BY: RMG

\\ctech-nt\Vp40466\p40466\elect\14-cntr9c\contract 9b\3cs09b300402c.sht 02/02/2005 09:09:59 AM
