F.A.I.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
94/90	*	COOK	598	4
STA.		TO STA.		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

62302 *(1816, ETC, 2324.6-1PIR-9

Project Construction Schedule
Dan Ryan Expressway

ID	Task Name	Duration	Start	Finish
1	LOCAL LANE PAVEMENT PATCHING	52 days	Sat 10/1/05	Wed 11/30/05
2	SETUP AND MAINTAIN ALTERNATE ROUTE SIGNING	359 days	Mon 1/2/06	Wed 2/28/07
3	PLACE INTERIM LOCAL LANE SIGNING	26 days	Mon 1/2/06	Tue 1/31/06
4	REMOVE OVERHEAD LOCAL LANE SIGN TRUSSES	24 days	Wed 2/1/06	Tue 2/28/06
5	RESTRIPE / SHIFT LOCAL LANE TRAFFIC	12 days	Wed 2/15/06	Tue 2/28/06
6	PLACE TEMPORARY CONCRETE BARRIER WALL	12 days	Wed 2/15/06	Tue 2/28/06
7	MAINTENANCE AND POSSESSION OF TEMPORARY CONCRETE BARRIER WALL	321 days	Wed 2/15/06	Wed 2/28/07
8	PAVEMENT AND APPURTENANCE REMOVAL	132 days	Wed 3/1/06	Tue 8/1/06
9	REMOVE OVERHEAD EXPRESS LANE SIGN TRUSSES	40 days	Wed 3/1/06	Sat 4/15/06
10	BARRIER WALL REMOVAL	118 days	Wed 3/1/06	Sat 7/15/06
11	PLACEMENT OF CHAIN LINK FENCE, 6' (SPECIAL)	40 days	Wed 3/1/06	Sat 4/15/06
12	NB HIGH BRIDGE <ROOSEVELT TO 31ST> REPAIRS (BY CONTRACT 62580)	194 days	Thu 3/16/06	Fri 10/27/06
13	LIGHT POLE REMOVALS (BY CONTRACT 62583)	65 days	Wed 3/1/06	Mon 5/15/06
14	SEWER JACKING	80 days	Wed 3/1/06	Thu 6/1/06
15	MAIN DRAIN CONNECTIONSREPAIRS (BY CONTRACT 62580)	80 days	Fri 3/31/06	Sat 7/1/06
16	EARTH EXCAVATION	105 days	Sat 4/1/06	Tue 8/1/06
17	LIGHT POLE FOUNDATION REMOVALS	38 days	Sat 4/1/06	Mon 5/15/06
18	DRAINAGE INSTALLATIONS	144 days	Sat 4/1/06	Fri 9/15/06
19	CTA BARRIER REMOVAL	91 days	Sat 4/1/06	Sat 7/15/06
20	72" CTA BARRIER WALL INSTALLATION	65 days	Sat 4/1/06	Thu 6/15/06
21	SUB-BASE GRANULAR PLACEMENT	119 days	Sat 4/15/06	Thu 8/31/06
22	PERSHING BOX CULVERT REPAIRS	92 days	Sat 4/15/06	Mon 7/31/06
23	LUG SYSTEM INSTALLATIONS	93 days	Sat 4/15/06	Tue 8/1/06
24	RETAINING WALL SEL	53 days	Mon 5/1/06	Fri 6/30/06
25	OVERHEAD SIGN FOUNDATIONS	79 days	Mon 5/1/06	Mon 7/31/06
26	FABRICATE OVERHEAD SIGN TRUSSES	106 days	Mon 5/1/06	Thu 8/31/06
27	PIPE UNDERDRAIN PLACEMENT	119 days	Mon 5/1/06	Fri 9/15/06
28	ELECTRICAL HANDHOLES AND CONDUITS	106 days	Mon 5/1/06	Thu 8/31/06
29	STABILIZED SUB-BASED	40 days	Thu 6/15/06	Mon 7/31/06
30	CRPCC 14" PAVEMENT	79 days	Fri 6/16/06	Fri 9/15/06
31	TEMP BARRIER WALL & LANE STRIPING (EXPRESS LANE)	86 days	Fri 6/23/06	Sat 9/30/06
32	WATER MAIN PROTECTION CAPS	22 days	Fri 7/7/06	Tue 8/1/06
33	INTERIM COMPLETION DATE - OPEN SINGLE EXPRESS LANE	0 days	Tue 8/15/06	Tue 8/15/06
34	42" CTA BARRIER WALL AND FENCE	65 days	Tue 8/1/06	Sat 10/14/06
35	CONCRETE BARRIER TRANSITIONS	65 days	Tue 8/1/06	Sat 10/14/06
36	TEMPORARY PAVEMENT AND SHOULDERS	65 days	Tue 8/1/06	Sat 10/14/06
37	EXPRESS LANE OVERHEAD SIGN TRUSSES	65 days	Tue 8/1/06	Sat 10/14/06
38	MAIN DRAIN CLEANING AND REPAIRS	65 days	Tue 8/1/06	Sat 10/14/06
39	INSIDE PROPOSED SHOULDER PLACEMENT	52 days	Wed 8/16/06	Sat 10/14/06
40	PROPOSED SIGNING	49 days	Fri 9/1/06	Fri 10/27/06
41	ATTENUATOR INSTALLATIONS	49 days	Fri 9/1/06	Fri 10/27/06
42	DRAINAGE STRUCTURES TO BE CLEANED	49 days	Fri 9/1/06	Fri 10/27/06
43	EXPRESS LANE PAVEMENT MARKINGS	49 days	Fri 9/1/06	Fri 10/27/06
44	INTERIM COMPLETION DATE - MEET CONTRACT 62304 STAGING	0 days	Fri 9/1/06	Fri 9/1/06
45	RELOCATE / REMOVE TEMPORARY CONCRETE BARRIER WALL	23 days	Mon 10/2/06	Fri 10/27/06
46	RESTRIPE / SHIFT LOCAL LANE TRAFFIC	11 days	Mon 10/2/06	Fri 10/27/06

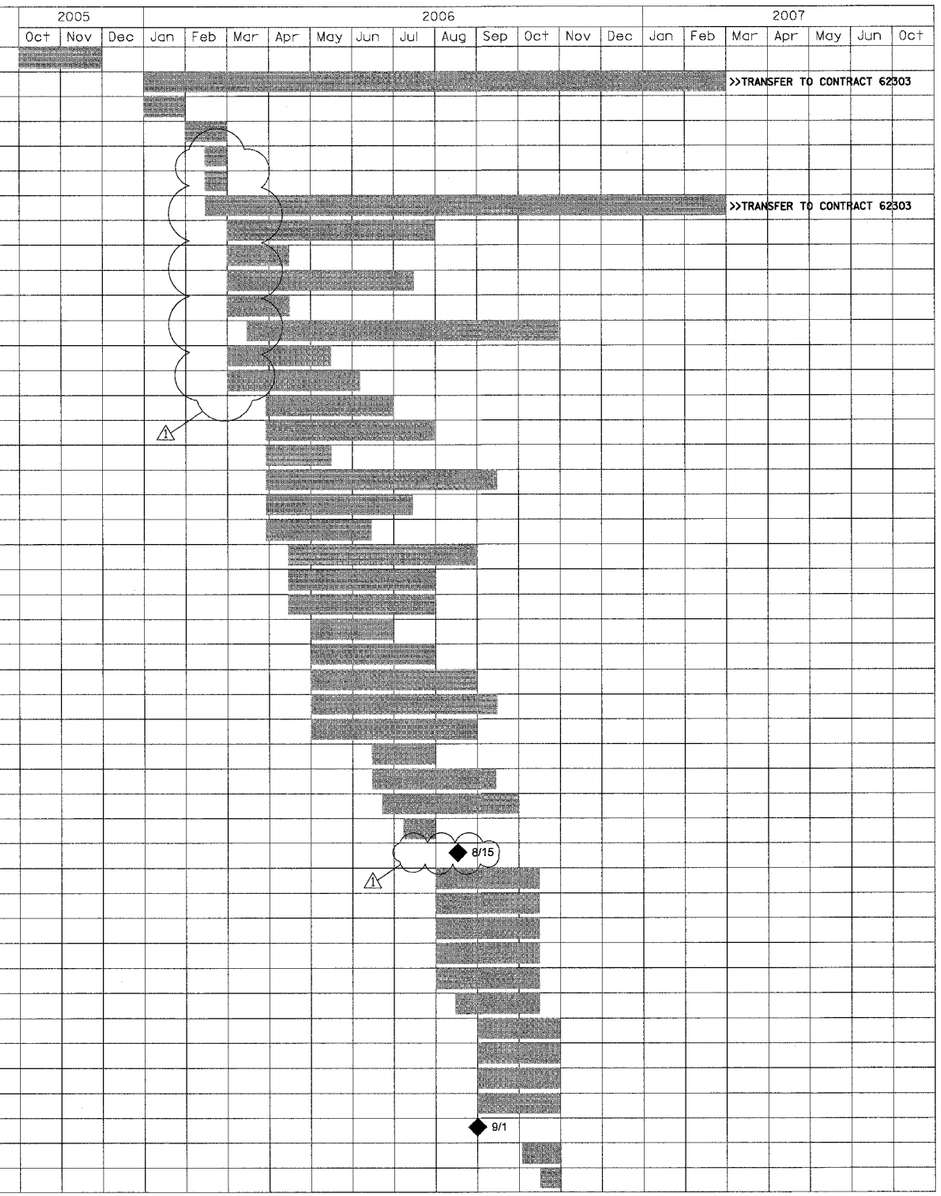

BOWMAN, BARRETT & ASSOCIATES INC.
CONSULTING ENGINEERS
Chicago, Illinois
312.228.0100
www.bbandainc.com

TASK: MILESTONE:

REVISIONS		
	NAME	DATE
1	ADDENDUM 1	8/12/05

ILLINOIS DEPARTMENT OF TRANSPORTATION

F.A.I. 94/90 (DAN RYAN EXPRESSWAY)
31ST STREET TO 71ST STREET
SB EXPRESS LANE RECONSTRUCTION

SUGGESTED CONSTRUCTION SCHEDULE

SCALE: NONE DRAWN BY: RZ
DATE: 07/07/05 CHECKED BY: JDC

n:\660\cad0\dn\N5\SHEETS\660_HSCSCH01.dgn 8/11/2005 2:32:07 PM
