F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90/94	2004-097DTR	COOK	21	3
STA.		TO STA.		
FED. ROAD DIST. NO. 1	ILLINOIS	FED. AID PROJECT		

62838

ACTIVITY ID	ACTIVITY DESCRIPTION	EARLY START	EARLY FINISH	ORIG DUR
CONTRACT 9C (62693) - WENTWORTH AVENUE				
PRE-STAGE - SEWER RELOCATION				
1	INSTALL TRAFFIC CONTROL	02-May-05	06-May-05	
2	SEWER RELOCATION (STA. 112+88 TO STA. 126+58)	06-May-05	03-Jun-05	
STAGE 1 - RETAINING WALLS & PAVE INSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	01-Jun-05	06-Jun-05	
2	CONSTRUCT PROPOSED RETAINING WALLS			
a.	S.N. 016-W882	06-Jun-05	05-Aug-05	
b.	S.N. 016-W886	06-Jun-05	09-Sep-05	
c.	S.N. 016-W901	06-Jun-05	19-Aug-05	
d.	S.N. 016-W887/W965	06-Jun-05	02-Sep-05	
e.	S.N. 016-WWRR	06-Jun-05	19-Aug-05	
3	COMED RELOCATION (60TH STREET)	18-July-05	05-Aug-05	
4	SEWER RELOCATION (STA. 126+58 TO STA. 131+12)	06-Jun-05	22-Jun-05	
5	CONSTRUCT PROPOSED FRONTAGE ROAD	03-Aug-05	10-Oct-05	
6	CONSTRUCT 14" TEMPORARY PAVEMENT & CONCRETE RAMPS	05-Aug-05	14-Oct-05	
STAGE 2 - PAVE OUTSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	17-Oct-05	24-Oct-05	
2	CONSTRUCT PROPOSED FRONTAGE ROAD	24-Oct-05	23-Nov-05	
CONTRACT 9C (62693) - WELLS STREET				
STAGE 1 - RETAINING WALLS & PAVE INSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	02-May-05	09-May-05	
2	CONSTRUCT PROPOSED RETAINING WALLS			
a.	S.N. 016-W894/964	09-May-05	22-Jul-05	
b.	S.N. 016-W903/W906	09-May-05	05-Aug-05	
c.	S.N. 016-W907	09-May-05	05-Aug-05	
4	CONSTRUCT PROPOSED FRONTAGE ROAD	20-Jun-05	23-Sep-05	
5	CONSTRUCT 14" TEMPORARY PAVEMENT & CONCRETE RAMPS	20-Jun-05	23-Aug-05	
STAGE 2 - PAVE OUTSIDE FRONTAGE				
1	INSTALL TRAFFIC CONTROL	23-Sep-05	29-Sep-05	
2	CONSTRUCT PROPOSED FRONTAGE ROAD	30-Sep-05	11-Nov-05	
CONTRACT 9C1 (62835) - SIDEWALKS & DRIVEWAYS				
WENTWORTH AVENUE				
1	CONSTRUCT PROPOSED SIDEWALKS & DRIVEWAYS	14-Nov-05	16-Dec-05	
WELLS STREET				
1	CONSTRUCT PROPOSED SIDEWALKS & DRIVEWAYS	31-Oct-05	02-Dec-05	
CONTRACT 9C4 (62836) - FRONTAGE ROAD SIGNING				
WENTWORTH AVENUE				
1	REMOVE EXISTING SIGNING	01-Jun-05	10-Jun-05	
2	INSTALL NEW SIGNAGE / REINSTALL SIGNAGE	28-Nov-05	09-Dec-05	
WELLS STREET				
1	REMOVE EXISTING SIGNING	02-May-05	13-May-05	
2	INSTALL NEW SIGNAGE / REINSTALL SIGNAGE	14-Nov-05	23-Nov-05	
CONTRACT 9C5 (62837) - FRONTAGE ROAD PAVEMENT MARKING				
STAGE 2 - WENTWORTH AVENUE				
1	INSTALL PERMANENT PAVEMENT MARKINGS	28-Nov-05	09-Dec-05	
STAGE 2 - WELLS STREET				
1	INSTALL PERMANENT PAVEMENT MARKINGS	14-Nov-05	23-Nov-05	
CONTRACT 9C6 (62838) - TREE REMOVAL				
WENTWORTH AVENUE				
1	REMOVE EMBANKMENT TREES	02-May-05	13-May-05	
WELLS STREET				
1	REMOVE EMBANKMENT TREES	25-Apr-05	06-May-05	
CONTRACT 9C7 (62839) - 59TH STREET TRAFFIC SIGNALS				
59TH STREET & WENTWORTH AVENUE				
1	INSTALL AND MAINTAIN TEMPORARY TRAFFIC SIGNALS, REMOVE EXISTING AND INSTALL NEW LIGHTING AND TRAFFIC SIGNALS	02-May-05	23-Nov-05	
59TH STREET & WELLS STREET				
1	INSTALL AND MAINTAIN TEMPORARY TRAFFIC SIGNALS, REMOVE EXISTING AND INSTALL NEW LIGHTING AND TRAFFIC SIGNALS	02-May-05	11-Nov-05	

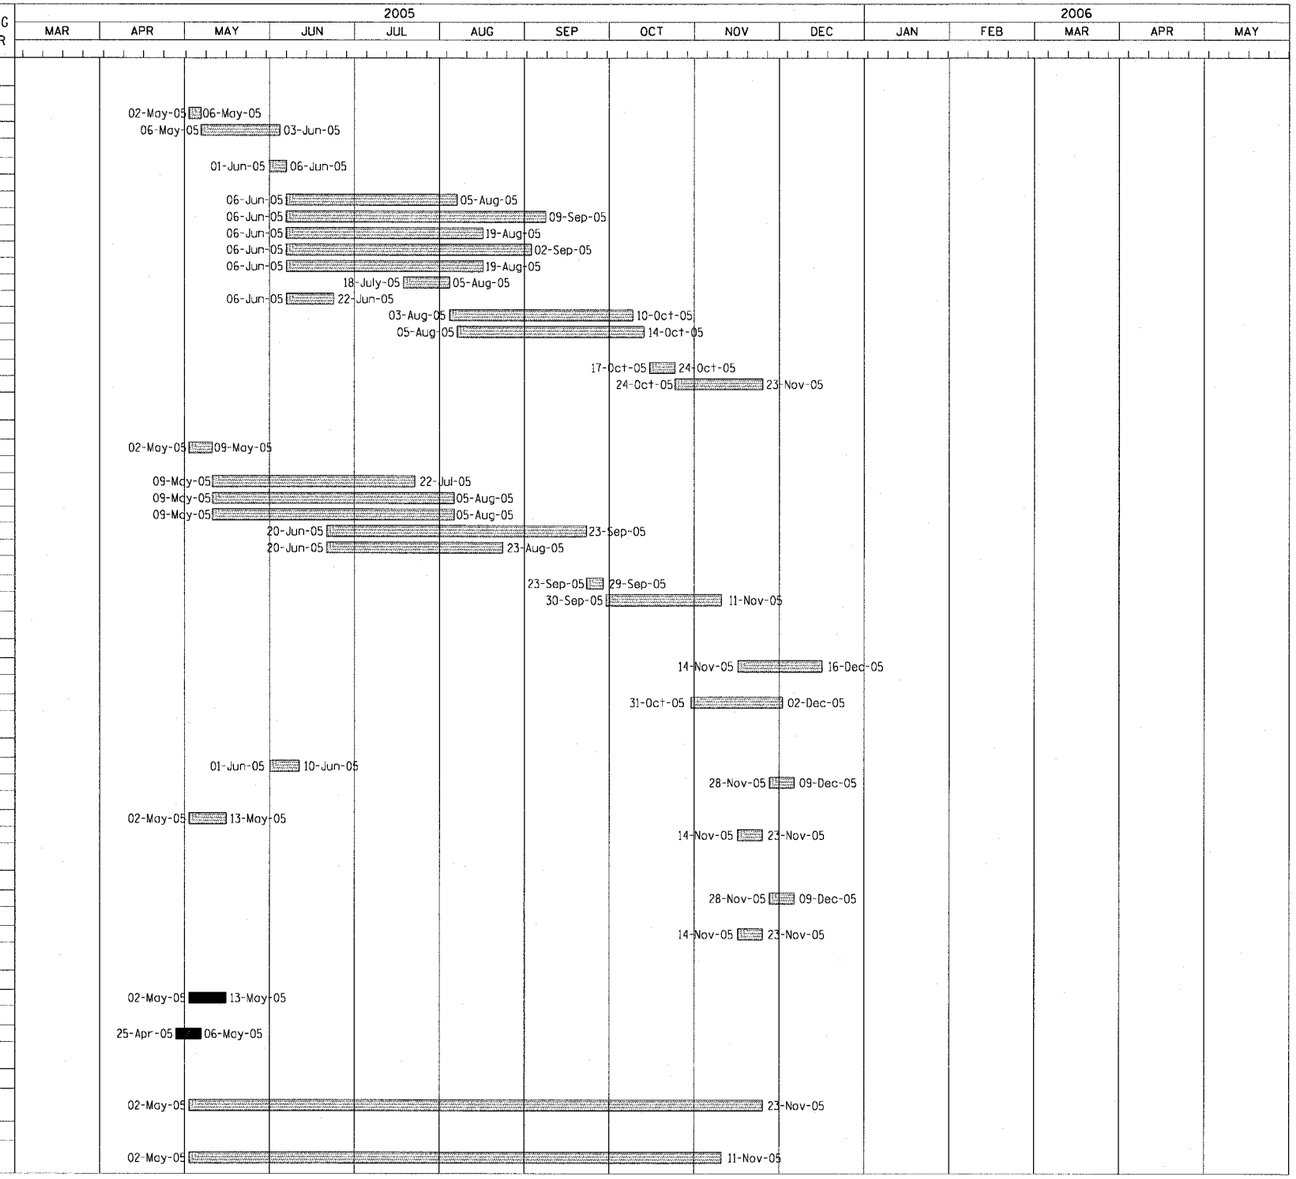

NOTES: DATES ASSOCIATED WITH WORK ITEMS MAY CHANGE BASED ON OTHER CONTRACTS AND/OR THE ENGINEER. NO ADDITIONAL COMPENSATION WILL BE CONSIDERED DUE TO CHANGES OR EXTENSIONS IN THE SCHEDULE.

SETUP FOR STAGE 1 TRAFFIC CONTROL CANNOT BEGIN UNTIL THE GARFIELD BLVD (55TH STREET) RAMPS ARE OPEN TO TRAFFIC IN CONTRACT 62586.

CTE ENGINEERS
CONSOER TOWNSEND ENVIRODYNE ENGINEERS, INC.
303 EAST WACKER DRIVE, SUITE 600
CHICAGO ILLINOIS 60601-5212, PHONE: (312) 938-0300

⚠ Rev. 1-7-05

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 90/94 (DAN RYAN EXPRESSWAY)
63rd ST TO 59th ST (TREE REMOVAL)

SUGGESTED CONSTRUCTION SCHEDULE

SCALE: NONE
DATE: October 22, 2004
DRAWN BY: AMM
CHECKED BY: RMG

12/3/2004 10:32:51 AM

MAP-P40-P46-P-C-W1-V4E-Cntr-9c-Add_Cntr-9c-Add_Cntr-9c-Sch-S-S-S-S-C-D-2A.SHT
