CONTRACT NO. 64C60

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
654	109 T	CARROLL	36	15
STA.		TO STA.		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

HORIZONTAL & VERTICAL CONTROL

APPARENT PROPERTY CORNERS

POINT	NORTH	EAST	ELEVATION	CHAIN	STATION	OFFSET	DESCRIPTION
700	2004327.8399	2394701.3440	928.1711	73	271+62.0288	5302.5024′ RT	PROPERTY CORNER, PIN
701	2004277.7034	2389393.3760	882.0622	73	272+43.0483	5.0841′ LT	PROPERTY CORNER, RAIL ROAD SPIKE
702	2004229.8704	2386749.9496	835.3716	73	272+60.5395	2648.8853′ LT	PROPERTY CORNER, PIN
703	2009566.2529	2383964.1909	866.1856	73	326+22.1276	5317.7428′ LT	PROPERTY CORNER, PIN
704	2009642.7694	2391909.5924	831.8167	73	325+65.1433	2627.8228′ RT	PROPERTY CORNER, RAIL ROAD SPIKE
705	2009620.6941	2394678.9486	938.0739	73	324+96.5434	5396.4172′ RT	R.O.W. CORNER, PIN
706	2014905.0862	2394514.9303	938.3865	73	377+82.9453	5321.2047′ RT	PROPERTY CORNER, PIN
707	2014817.7280	2389154.7355	911.3484	73	377+85.6556	39.7012′ LT	QUARTER CORNER, PIN
708	2014834.6237	2383910.7497	857.4501	73	378+90.6527	5282.663′ LT	PROPERTY CORNER, NAIL
709	2015316.8154	2383988.8263	891.4545	73	383+71.4646	5196.4962′ LT	TRAVERSE STATION, NAIL
710	2012310.2563	2389206.3180	803.8525	73	352+77.6712	30.2538′ LT	PROPERTY CORNER, PIN
711	2006948.2588	2389316.5089	926.1689	73	299+14.6877	15.9479′ LT	PROPERTY CORNER, NAIL
712	2004354.5829	2397336.5684	929.6262	73	271+23.6567	7937.5831′ RT	QUARTER CORNER, PIN
713	2004370.4992	2399978.6808	942.8918	73	270+74.2911	10579.2822′ RT	SECTION CORNER, PIN
714	2007045.9543	2399886.0257	975.7411	73	297+51.2187	10552.7563′ RT	FENCE POST, PIN
715	2009718.8462	2399855.6229	958.7313	73	325+07.7088	10574.0099′ RT	SECTION CORNER, PIN
716	2009684.3449	2397207.0467	967.7885	73	325+17.7108	7925.2279′ RT	QUARTER CORNER, RAIL ROAD SPIKE
717	2009650.2236	2394558.2640	935.3539	73	325+28.0963	5276.2458′ RT	SECTION CORNER, PIN
718	2014818.8002	2389221.0618	911.0664	73	377+85.6133	26.6337′ RT	QUARTER CORNER, PIN
719	2014831.9900	2383861.6700	858.7300	73	378+88.8439	5331.78′ LT	QUARTER CORNER, PIPE

HORIZONTAL CONTROL POINTS

POINT	NORTH	EAST	ELEVATION	CHAIN	STATION	OFFSET	DESCRIPTION
12	2010044.2130	2389257.8750	879.3020	73	330+11.0815	16.7757′ LT	TRAVERSE STATION, PIN
11	2008649.1045	2389280.3903	930.0062	73	316+15.7917	17.7027′ LT	TRAVERSE STATION, PIN

CURVE POINT NUMBERS

CHAIN	CURVE	PI	CC	PC	PT
73	200	200	201	202	203

CURVE POINT NUMBERS

CHAIN	CURVE	PI	CC	PC	PT
P&Q_RD	210	210	211	212	213
P&Q_RD	220	220	221	222	223
P&Q_RD	230	230	231	232	233

BENCH MARKS

POINT	NORTH	EAST	ELEVATION	CHAIN	STATION	OFFSET	DESCRIPTION
411	2008866.1320	2389317.4260	923.1550	73	318+32.1663	22.974′ RT	HEADWALL, CHISELED SQUARE
412	2009570.9530	2389229.4210	889.4370	73	325+38.3664	53.1769′ LT	R.O.W. MARKER, TOP

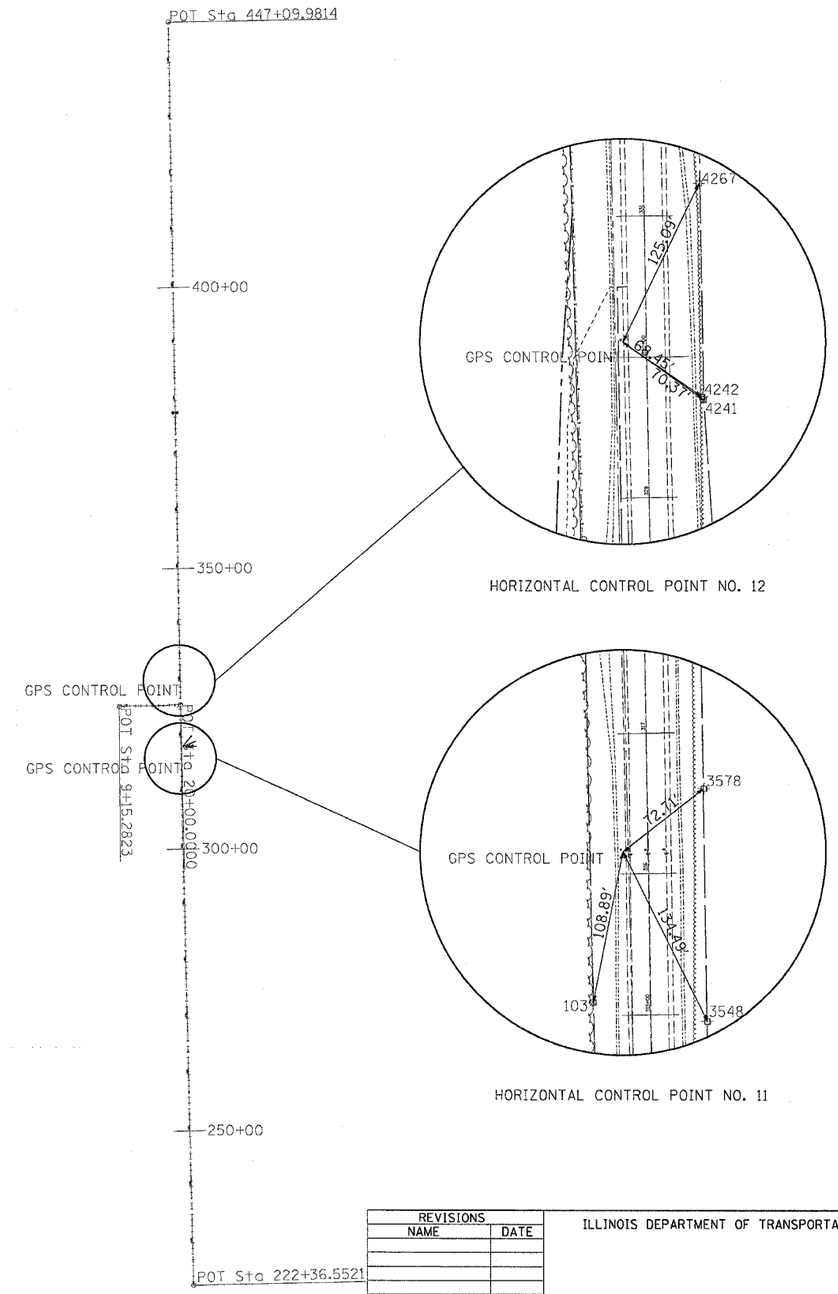

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

SCALE: VERT. HORIZ.

DATE

DRAWN BY

CHECKED BY

PLOT DATE = Fri Mar 16 11:03:50 2007
FILE NAME = c:\projects\o210305\d8285hvc.dgn
PLOT SCALE = 50.0000 ' / IN.
USER NAME = garfjl

HORIZONTAL & VERTICAL CONTROL
