CONTRACT NO. 62636

F.A.I RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
94	2003-071 RS	COOK	91	13
STA.		TO STA.		
FED. ROAD DIST. NO. 1	ILLINOIS	FED. AID PROJECT		

STAGE I: 2007

WEEKDAY OPERATIONS:

WORK SEQUENCE:

APPLY TEMPORARY PAVEMENT MARKING LANES 1 & 2
(LANE CLOSURES ALLOWED AS DETAILED IN THE SPECIAL PROVISIONS)
COMPLETE PATCH OPERATIONS LANE 3 AND OUTSIDE SHOULDER WHERE SPECIFIED
COMPLETE JOINT REPAIR BETWEEN LANE 3 AND SHOULDER AT LOCATIONS SPECIFIED IN THE SCHEDULE

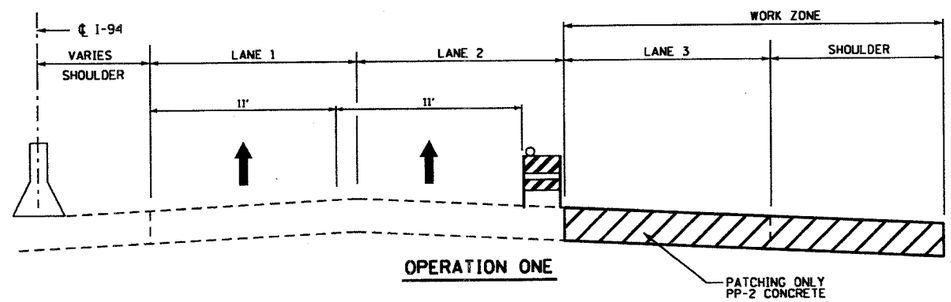

OPERATION ONE

WEEKEND OPERATIONS:

(LANE CLOSURES ALLOWED AS DETAILED IN THE SPECIAL PROVISIONS)
COMPLETE PATCH OPERATIONS LANE 2 USING PP-5 CONCRETE
LANE 2 AND 3 CLOSURE
FRIDAY 10:00 PM TO SATURDAY 9:00 AM
AND SATURDAY 10:00 PM TO SUNDAY 9:00 AM.



OPERATION TWO

PATCHING REQUIRED IN LANE 2

WEEKEND OPERATIONS (AFTER 9:00 AM SATURDAY AND SUNDAY):

TRAFFIC CONTROL AS PER DISTRICT ONE DETAIL FOR FREEWAY CENTER LANE CLOSURE.
CENTER LANE CLOSURE SHALL BE REMOVED ONCE CLASS A PATCH REACHES APPROPRIATE STRENGTH.

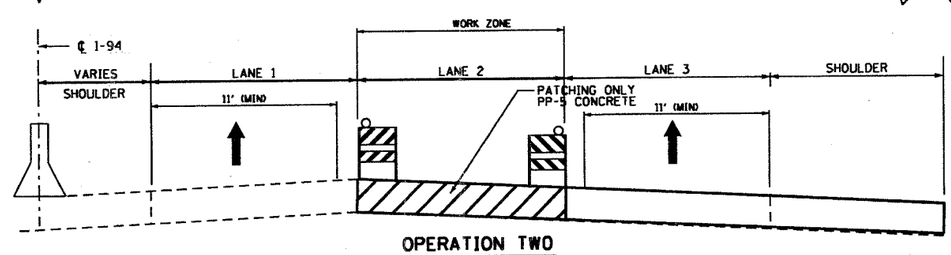

OPERATION TWO

PATCHING REQUIRED IN LANE 2

REVISIONS	
NAME	DATE
HWL	7/11/07

ILLINOIS DEPARTMENT OF TRANSPORTATION

N.T.S.

TRAFFIC CONTROL
AND PROTECTION
F.A.I. 94 EDENS EXPRESSWAY
TYPICAL SECTIONS PER SEGMENT

SCALE: DRAWN BY
DATE JUNE 2007 CHECKED BY

Edens I 94 Resurfacing Project

Rev. 7-20-07

PLOT DATE : 7/18/2007
FILE NAME : $FILE$
PLOT SCALE : $SCALE$
USER NAME : $DATE$
