PART OF THE NE 1/4 SECTION 20, T36N, R14E OF THE 3rd PM, THORNTON TOWNSHIP, COOK COUNTY, ILLINOIS.

PARCEL NUMBER	OWNER	TOTAL HOLDING HA – [AC]	PART TAKEN HA – [AC]	REMAINDER HA – [AC]	PREV. DED. HA–[AC]	EASEMENT HA – [AC]	EASEMENT PURPOSE	PERMANENT TAX INDEX NUMBER	PROPERTY ACQUIRED BY
ODE0213	I. MICHAEL IBARRA	0.0976 [0.241]	0.0096 [0.024]	0.0880 [0.217]				29–20–202–001;002;003	0020377622
ODE0213TE						0.0880 [0.217]	BUILDING DEMOLITION		
ODE0214	KINGSMEN LLC	0.1163 [0.287]	0.1163 [0.287]	0.0000 [0.000]				29–20–202–004;005;006;007	
ODE0215	SUPREME FINANCE CORPORATION	0.0974 [0.241]	0.0096 [0.024]	0.0878 [0.217]				29–20–202–008;009;010	
ODE0215TE						0.0625 [0.154]	BUILDING DEMOLITION		

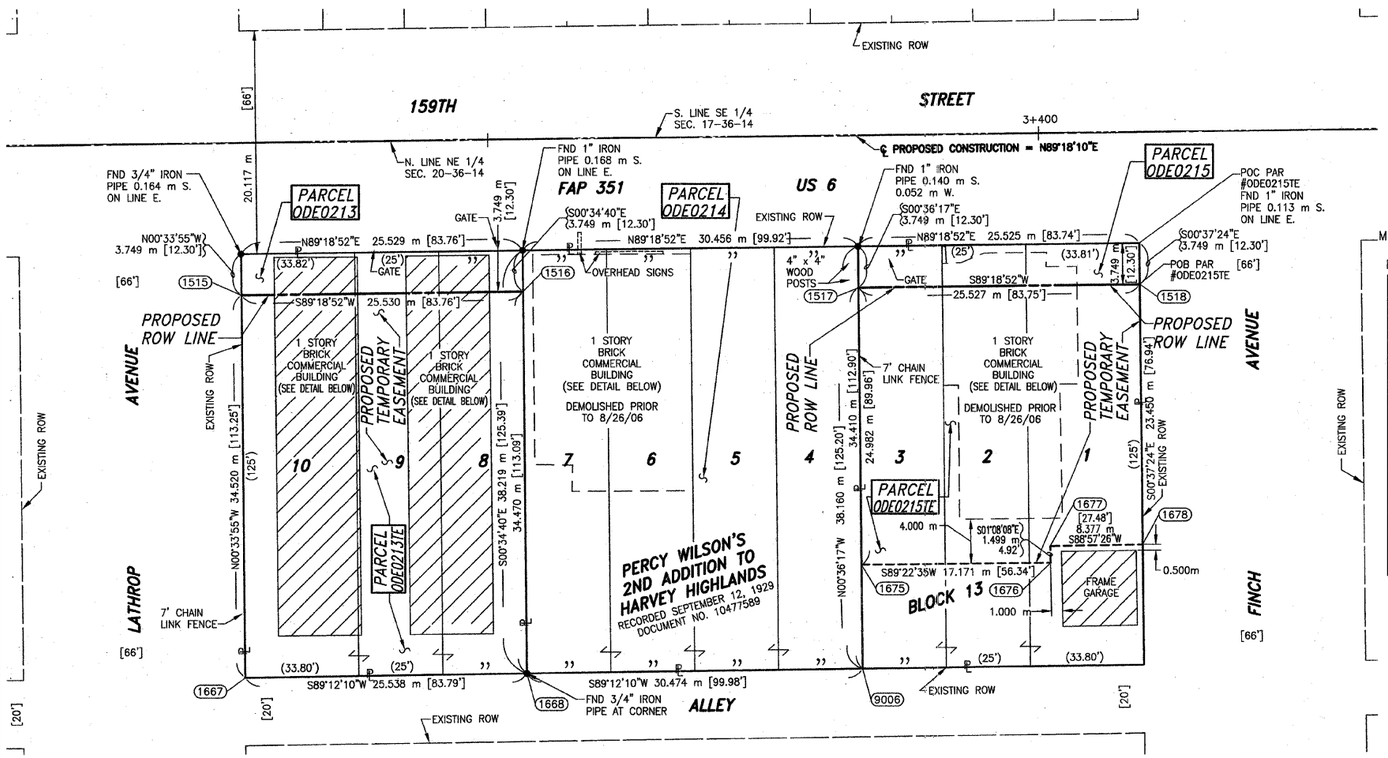

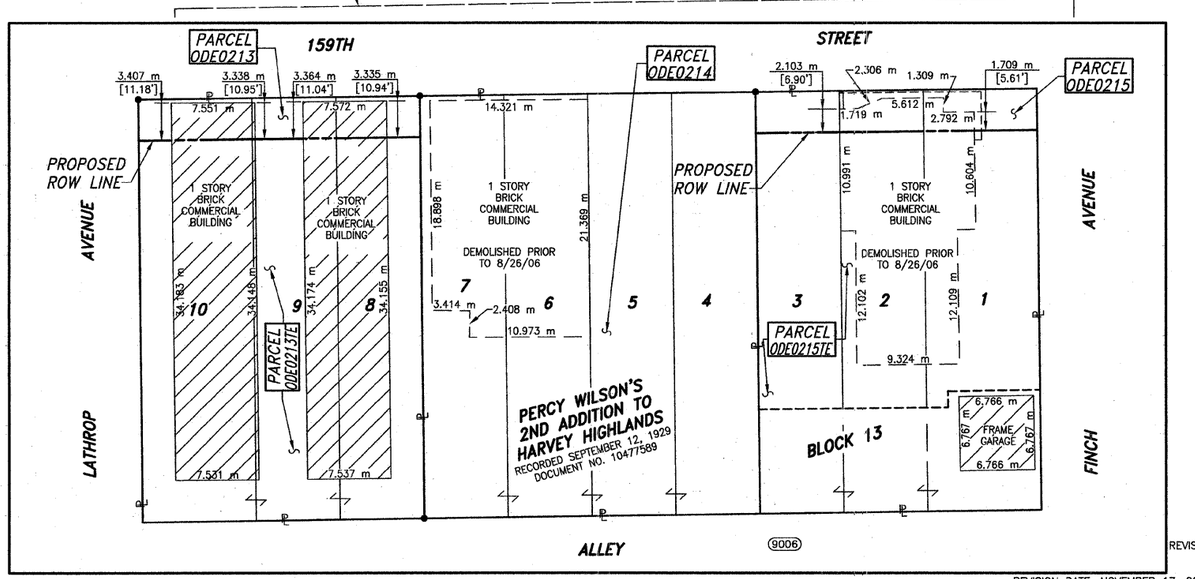

LEGEND

TOTAL SHEETS 541 — SHEET NO. 217

SECTION CORNER — QUARTER SECTION CORNER

SECTION LINE
QUARTER SECTION LINE
QUARTER, QUARTER SECTION LINE
PLATTED LOT LINE
PROPERTY (DEED) LINE
APPARENT PROPERTY LINE
CENTERLINE
EXISTING RIGHT OF WAY LINE
PROPOSED RIGHT OF WAY LINE
PROPOSED EASEMENT
EXISTING ACCESS CONTROL LINE
PROPOSED ACCESS CONTROL LINE
123.456m [1.23'] MEASURED DIMENSION METRIC WITH IMPERIAL
123.45' (COMP) [0.00'] COMPUTED DIMENSION METRIC WITH IMPERIAL
( ) RECORD DATA
EXISTING BUILDING

BEARINGS REFERENCED TO THE ILLINOIS STATE PLANE COORDINATE SYSTEM, EAST ZONE, NAD 1983, PROVIDED BY THE ILLINOIS DEPARTMENT OF TRANSPORTATION.

● IRON PIPE OR ROD FOUND — ○ SET 5/8" x 30" REBAR
+ CUT CROSS FOUND OR SET — ●PK FOUND PK NAIL — ○PK SET PK NAIL

● T1 T2 T3 **THESE STAKES REFERENCE FOUND OR SET MONUMENTATION.** SET 5/8 INCH REBAR FLUSH WITH GROUND TO TIE FOUND IRON STAKE. IDENTIFIED BY COLORED PLASTIC CAP AND BEARING SURVEYORS PROFESSIONAL NUMBER.

● BT1 BT2 BT3 **THESE STAKES, IN CULTIVATED AREAS, REFERENCE FOUND OR SET MONUMENTATION.** BURIED 5\8 INCH REBAR 20 INCHES BELOW GROUND TO TIE FOUND IRON STAKE. IDENTIFIED BY COLORED PLASTIC CAP BEARING SURVEYORS PROFESSIONAL NUMBER.

■ **STAKING OF PROPOSED RIGHT OF WAY.** SET DIVISION OF HIGHWAYS SURVEY MARKER TO MONUMENT THE POSITION SHOWN. IDENTIFIED BY INSCRIPTION DATA AND SURVEYORS PROFESSIONAL NUMBER.

■ M **STAKING OF PROPOSED RIGHT OF WAY IN CULTIVATED AREAS.** BURIED 5/8 INCH REBAR 20 INCHES BELOW GROUND TO MARK FUTURE SURVEY MARKER POSITION. IDENTIFIED BY COLORED PLASTIC CAP BEARING SURVEYORS PROFESSIONAL NUMBER.

PERMANENT SURVEY MARKER. IDOT STD. 2135 (TO BE SET BY OTHERS)

□ RIGHT OF WAY STAKING PROPOSED TO BE SET.

COORDINATE VALUE

METRIC PROJECT COORDINATES ARE GROUND VALUES AND CAN BE CONVERTED TO GRID VALUES BY MULTIPLYING THE PUBLISHED GROUND COORDINATES BY 0.999988, PROVIDED BY THE ILLINOIS DEPARTMENT OF TRANSPORTATION.

COORDINATE TABLE

DATA POINT NO.	STATION	OFFSET	–N– COORDINATES	–E–
1667	3+327.430	48.243 m R	547,964.4242	357,704.6040
1515	3+327.510	13.724 m R	547,998.9422	357,704.2634
1668	3+352.968	48.199 m R	547,964.7796	357,730.1390
1516	3+353.040	13.729 m R	547,999.2477	357,729.7914
1673	3+375.823	48.159 m R	547,965.0976	357,752.9925
1517	3+383.498	13.735 m R	547,999.6122	357,760.2472
1518	3+409.024	13.740 m R	547,999.9177	357,785.7719
1675	3+383.457	38.717 m R	547,974.6313	357,760.5109
1676	3+400.629	38.739 m R	547,974.8182	357,777.6811
1677	3+400.617	37.241 m R	547,976.3167	357,777.6514
1678	3+408.994	37.190 m R	547,976.4692	357,786.0269
9006	3+383.442	48.145 m R	547,965.2036	357,760.6104

STATE OF ILLINOIS } SS
COUNTY OF COOK }

THIS IS TO CERTIFY THAT I, COVENTINE FIDIS, AN ILLINOIS PROFESSIONAL LAND SURVEYOR, HAVE RESURVEYED PARCEL ODE0214 ON THE PLAT OF HIGHWAYS SHOWN HEREON IN SECTION 20, TOWNSHIP 36 NORTH, RANGE 14 EAST OF THE THIRD PRINCIPAL MERIDIAN, COOK COUNTY; THAT SAID PLAT OF HIGHWAYS WAS ORIGINALLY SIGNED AND CERTIFIED ON MARCH 26, 2002 BY THOMAS E. BAUMGARTNER, ILLINOIS PROFESSIONAL LAND SURVEYOR NO. 3142; THAT THE RESURVEY IS TRUE AND COMPLETE AS SHOWN TO THE BEST OF MY KNOWLEDGE AND BELIEF; THAT THE PLAT CORRECTLY REPRESENTS SAID RESURVEY; THAT ALL MONUMENTS FOUND AND ESTABLISHED ARE OF PERMANENT QUALITY AND OCCUPY THE POSITIONS SHOWN THEREON AND THAT THE MONUMENTS ARE SUFFICIENT TO ENABLE THE RESURVEY TO BE RETRACED. MADE FOR THE DEPARTMENT OF TRANSPORTATION, STATE OF ILLINOIS.

DATED AT CHICAGO, ILLINOIS THIS 28TH DAY OF AUGUST, 2006 A.D.

COVENTINE FIDIS
ILLINOIS PROFESSIONAL LAND SURVEYOR NO. 2159
LICENSE EXPIRATION DATE: 11/30/06

THIS PROFESSIONAL SERVICE CONFORMS TO THE CURRENT ILLINOIS MINIMUM SURVEY STANDARDS.

STATE OF ILLINOIS — COVENTINE FIDIS — 35–2159 — CHICAGO, ILL. — PROFESSIONAL LAND SURVEYOR

BUILDING DETAIL

GRAPHIC SCALE (IN METERS) 5 0 2.5 5 10 15 20 25

1 : 250

GRAPHIC SCALE (IN METERS) 5 0 2.5 5 10 15 20 25

1 : 250

ASC
AMERICAN SURVEYING CONSULTANTS, P.C.
841 N. GALENA AVE. / DIXON, IL. 61021 / 815–288–6231
8604 W. CATALPA AVE. / CHICAGO, IL. 60656 / 773–444–0800
ILLINOIS PROFESSIONAL DESIGN FIRM NO. 184–003192

RECEIVED
APR 09 2007
PLATS & LEGALS

REVISION DATE: AUGUST 28, 2006 — REVISION: NOTED DEMOLISHED BUILDINGS ON PARCELS ODE0214 AND ODE0215. — MADE BY: DD
REVISION DATE: NOVEMBER 17, 2004 — REVISION: CHANGED PARCEL ODE0214 TO TOTAL TAKE AND REMOVED PARCEL ODE0214TE. — MADE BY: BAN
REVISION DATE: JULY 25, 2002 — REVISION: ADDED PARCEL ODE0215TE. — MADE BY: REW
REVISION DATE: SEPTEMBER 5, 2001 — REVISION: CHANGED OWNER FOR PARCEL ODE0214 AND ADDED PARCEL ODE0214TE. — MADE BY: JLS/RJW
REVISION DATE: FEBRUARY 7, 2001 — REVISION: ADDED PARCEL ODE0213TE. — MADE BY: KAR

JOB # 3378 ODE DWG. # 900–215–C6

PLAT OF HIGHWAYS
STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION
FAP 351 US 6 (159TH STREET)

SECTION — COOK COUNTY
PROJECT — JOB NO. R–90–011–99
STATION 3+315.000 — TO STATION 3+420.000
SCALE: 1:250 — SHEET C6 OF ___

BUREAU OF LAND ACQUISITION
201 WEST CENTER COURT
SCHAUMBURG, ILLINOIS 60196–1096

FAP 351 US 6 (159TH STREET), SECTION , JOB. NO. R–90–011–99.
