NORTH FRONTAGE RD

SHARED USE PATH

℄ SHARED USE PATH

FLEMING RD

℄ FLEMING RD

℄ NORTH FRONTAGE RD

MATCH LINE STA 563+00

500′ BUFFER PRIOR TO WORK ZONE

880′ LANE SHIFT TAPER

SIGN ACCORDING TO STD 701422
REPLACE LANE CLOSED AHEAD SIGN WITH LANE SHIFT AHEAD SIGNS
DELETE ARROW BOARD

℄ IL 13 WB

℄ IL 13 EB

IL 13 WB

IL 13 EB

220′ LANE SHIFT TAPER

℄ BRIGGS RD

℄ BRIGGS RD SPUR

BRIGGS RD SPUR

FOLLOWING STAGE 1 PREREQUISITES WITH STAGE 1D, TEMPORARY TIE TO EXISTING TO PROVIDE ACCESS TO BRIGGS RD/ BRIGGS RD SPUR.

BRIGGS RD

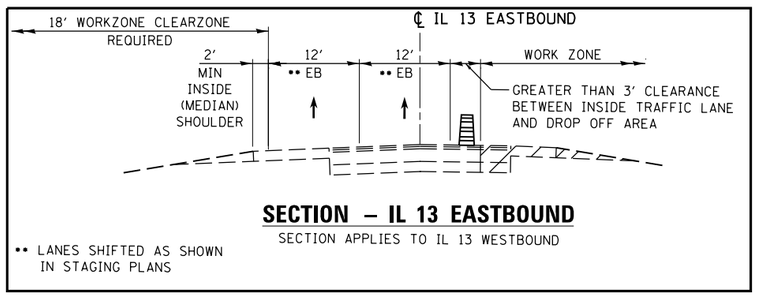


**SECTION – IL 13 EASTBOUND**

SECTION APPLIES TO IL 13 WESTBOUND

•• LANES SHIFTED AS SHOWN IN STAGING PLANS

N

0 50 100
SCALE IN FEET

**LEGEND**

- CONSTRUCTION THIS STAGE
- TEMPORARY PAVEMENT
- ROAD CLOSED
- DIRECTION OF TRAVEL/LANE MAINTAINED
- DRUMS, CONES, OR BARRICADE

| | | | |
|---|---|---|---|
| FILE NAME = c:\pw_work\pwidot\lavenderba\d0363618\D978221-sht-staging-07.dgn | USER NAME = $USER$ | DESIGNED - KN | REVISED - |
| | | DRAWN - AS | REVISED - |
| | PLOT SCALE = 200.0000 ′ / in. | CHECKED - | REVISED - |
| | PLOT DATE = 1/31/2014 | DATE - | REVISED - |

**STATE OF ILLINOIS**
**DEPARTMENT OF TRANSPORTATION**

**SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL**
**IL 13 – STAGE 1**

SCALE: | SHEET NO. 7 OF 17 SHEETS | STA. | TO STA.

| F.A.P. RTE. | SECTION | COUNTY | TOTAL SHEETS | SHEET NO. |
|---|---|---|---|---|
| 331 | (1-3)R-2, N-4, TS-4, HBK-1 | WILLIAMSON | 733 | 200 |
| DRAWING NO. TC-07 | | CONTRACT NO. 78221 | | |
| | | ILLINOIS FED. AID PROJECT | | |
