ID	Task Name
66	EARTH EXCAVATION
67	SUBBASE GRANULAR MATERIAL TYPE B 24"
68	ELECTRICAL DUCTBANKS
69	UNDERDRAINS
70	STABILIZED SUBBASE 6"
71	CONTINUOUSLY REINFORCED PCC PVMT 14"
72	PCC SHOULDERS 14"
73	HANDHOLES
74	CURB AND GUTTER
75	BARRIER WALL
76	SIGN FOUNDATIONS
77	BARRIER WALL TRANSITIONS
78	CONCRETE MEDIAN
79	TOPSOIL PLACEMENT
80	SEEDING
81	BLANKET
82	CONTRACT 62303 47TH TO 31ST STAGE 3
83	EROSION CONTROL
84	PAVEMENT REMOVAL
85	STORM SEWER
86	UNDERDRAINS
87	EARTH EXCAVATION
88	SUBBASE GRANULAR MATERIAL TYPE B 24"
89	STABILIZED SUBBASE 6"
90	CONTINUOUSLY REINFORCED PCC PAVEMENT 14"
91	PCC SHOULDERS 14"
92	BARRIER WALL/GUARDRAIL
93	ELECTRICAL
94	TOPSOIL AND SEEDING
95	FINAL PAVEMENT MARKINGS/SIGNING
96	START STAGE 4: OPEN CONTRACT 62303 & 60A63 TO TRAFFIC
97	STAGE 4 WORK USING DAILY LANE CLOSURES
98	BARRIER WALL
99	RUMBLE STRIPS
100	CONTRACT 62303 & 60A63 COMPLETE
101	PUNCHLIST
102	CONTRACT 60A63
103	START CONTRACT 60A63 PRESTAGE
104	ELECTRICAL COORDINATION
105	EROSION CONTROL
106	FORMED CONCRETE REPAIRS
107	FABRICATE & DELIVER & ERECT OVERHEAD SIGN STRUCTURES
108	CONTRACT 60A63 69TH ST RETAINING WALL
109	ELECTRICAL DEMOLITION BY CITY
110	STRUCTURE EXCAVATION
111	CONCRETE REMOVAL
112	REINFORCING STEEL
113	CONCRETE SUPERSTRUCTURE
114	CHAIN LINK FENCE
115	INSTALL LIGHTING BY CITY
116	CONTRACT 60A63 3423+00 TO 3449+00 (Stage 1)
117	PAVEMENT REMOVAL
118	EARTH RETENTION SYSTEMS
119	STORM SEWERS
120	EARTH EXCAVATION
121	SUBBASE GRANULAR MATERIAL TYPE B 24"
122	ELECTRICAL DUCTBANK AND HANDHOLES
123	UNDERDRAINS
124	STABILIZED SUBBASE 6"
125	CONTINUOUSLY REINFORCED PCC PVMT 14"
126	PCC SHOULDERS 14"
127	CURB AND GUTTER
128	GUARDRAIL
129	BARRIER WALL
130	SIGN FOUNDATIONS

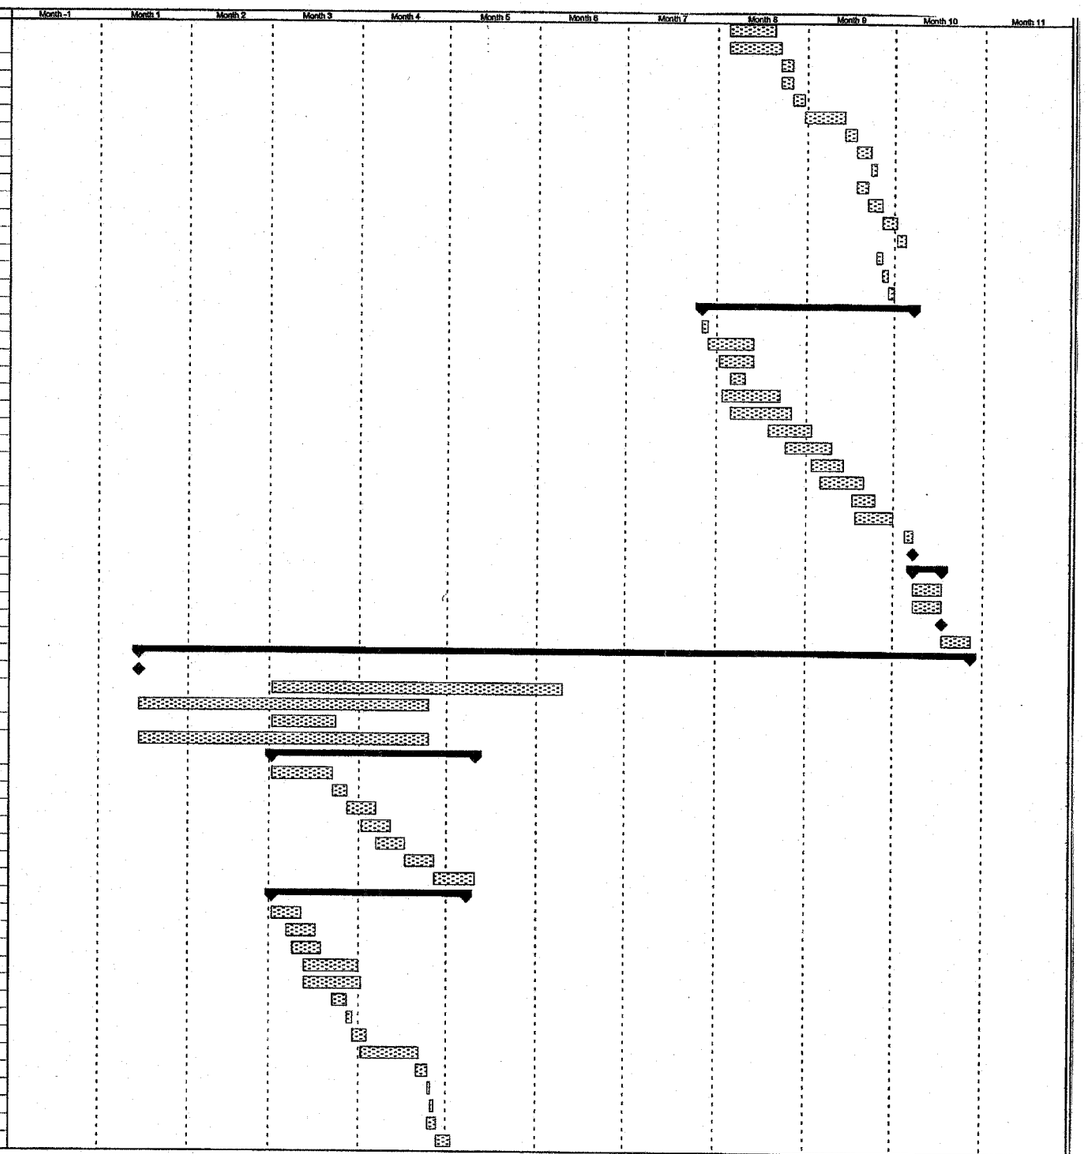

Project: DANRYAN19&19A REV3
Date: Fri 6/2/06

Task | Progress | Summary | Rolled Up Split | Rolled Up Progress | Project Summary | Deadline
Split | Milestone | Rolled Up Task | Rolled Up Milestone | External Tasks | External Milestone

CTE | AECOM

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90/94	*	COOK	588	5
STA.		TO STA.		
FED. ROAD DIST. NO. 1	ILLINOIS	FED. AID PROJECT		

62303 • (2021-922 PT2 ETC 2324.6-1P) R-11

D:\p4\45b\civil\8-cntrs 18 & 19\sht\cntr 19\schedules\cs90022a.sht

CS-2

REVISIONS NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 90/94 (DAN RYAN EXPRESSWAY)
GARFIELD BLVD TO 31ST STREET (SB LOCAL LANES)

SUGGESTED SEQUENCE OF OPERATION

SCALE: NONE
DATE: June 9, 2006
DRAWN BY: NJH
CHECKED BY: RMG

6/6/2006 7:35:15 PM
