F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO
353	(12&13)WRS-3	WILL	1235	221
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	

CONTRACT NO. 62479

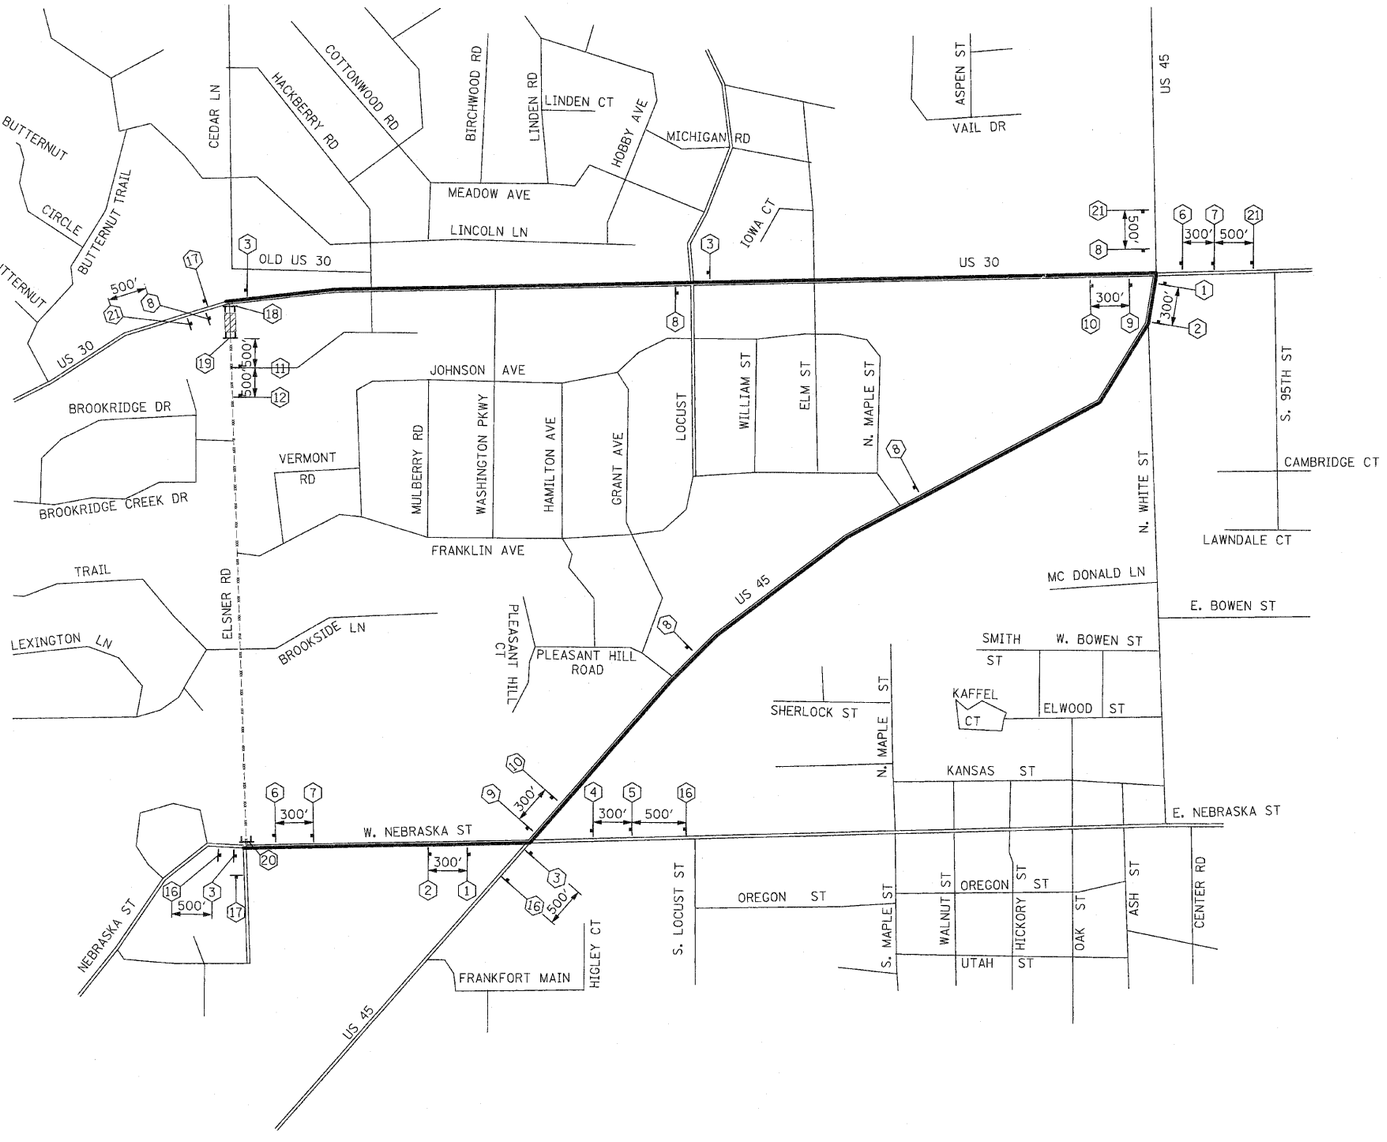

LEGEND

- DETOUR ROUTE
- PARTIALLY CLOSED ROADWAY
- COMPLETELY CLOSED ROADWAY
- MAJOR STREET
- MINOR STREET
- TYPE A MONODIRECTIONAL FLASHING LIGHT
- TYPE III BARRICADE

ELSNER ROAD

4" BLACK LETTERS ON ORANGE
REFLECTIVE BACKGROUND - 24" x 18"

SIGN DETAIL

SIGN LEGEND

1. DETOUR / NORTH / ELSNER ROAD — M4-8-2412, M3-1-2412, SEE DETAIL; M6-1L-2115
2. DETOUR / NORTH / ELSNER ROAD — M4-8-2412, M3-1-2412, SEE DETAIL; M5-1L-2115
3. DETOUR / NORTH / ELSNER ROAD — M4-8-2412, M3-1-2412, SEE DETAIL; M6-3-2115
4. DETOUR / NORTH / ELSNER ROAD — M4-8-2412, M3-1-2412, SEE DETAIL; M6-1R-2115
5. DETOUR / NORTH / ELSNER ROAD — M4-8-2412, M3-1-2412, SEE DETAIL; M5-1R-2115
6. DETOUR / SOUTH / ELSNER ROAD — M4-8-2412, M3-3-2412, SEE DETAIL; M6-1L-2115
7. DETOUR / SOUTH / ELSNER ROAD — M4-8-2412, M3-3-2412, SEE DETAIL; M5-1L-2115
8. DETOUR / SOUTH / ELSNER ROAD — M4-8-2412, M3-3-2412, SEE DETAIL; M6-3-2115
9. DETOUR / SOUTH / ELSNER ROAD — M4-8-2412, M3-3-2412, SEE DETAIL; M6-1R-2115
10. DETOUR / SOUTH / ELSNER ROAD — M4-8-2412, M3-3-2412, SEE DETAIL; M5-1R-2115
11. ROAD CLOSED 500 FT — W20-3-4848
12. ROAD CLOSED 1000 FT — W20-3-4848
13. ROAD CLOSED AHEAD — W20-3-4848
14. DETOUR AHEAD — W20-2-4848
15. ROAD CLOSED 500 FT — W20-3-4848
16. DETOUR AHEAD — W20-2-4848; NORTH / ELSNER RD — M3-1-2412, D3-3612 (BLACK ON ORANGE)
17. END DETOUR — M4-8A-2418
18. ROAD CLOSED TO THRU TRAFFIC / DETOUR — R11-4-6030; M4-10L-4818; TYPE III BARRICADE — MIN. 5 EACH
19. ROAD CLOSED — R11-2-4830; TYPE III BARRICADE — MIN. 5 EACH
20. ROAD CLOSED TO THRU TRAFFIC / DETOUR — R11-4-6030; M4-10R-4818; TYPE III BARRICADE — MIN. 5 EACH
21. DETOUR AHEAD — W20-2-4848; SOUTH / ELSNER RD — M3-3-2412, D3-3612 (BLACK ON ORANGE)
22. ROAD CLOSED AHEAD — W20-3-4848; NORTH / ELSNER RD — M3-1-2412, D3-3612 (BLACK ON ORANGE)
23. ROAD CLOSED AHEAD — W20-3-4848; SOUTH / ELSNER RD — M3-3-2412, D3-3612 (BLACK ON ORANGE)

REVISIONS NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

DETOUR PLAN STAGE 1A.
ELSNER RD.

SCALE : 1" = NTS
DATE : / /
DRAWN BY : BEC
CHECKED BY : GB

DLZ ENGINEERS · ARCHITECTS · SCIENTISTS · PLANNERS · SURVEYORS
85 W. ALGONQUIN ROAD, SUITE 220 ARLINGTON HEIGHTS, IL 60005 TEL: (847) 640-0840
