PART OF THE NE 1/4 SECTION 20, T36N, R14E OF THE 3rd PM, THORNTON TOWNSHIP, COOK COUNTY, ILLINOIS.

PARCEL NUMBER	OWNER	TOTAL HOLDING HA – [AC]	PART TAKEN HA – [AC]	REMAINDER HA – [AC]	PREV. DED. HA–[AC]	EASEMENT HA – [AC]	EASEMENT PURPOSE	PERMANENT TAX INDEX NUMBER	PROPERTY ACQUIRED BY
ODE3200TE	CITY OF HARVEY	3.0895 [7.634]				0.0075 [0.019]	CONSTRUCTION	29–20–200–018	
ODE0201	NEW CHRISTIAN VALLEY HOUSING MINISTRY, INC.	3.2784 [8.101]	0.1851 [0.457]	3.0933 [7.644]	0.0184 [0.045]			29–20–200–017	
ODE3201TE	CITY OF HARVEY	3.0933 [7.644]				0.0138 [0.034]	CONSTRUCTION	29–20–200–017	

COORDINATE VALUE

METRIC PROJECT COORDINATES ARE GROUND VALUES AND CAN BE CONVERTED TO GRID VALUES BY MULTIPLYING THE PUBLISHED GROUND COORDINATES BY 0.999988, PROVIDED BY THE ILLINOIS DEPARTMENT OF TRANSPORTATION.

COORDINATE TABLE

DATA POINT NO.	STATION	OFFSET	–N– COORDINATES	–E–
1600	0+853.108	8.868 m R	547,861.7894	357,390.6434
1601	0+853.307	13.864 m R	547,861.8399	357,395.6431
1500	0+868.191	8.205 m R	547,876.8065	357,390.4918
1501	0+868.297	10.526 m R	547,876.8217	357,392.8149
1602	0+868.419	13.200 m R	547,876.8392	357,395.4917
1502	0+889.878	9.407 m R	547,898.3943	357,392.5971
1503	0+890.123	14.088 m R	547,898.4416	357,397.2841
1504	3+019.505	26.489 m R	547,982.4295	357,396.4363
1505	3+035.000	15.249 m R	547,993.8570	357,411.7942
1604	3+105.700	21.263 m R	547,988.7035	357,482.5622
1603	3+105.702	15.263 m R	547,994.7030	357,482.4904
1605	3+128.700	21.268 m R	547,988.9787	357,505.5606
1606	3+128.702	15.268 m R	547,994.9783	357,505.4888
1506	3+174.111	15.277 m R	547,995.5217	357,550.8945

CURVE DATA

CENTERLINE PROPOSED CONSTRUCTION

CURVE NO. 1

Δ = 2°28'13"
D = 3°31'33"
R = 1625 m
L = 70.064 m
T = 35.037 m
E = 0.378 m

PI STA. 0+838.965

PC STA. 0+803.928

PT STA. 0+873.992

LEGEND

TOTAL SHEETS 579 — SHEET NO. 102

SECTION CORNER — QUARTER SECTION CORNER

SECTION LINE
QUARTER SECTION LINE
QUARTER, QUARTER SECTION LINE
PLATTED LOT LINE
PROPERTY (DEED) LINE
APPARENT PROPERTY LINE
CENTERLINE
EXISTING RIGHT OF WAY LINE
PROPOSED RIGHT OF WAY LINE
PROPOSED EASEMENT
EXISTING ACCESS CONTROL LINE
PROPOSED ACCESS CONTROL LINE
123.456m [1.23'] MEASURED DIMENSION METRIC WITH IMPERIAL
123.45' (COMP) [0.00'] COMPUTED DIMENSION METRIC WITH IMPERIAL
RECORD DATA
EXISTING BUILDING

BEARINGS REFERENCED TO THE ILLINOIS STATE PLANE COORDINATE SYSTEM, EAST ZONE, NAD 83, PROVIDED BY THE ILLINOIS DEPARTMENT OF TRANSPORTATION.

● IRON PIPE OR ROD FOUND — ○ SET 5/8" x 30" REBAR
+ CUT CROSS FOUND OR SET — ●PK FOUND PK NAIL — ○PK SET PK NAIL

● T1 T2 T3 THESE STAKES REFERENCE FOUND OR SET MONUMENTATION. SET 5/8 INCH REBAR FLUSH WITH GROUND TO TIE FOUND IRON STAKE. IDENTIFIED BY COLORED PLASTIC CAP AND BEARING SURVEYORS PROFESSIONAL NUMBER.

● BT1 BT2 BT3 THESE STAKES, IN CULTIVATED AREAS, REFERENCE FOUND OR SET MONUMENTATION. BURIED 5\8 INCH REBAR 20 INCHES BELOW GROUND TO TIE FOUND IRON STAKE. IDENTIFIED BY COLORED PLASTIC CAP BEARING SURVEYORS PROFESSIONAL NUMBER.

■ STAKING OF PROPOSED RIGHT OF WAY. SET DIVISION OF HIGHWAYS SURVEY MARKER TO MONUMENT THE POSITION SHOWN. IDENTIFIED BY INSCRIPTION DATA AND SURVEYORS PROFESSIONAL NUMBER.

■ M STAKING OF PROPOSED RIGHT OF WAY IN CULTIVATED AREAS. BURIED 5/8 INCH REBAR 20 INCHES BELOW GROUND TO MARK FUTURE SURVEY MARKER POSITION. IDENTIFIED BY COLORED PLASTIC CAP BEARING SURVEYORS PROFESSIONAL NUMBER.

PERMANENT SURVEY MARKER. IDOT STD. 2135 (TO BE SET BY OTHERS)

□ RIGHT OF WAY STAKING PROPOSED TO BE SET.

STATE OF ILLINOIS }
COUNTY OF WILL } SS

THIS IS TO CERTIFY THAT I, THOMAS E. BAUMGARTNER, AN ILLINOIS PROFESSIONAL LAND SURVEYOR, HAVE SURVEYED THE PLAT OF HIGHWAYS SHOWN HEREON BETWEEN SECTION 20 , TOWNSHIP 36 NORTH, RANGE 14 EAST, AND SECTION , TOWNSHIP NORTH, RANGE EAST OF THE THIRD PRINCIPAL MERIDIAN, COOK COUNTY; THAT THE SURVEY IS TRUE AND COMPLETE AS SHOWN TO THE BEST OF MY KNOWLEDGE AND BELIEF; THAT THE PLAT CORRECTLY REPRESENTS SAID SURVEY; THAT ALL MONUMENTS FOUND AND ESTABLISHED ARE OF PERMANENT QUALITY AND OCCUPY THE POSITIONS SHOWN THEREON AND THAT THE MONUMENTS ARE SUFFICIENT TO ENABLE THE SURVEY TO BE RETRACED. MADE FOR THE DEPARTMENT OF TRANSPORTATION, STATE OF ILLINOIS.

DATED AT LOCKPORT, ILLINOIS THIS 26TH DAY OF MARCH 2002 A.D.

Baird & Company
– LAND SURVEYORS –
AT THE HISTORIC RAILROAD DEPOT
133 WEST THIRTEENTH STREET
LOCKPORT, ILLINOIS 60441

ILLINOIS PROFESSIONAL LAND SURVEYOR NO. 3142
LICENSE EXPIRES 11/30/04

STATE OF ILLINOIS PROFESSIONAL LAND SURVEYOR — THOMAS E. BAUMGARTNER 35-3142 LOCKPORT

STATE OF ILLINOIS }
COUNTY OF COOK } S.S.

THIS IS TO CERTIFY THAT I, COVENTINE FIDIS, AN ILLINOIS PROFESSIONAL LAND SURVEYOR, HAVE REVISED THE PLAT OF HIGHWAYS SHOWN HEREON; THAT SAID PLAT OF HIGHWAYS WAS ORIGINALLY SIGNED AND CERTIFIED ON MARCH 26TH, 2002 BY THOMAS E. BAUMGARTNER, ILLINOIS PROFESSIONAL LAND SURVEYOR NO. 3142. NO CERTIFICATION AS TO PARCEL BOUNDARIES, AS WOULD BE DETERMINED FROM A BOUNDARY SURVEY, ARE MADE OR IMPLIED. MADE FOR THE DEPARTMENT OF TRANSPORTATION, STATE OF ILLINOIS.

DATED AT CHICAGO, ILLINOIS THIS 28TH DAY OF AUGUST, 2006.

COVENTINE FIDIS
ILLINOIS PROFESSIONAL LAND SURVEYOR NO. 2159
LICENSE EXPIRATION DATE 11/30/2006

STATE OF ILLINOIS — COVENTINE FIDIS 35-2159 — CHICAGO, ILL. — PROFESSIONAL LAND SURVEYOR

ASC
AMERICAN SURVEYING CONSULTANTS, P.C.
841 N. GALENA AVE. / DIXON, IL. 61021 / 815-288-6231
8604 W. CATALPA AVE. / CHICAGO, IL. 60656 / 773-444-0800
ILLINOIS PROFESSIONAL DESIGN FIRM NO. 184-003192

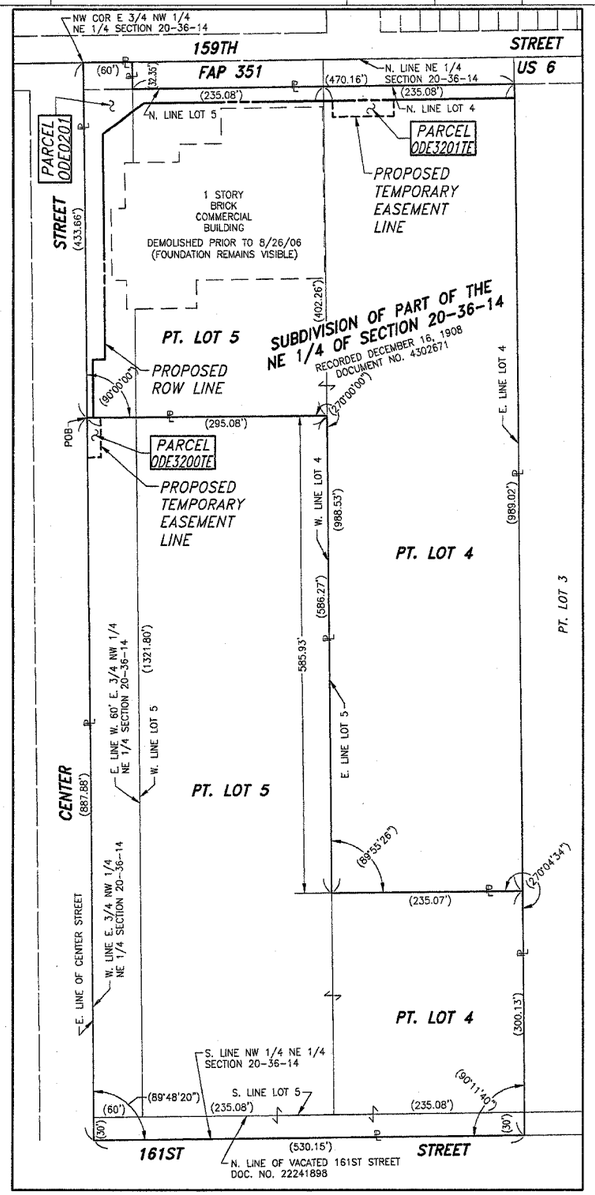

TOTAL HOLDING DETAIL

GRAPHIC SCALE (IN METERS) 20 0 10 20 40 60 80 100

1 : 1000

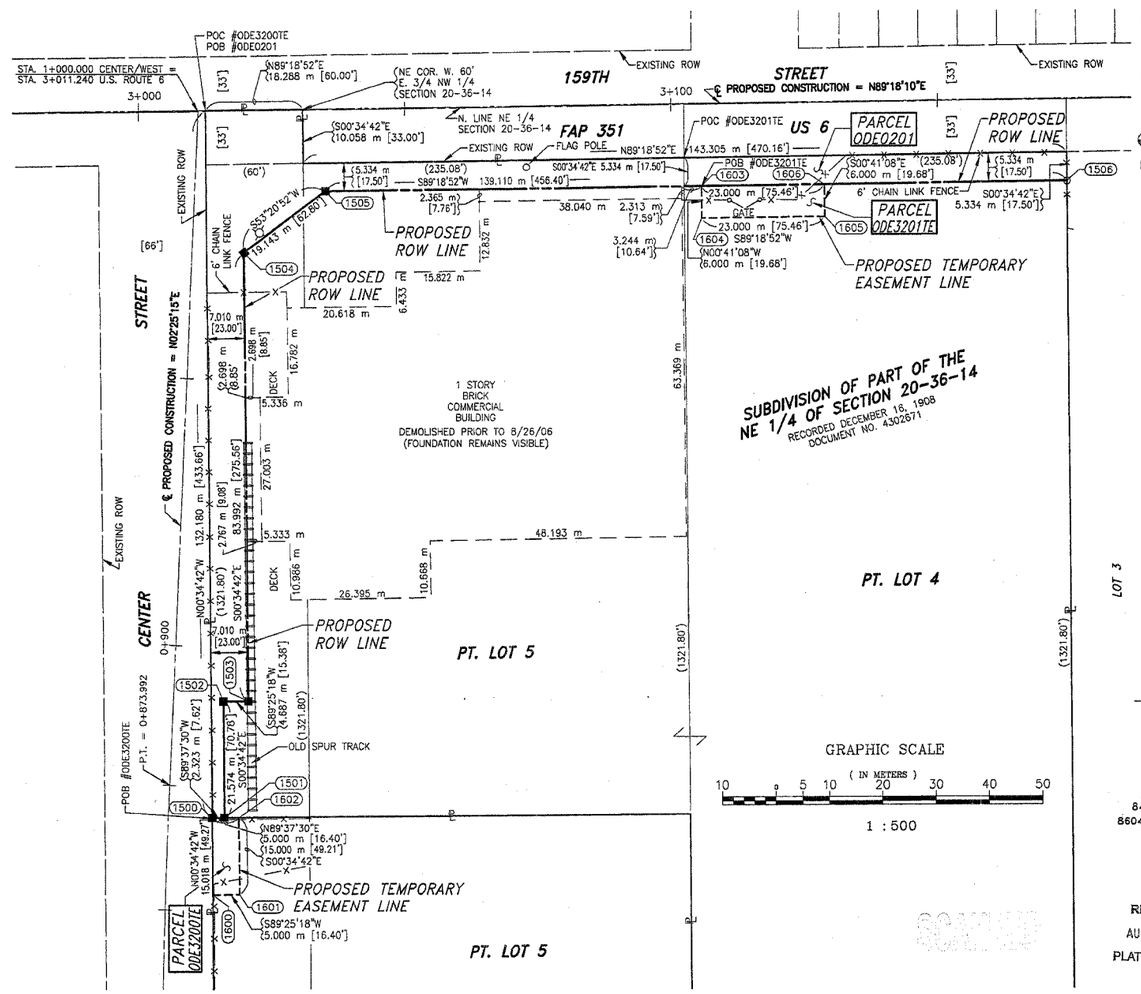

GRAPHIC SCALE (IN METERS) 10 0 5 10 20 30 40 50

1 : 500

RECEIVED AUG 2 9 2006 PLATS & LEGALS

PLAT OF HIGHWAYS
STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION
FAP 351 US 6 (159TH STREET)

SECTION — COOK COUNTY
PROJECT — JOB NO. R-90-011-99
STATION 3+000.000 — TO STATION 3+174.111
SCALE: 1:500 — SHEET C1 OF ___

BUREAU OF LAND ACQUISITION
201 WEST CENTER COURT
SCHAUMBURG, ILLINOIS 60196-1096

JOB # 3378 ODE DWG. # 900-215-C1

A.S.C. REVISION DATE: 08-28-06 — REVISION: NOTED DEMOLISHED BUILDING ON PARCEL ODE0201. — MADE BY: DD
A.S.C. REVISION DATE: 08-23-06 — REVISION: CHANGED OWNERSHIP FOR PARCEL ODE3201TE IN PARCEL TABLE. — MADE BY: DD
A.S.C. REVISION DATE: 05-26-06 — REVISION: ADDED REVISION CERTIFICATE AND SIGNATURE. RENUMBERED PARCELS ODE0200TE AND ODE0201TE TO ODE3200TE AND ODE3201TE. — MADE BY: DD

FAP 351 US 6 (159TH STREET), SECTION , JOB. NO. R-90-011-99.
