F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90/94	*	COOK	247	5
STA.		TO STA.		
FED. ROAD DIST. NO. 1	ILLINOIS	FED. AID PROJECT		
60A63	* (1919.15, 2021-922 PT1 & PT2) R-2			

ID		Task Name
66		EARTH EXCAVATION
67		SUBBASE GRANULAR MATERIAL TYPE B 24"
68		ELECTRICAL DUCTBANKS
69		UNDERDRAINS
70		STABILIZED SUBBASE 6"
71		CONTINUOUSLY REINFORCED PCC PVMT 14"
72		PCC SHOULDERS 14"
73		HANDHOLES
74		CURB AND GUTTER
75		BARRIER WALL
76		SIGN FOUNDATIONS
77		BARRIER WALL TRANSITIONS
78		CONCRETE MEDIAN
79		TOPSOIL PLACEMENT
80		SEEDING
81		BLANKET
82		CONTRACT 62303 47TH TO 31ST STAGE 3
83		EROSION CONTROL
84		PAVEMENT REMOVAL
85		STORM SEWER
86		UNDERDRAINS
87		EARTH EXCAVATION
88		SUBBASE GRANULAR MATERIAL TYPE B 24"
89		STABILIZED SUBBASE 6"
90		CONTINUOUSLY REINFORCED PCC PAVEMENT 14"
91		PCC SHOULDERS 14"
92		BARRIER WALL/GUARDRAIL
93		ELECTRICAL
94		TOPSOIL AND SEEDING
95		FINAL PAVEMENT MARKINGS/SIGNING
96		START STAGE 4: OPEN CONTRACT 62303 & 60A63 TO TRAFFIC
97		STAGE 4 WORK USING DAILY LANE CLOSURES
98		BARRIER WALL
99		RUMBLE STRIPS
100		CONTRACT 62303 & 60A63 COMPLETE
101		PUNCHLIST
102		CONTRACT 60A63
103		START CONTRACT 60A63 PRESTAGE
104		ELECTRICAL COORDINATION
105		EROSION CONTROL
106		FORMED CONCRETE REPAIRS
107		FABRICATE & DELIVER & ERECT OVERHEAD SIGN STRUCTURES
108		CONTRACT 60A63 69TH ST RETAINING WALL
109		ELECTRICAL DEMOLITION BY CITY
110		STRUCTURE EXCAVATION
111		CONCRETE REMOVAL
112		REINFORCING STEEL
113		CONCRETE SUPERSTRUCTURE
114		CHAIN LINK FENCE
115		INSTALL LIGHTING BY CITY
116		CONTRACT 60A63 3423+00 TO 3449+00 (Stage 1)
117		PAVEMENT REMOVAL
118		EARTH RETENTION SYSTEMS
119		STORM SEWERS
120		EARTH EXCAVATION
121		SUBBASE GRANULAR MATERIAL TYPE B 24"
122		ELECTRICAL DUCTBANK AND HANDHOLES
123		UNDERDRAINS
124		STABILIZED SUBBASE 6"
125		CONTINUOUSLY REINFORCED PCC PVMT 14"
126		PCC SHOULDERS 14"
127		CURB AND GUTTER
128		GUARDRAIL
129		BARRIER WALL
130		SIGN FOUNDATIONS

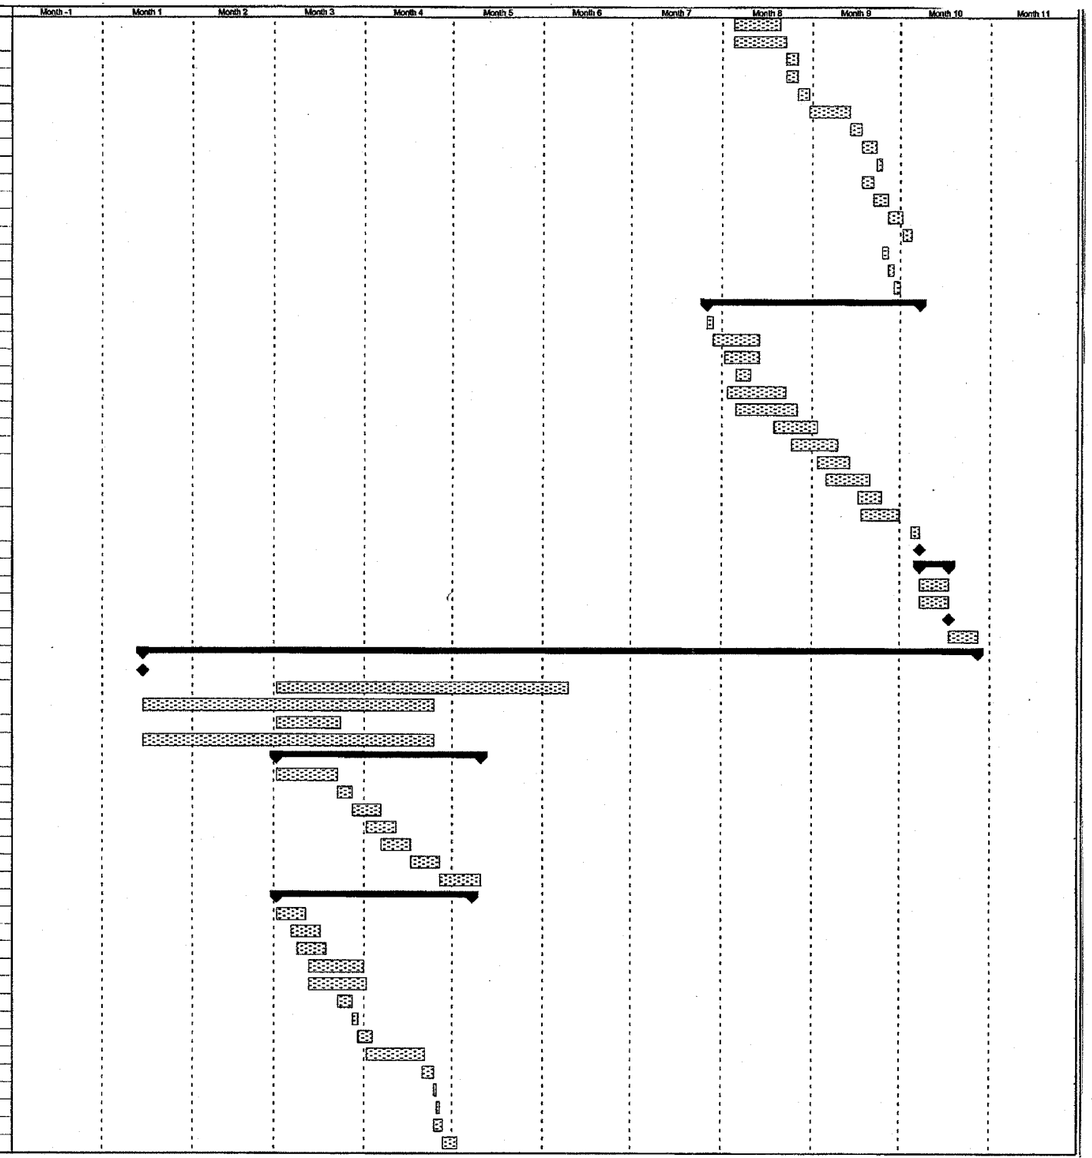

Project: DANRYAN19&19A REV3
Date: Fri 6/2/06

Task — Progress — Summary — Rolled Up Split — Rolled Up Progress — Project Summary — Deadline
Split — Milestone — Rolled Up Task — Rolled Up Milestone — External Tasks — External Milestone

Page 2

CS-2

REVISIONS NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 90/94 (DAN RYAN EXPRESSWAY)
63RD STREET TO GARFIELD BLVD (SB LOCAL LANES)

SUGGESTED SEQUENCE OF OPERATION

SCALE: NONE — DRAWN BY: NJH
DATE: June 9, 2006 — CHECKED BY: RMG

6/5/2006 11:12 PM

CTE | AECOM

p:\p60468\civil\18-cntrs 18 & 19\sht\cntr 190\schedules\cs190022e.sht
