



SEQUENCE OF CONSTRUCTION PLAN NOTES - PHASE 2

1. THE CONTRACTOR SHALL PLACE ALL BARRICADES AS SHOWN PRIOR TO STARTING WORK ON THIS PHASE OR AS DIRECTED BY THE ENGINEER.
2. MARK THE AIR OPERATIONS AREA (A.O.A.) WITH LATHE AND RIBBON AS SHOWN BY THE CONSTRUCTION SETBACK LINE OR AS DIRECTED BY THE ENGINEER.
3. THE AIRPORT WILL REQUIRE THREE (3) CALENDAR DAYS NOTICE FROM THE CONTRACTOR PRIOR TO INITIATING THIS PHASE TO COORDINATE WITH THE TENANTS.
4. THE CONTRACTOR MAY WORK IN THE PHASE 2 WORK AREA CONCURRENTLY WITH PHASE 1 PROVIDED THAT IT DOES NOT IMPACT THE PROGRESS OF THE PHASE 1 WORK ON A TEMPORARY BASIS AS APPROVED BY THE AIRPORT MANAGER.
5. FOR ALL PHASES OF WORK, THE CONTRACTOR SHALL RETURN THE EQUIPMENT TO THE STAGING & STORAGE AREA UNLESS PERMISSION IS GIVEN BY THE AIRPORT TO DO OTHERWISE.

CLOSED PAVEMENT AREAS

- TXY A FROM TXY F TO TXY C.
- TXY A FROM TXY G2 TO TXY E
- TXY C FROM TXY A TO RWY 9/27

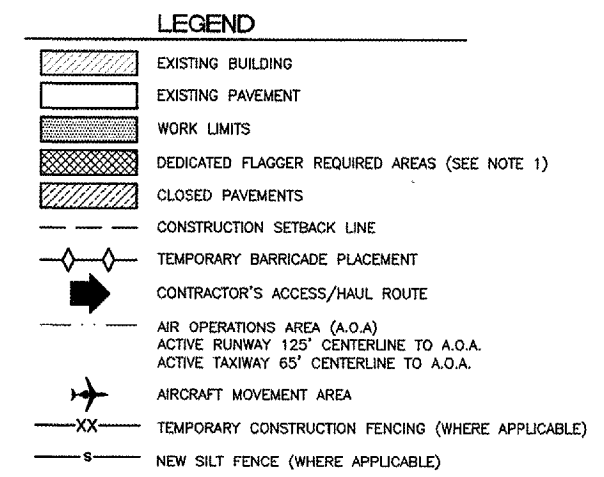

NOTES


1. CONTRACTOR SHALL HAVE DEDICATED FLAGGER ONSITE WHEN WORKING WITHIN TAXIWAY F, TAXIWAY A, TAXIWAY C, AND TAXIWAY G2 A.O.A. AND YIELD TO ALL ONCOMING AIRCRAFT (COST SHALL BE INCIDENTAL TO CONTRACT).
2. ALL WORK INCLUDING RUNWAY LIGHTING AND AIRFIELD PAVEMENT MARKINGS FOR RUNWAY 9/27 SHALL BE IN PLACE AND OPERATIONAL PRIOR TO OPENING RUNWAY 9/27 TO AIR TRAFFIC.
3. CONTRACTOR SHALL EXPEDITE WORK ALONG TAXIWAY CHARLIE. THE COST FOR THE EXPEDITED WORK SHALL BE INCLUDED IN THE CONTRACT.
4. CONTRACTOR SHALL VERIFY AT THE END OF EACH WORKING DAY THAT THE LIGHTS ADJACENT TO OPERATIONAL PAVEMENTS FOR TAXIWAY ALPHA ARE OPERATIONAL AT THE END OF EACH DAY.

IL. CONTRACT: **LA036**
 IL. LETTING ITEM: **2A**
 IL. PROJECT: **IGQ-3565**
 A.I.P. PROJECT: **3-17-0121-825**

SURVEY BOOK # BOOK #

REVISIONS		
NUMBER	BY	DATE

VILLAGE OF LANSING
LANSING MUNICIPAL AIRPORT
LANSING, ILLINOIS
REHABILITATE AIRFIELD LIGHTING SYSTEM
SEQUENCE OF CONSTRUCTION
PER AC150/5370-2E (LATEST EDITION)
PHASE 2



DESIGN BY:	LAO
DRAWN BY:	JWD
CHECKED BY:	DKP
APPROVED BY:	----
DATE:	02 MARCH 2007
JOB No:	06297-02

DATE: Thursday, March 08, 2007 9:00:31 PM
 FILE: K:\lansing\0629702 Rehab 9-27_Elect\Draw\Sheets\06_conseq02.dwg
 UPDATE BY: Jason Dove
 LAYOUT: Layout 1
 XREF: DWG: boairt.dwg
 to: bmp-base.dwg
 bmp-base.dwg
 bmp-base.dwg
