| F.A.I. RTE. | SECTION | COUNTY | TOTAL SHEETS | SHEET NO. |
|---|---|---|---|---|
| 94 | * | COOK | 907 | 6 |
| STA. 1200+00.00 | TO STA. 1365+00 | | | |
| FED. ROAD DIST. NO. | ILLINOIS | FED. AID PROJECT | | |

* (1516.1, 1717 & 1818) R-9

62695

CONTRACT 62695

| ID | Task Name | | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | PUBLIC NOTIFICATION (2 weeks) | | 0 days | Wed 8/17/05 | Wed 8/17/05 |
| 2 | traffic control and protection | | 238 days | Thu 9/1/05 | Mon 7/31/06 |
| 3 | BEGIN SB I-94 STAGE 1 | | 0 days | Thu 9/1/05 | Thu 9/1/05 |
| 4 | CLOSE RAMPS @ 71st Ent./75th Ex., 87th Ex., Wentworth Ex. | | 0 days | Thu 9/1/05 | Thu 9/1/05 |
| 5 | temporary pvmt markings | | 1 day | Thu 9/1/05 | Thu 9/1/05 |
| 6 | temporary concrete barrier | | 5 days | Fri 9/2/05 | Thu 9/8/05 |
| 7 | drill & set soldier piles (walls 33,AIS3,68) | (3 crews) | 6 days | Wed 9/7/05 | Wed 9/14/05 |
| 8 | timber lagging | (3 crews) | 3 days | Wed 9/14/05 | Fri 9/16/05 |
| 9 | structure excavation | | 2 days | Wed 9/14/05 | Thu 9/15/05 |
| 10 | reinf. bars epoxy ctd. | (3 crews) | 4 days | Fri 9/16/05 | Wed 9/21/05 |
| 11 | concrete structures | (3 crews) | 3 days | Fri 9/23/05 | Tue 9/27/05 |
| 12 | curb & gutter removal | (3 crews) | 3 days | Tue 9/6/05 | Thu 9/8/05 |
| 13 | pavement removal | (3 crews) | 2 days | Tue 9/6/05 | Wed 9/7/05 |
| 14 | paved shoulder removal | | 2 days | Tue 9/6/05 | Wed 9/7/05 |
| 15 | earth excavation | | 12 days | Tue 9/13/05 | Wed 9/28/05 |
| 16 | storm sewer (jacked in place) | | 5 days | Thu 9/8/05 | Wed 9/14/05 |
| 17 | storm sewer 36" to 48" | | 7 days | Fri 9/16/05 | Mon 9/26/05 |
| 18 | storm sewer 12" to 30" | (3 crews) | 10 days | Fri 9/16/05 | Thu 9/29/05 |
| 19 | manholes | | 7 days | Fri 9/16/05 | Mon 9/26/05 |
| 20 | catch basins | (3 crews) | 11 days | Fri 9/16/05 | Fri 9/30/05 |
| 21 | CTA NOTIFICATION FOR SINGLE TRACKING (42 days) | | 42 days | Thu 9/1/05 | Fri 10/28/05 |
| 22 | ovrhd./cant. sign foundations | | 4 days | Mon 10/31/05 | Thu 11/3/05 |
| 23 | subbase gran. mat. 24" | (2 crews) | 4 days | Mon 10/3/05 | Thu 10/6/05 |
| 24 | stabilized subbase 4" | | 2 days | Fri 10/7/05 | Mon 10/10/05 |
| 25 | pcc pvmt. 11" (jointed) | | 5 days | Tue 10/11/05 | Mon 10/17/05 |
| 26 | pcc shoulders 11" | | 4 days | Tue 10/18/05 | Fri 10/21/05 |
| 27 | temporary pavement | (2 crews) | 3 days | Tue 10/18/05 | Thu 10/20/05 |
| 28 | subbase gran. mat. 6" | | 1 day | Mon 10/3/05 | Mon 10/3/05 |
| 29 | pcc base course | | 4 days | Tue 10/4/05 | Fri 10/7/05 |
| 30 | concrete curb and gutter | (2 crews) | 6 days | Mon 10/24/05 | Mon 10/31/05 |
| 31 | conc. median surf. | (2 crews) | 3 days | Tue 11/1/05 | Thu 11/3/05 |
| 32 | pavement markings | | 2 days | Fri 11/4/05 | Mon 11/7/05 |
| 33 | topsoil furnish & place | (2 crews) | 3 days | Tue 11/8/05 | Thu 11/10/05 |
| 34 | seeding class 2A | | 1 day | Fri 11/11/05 | Fri 11/11/05 |
| 35 | erosion control blanket | (2 crews) | 6 days | Mon 11/14/05 | Mon 11/21/05 |
| 36 | OPEN RAMPS @ 71st Ent./75th Ex., 87th Ex., Wentworth Ex. | | 0 days | Mon 11/21/05 | Mon 11/21/05 |
| 37 | STAGE 1 COMPLETION DATE | | 0 days | Tue 11/22/05 | Tue 11/22/05 |
| 38 | | | | | |
| 39 | | | | | |
| 40 | | | | | |
| 41 | | | | | |
| 42 | | | | | |
| 43 | | | | | |
| 44 | | | | | |

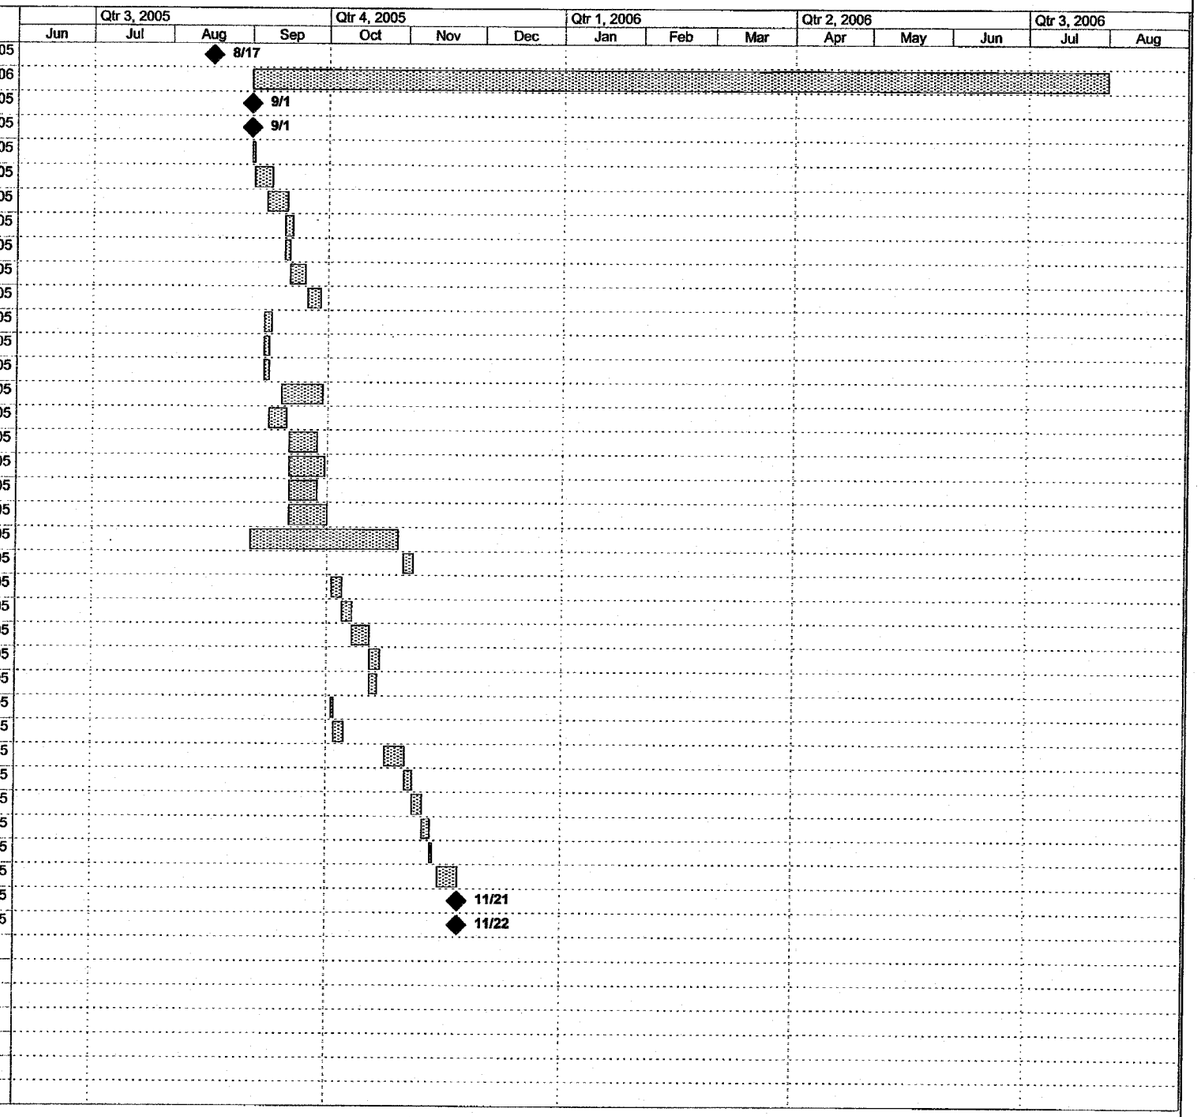


Project:17B Construction Schedule
Date: Tue 3/29/05

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline



TY·LIN INTERNATIONAL

| REVISIONS | |
|---|---|
| NAME | DATE |
| | |

ILLINOIS DEPARTMENT OF TRANSPORTATION

F.A.I. 94 (DAN RYAN EXPRESSWAY)

SUGGESTED CONSTRUCTION SEQUENCE
SHEET 1 OF 4

SCALE: NONE DRAWN BY: JPA
DATE: MARCH 25, 2005 CHECKED BY: MAG

03/30/2005 11:33:21 AM
