


SAUK TRAIL – STAGE 4a NOTES

1. SHIFT VEHICLES TO THE NORTH SIDE OF SAUK TRAIL.
2. INSTALL STORM SEWER. DURING THE INSTALLATION OF PIPE 144 AND PIPE 154, IT WILL BE REQUIRED FOR CONTRACTOR TO CROSS OVER LIVE LANES. CONTRACTOR TO FOLLOW HIGHWAY STANDARD 701501-06.
3. CONTRACTOR TO INSTALL TEMPORARY PAVEMENT ON SAUK TRAIL MEDIAN.
4. CONTRACTOR TO INSTALL TEMPORARY STORM SEWER PIPING.

** REMOVAL OF EPOXY STRIPING SHALL ONLY BE REMOVED BY WATER BLASTING PER RECURRING SPECIAL PROVISION AND PAID FOR AS PAVEMENT MARKING REMOVAL.

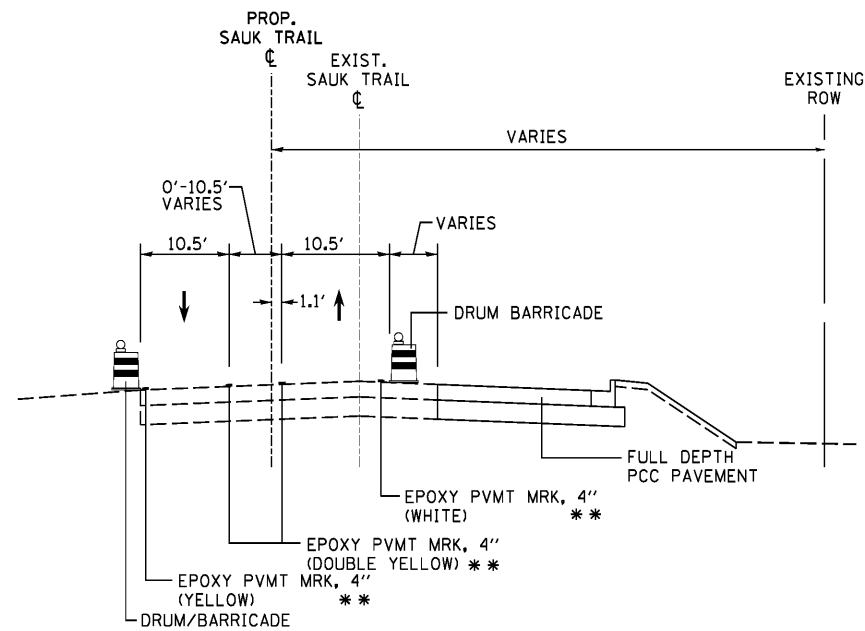


STAGE 4A TYPICAL SECTION SAUK TRAIL

STA 384+50.00


SAUK TRAIL – STAGE 4b NOTES

1. SHIFT VEHICLES TO THE SOUTH SIDE OF SAUK TRAIL.
2. CONTRACTOR TO INSTALL REMAINING STORM SEWER.
3. REMOVE TEMPORARY PAVEMENT IN SAUK TRAIL MEDIAN AND INSTALL CURB AND GUTTER.

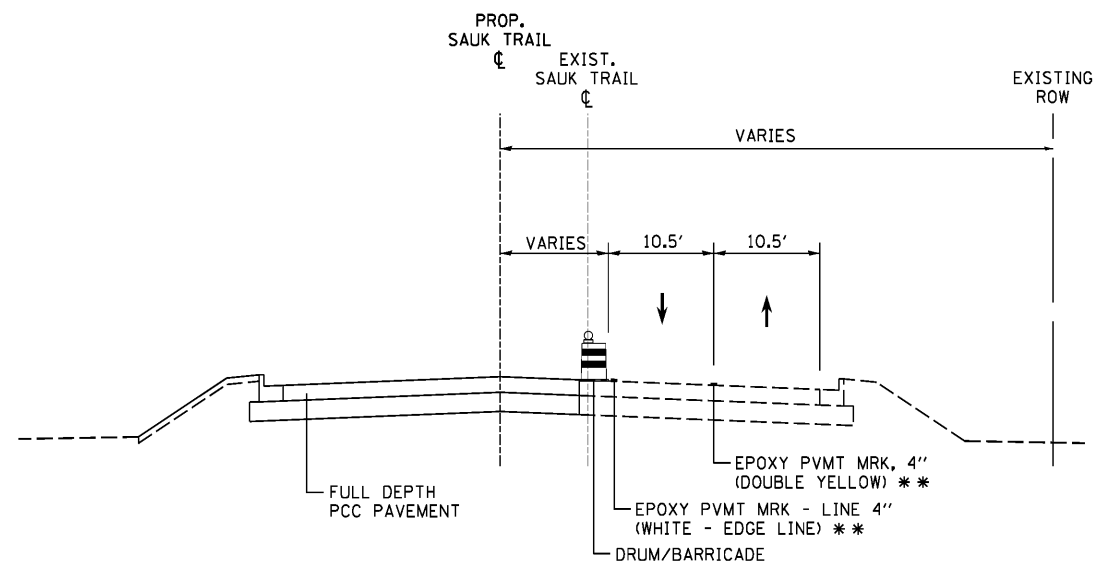

STAGE 4B TYPICAL SECTION SAUK TRAIL

STA 384+50.00



V3 Companies
7325 Janes Avenue
Woodridge, IL 60517
630.724.9200 phone
630.724.9202 fax
www.v3co.com

USER NAME = dsherman
DESIGNED - DSS
DRAWN - DRP
CHECKED - VJD
DATE - 01/31/2014

REVISED -
REVISED -
REVISED -
REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

MAINTENANCE OF TRAFFIC – SAUK TRAIL – STAGE 4A & 4B
TYPICAL SECTIONS

SCALE: N/A SHEET NO. 6 OF 6 SHEETS

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
353	11-Y-A	COOK	354	45
CONTRACT NO. 60R19				
ILLINOIS FED. AID PROJECT				
