



STATE OF ILLINOIS  
DEPARTMENT OF TRANSPORTATION

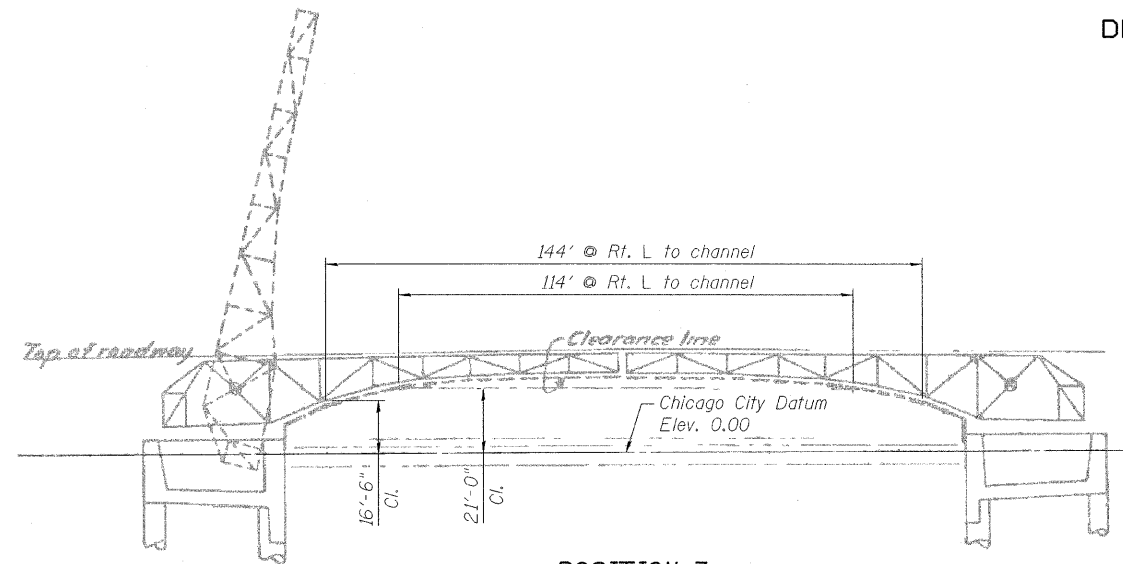

**POSITION 3**

SW leaf open & SE leaf closed


Stage I: Westbound bridge operable. SW leaf may be operable, SE leaf must be operable for open position for navigation. Rehabilitation of the SW leaf may be performed in this position.

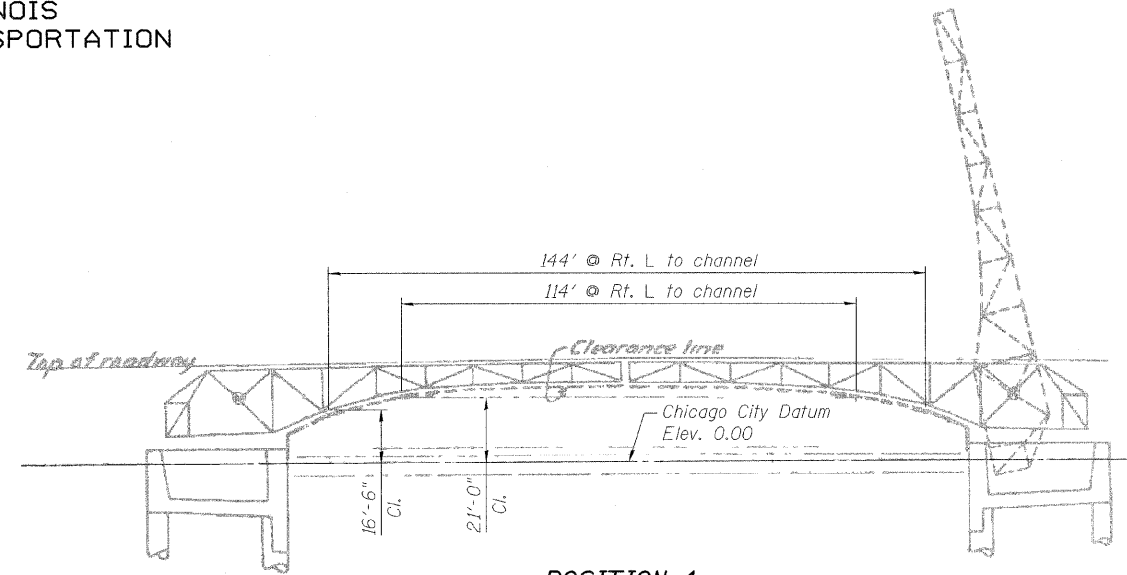


**POSITION 4**

SE leaf open & SW leaf closed

Stage I: Westbound bridge operable. SE leaf may be operable, SW leaf must be operable for open position for navigation. Rehabilitation of the SE leaf may be performed in this position.

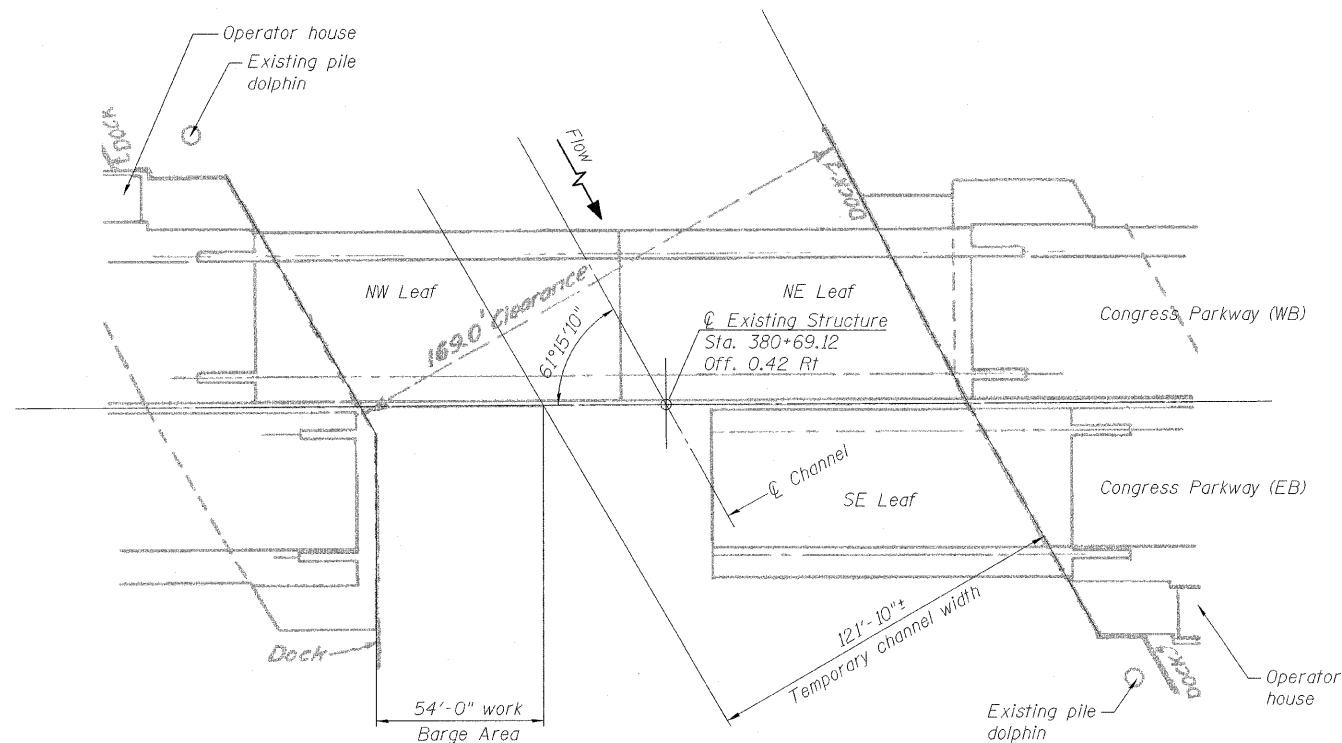

**PLAN**

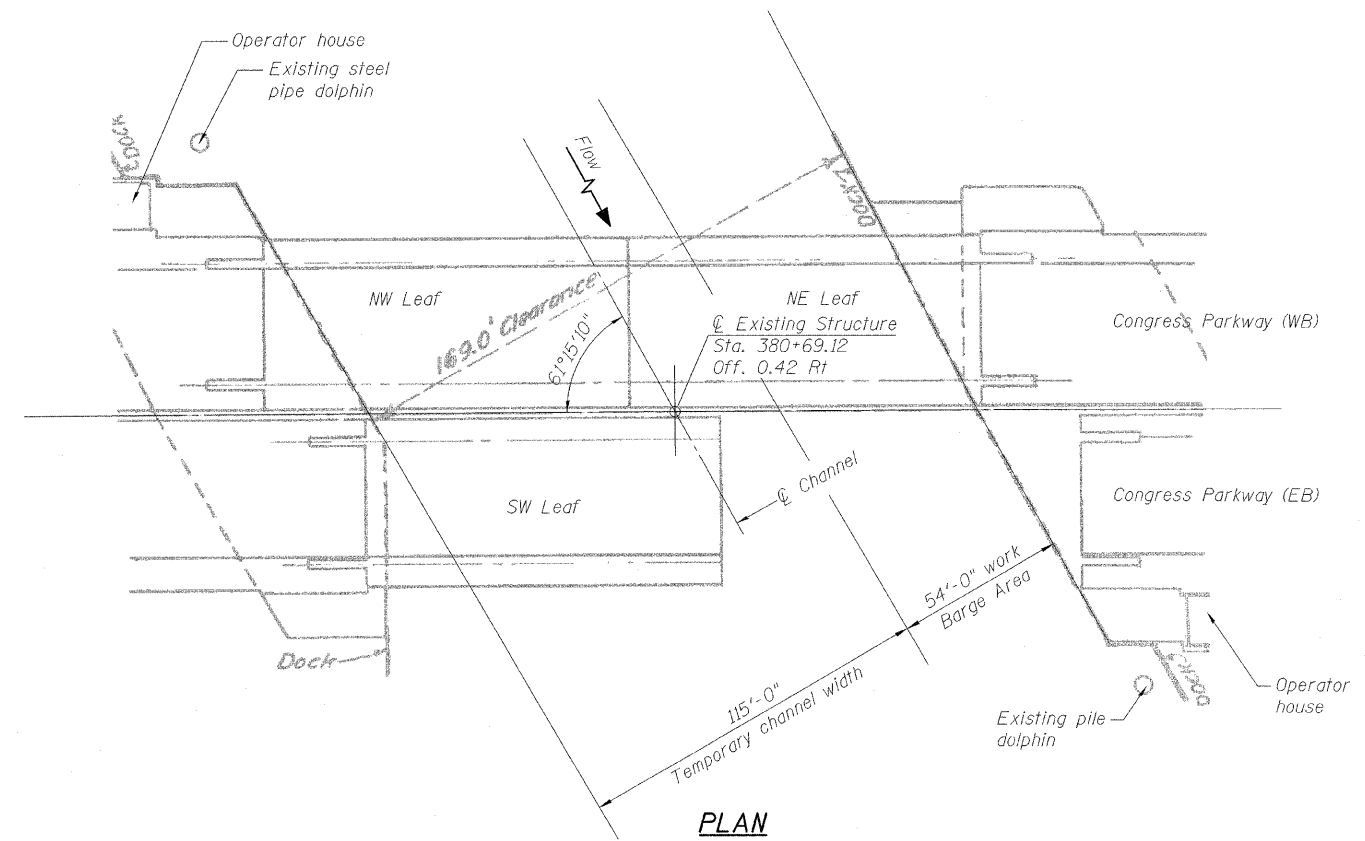

**PLAN**

DESIGNED	A. HAMMAD
CHECKED	J. GRAINAWI
DRAWN	D. C. PATEL
CHECKED	A. HAMMAD

**PB Americas, Inc.**  
230 WEST MONROE STREET,  
SUITE 900  
CHICAGO, IL. 60606

SHEET NO. 4 163 SHEETS	F.A.P RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	389	2424.2B-R	COOK	398	85
CONTRACT NO. 60D61					
FED. ROAD DIST. NO. 7 ILLINOIS FED. AID PROJECT					

**STAGE CONSTRUCTION DETAILS  
STRUCTURE NO. 016-2445**

T:\1684\Structural\Cadd\Pre-final\EB\_Plans\0162445-60D61-STG-004.dgn  
07-MAY-2009
