



ROUTE NO.	SECTION NO.	TOTAL SHEET
F.A.U. 8578 F.A.U. 8878	03-00019-1 1-FP	98
FED. ROAD DIST. NO.	COUNTY	PROJECT
	PEORIA	M-5093
	ILLINOIS	
CONTRACT NO. 89369		

CONSTRUCTION STAGING (SUGGESTED)

THE CONTRACTOR WILL PERFORM ALL PHASE WORK BY CLOSING ONE LANE OF TRAFFIC WHEN NECESSARY IN ACCORDANCE WITH ILLINOIS DEPARTMENT OF TRANSPORTATION STANDARDS. DURING NON-WORKING HOURS BOTH LANES OF TRAFFIC WILL REMAIN OPEN. ACCESS WILL BE MAINTAINED TO ALL BUSINESSES AND SCHOOLS EXCEPT AS DIRECTED BY THE ENGINEER. DRAINAGE AND UTILITIES WILL BE MAINTAINED AT ALL TIMES EXCEPT TO MAKE NEW CONNECTIONS

PHASE 5 (HATCHED AREA)
 CONSTRUCT EASTBOUND LANE OF PFEIFFER (ON WEST LEG OF PFEIFFER)
 CONSTRUCT SOUTHBOUND AIRPORT ROAD SOUTH OF THE PFEIFFER INTERSECTION
 EASTBOUND PFEIFFER TRAFFIC WILL SHIFT TO OLD WESTBOUND TRAFFIC LANE
 SOUTHBOUND AIRPORT ROAD TRAFFIC WILL BE SHIFTED EAST IF NECESSARY

TEMPORARY PAVEMENT MARKING QUANTITY THIS PHASE - 360 METER
 COST TO REMOVE ANY EXISTING OR TEMPORARY PAVEMENT MARKINGS WILL BE CONSIDERED INCLUDED IN THE CONTRACT UNIT COST FOR TEMPORARY PAVEMENT MARKINGS

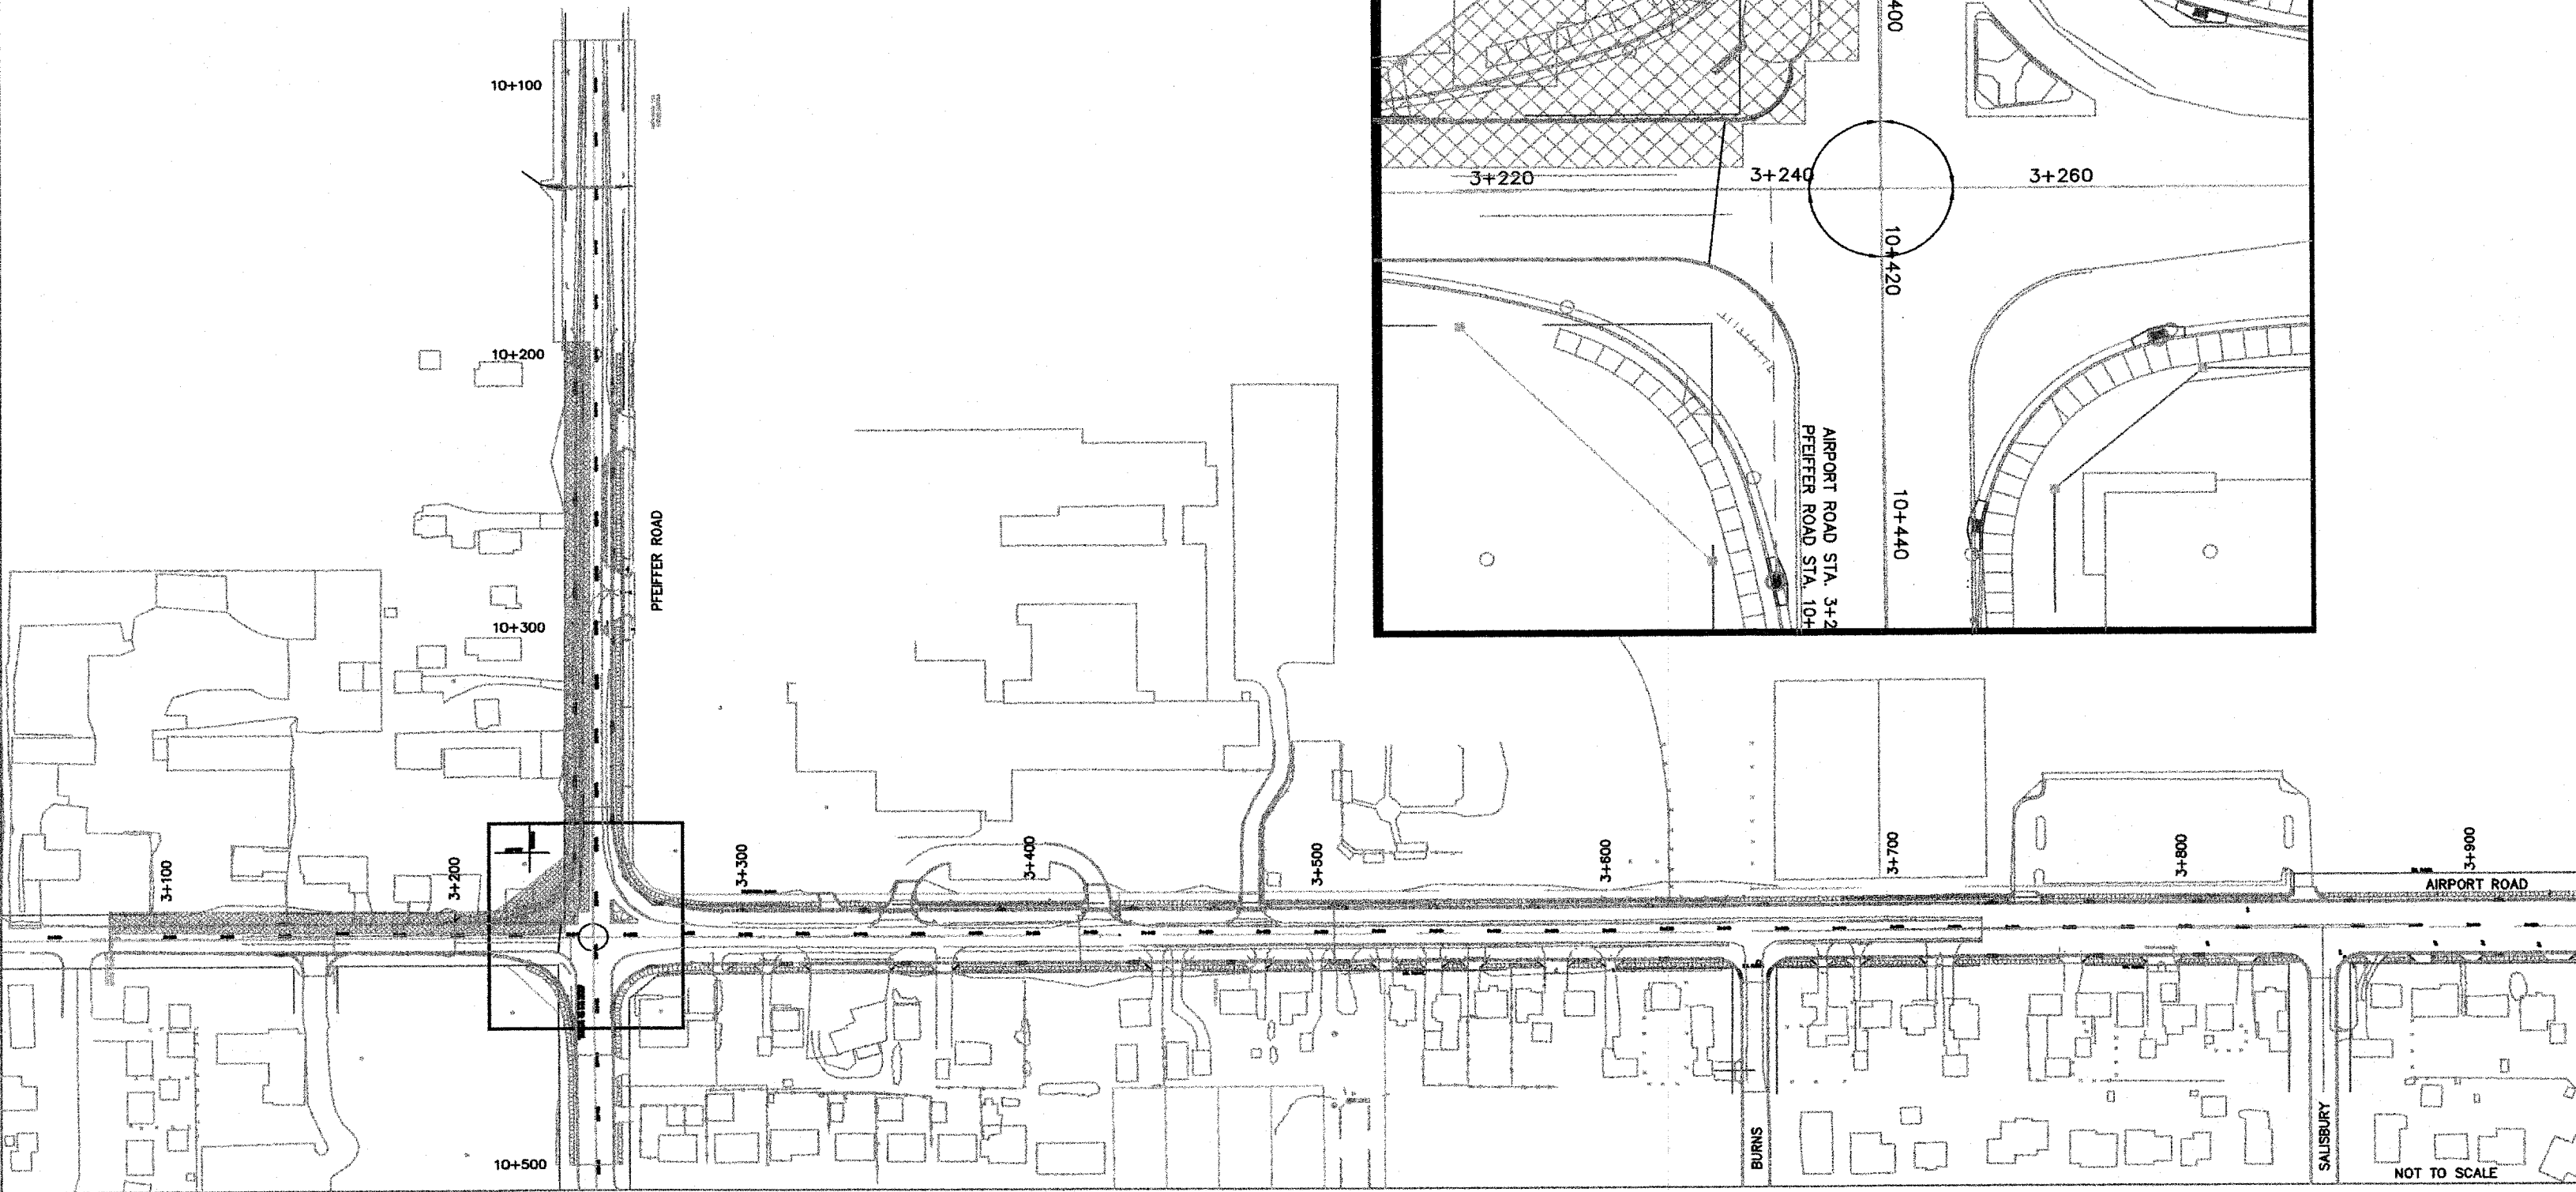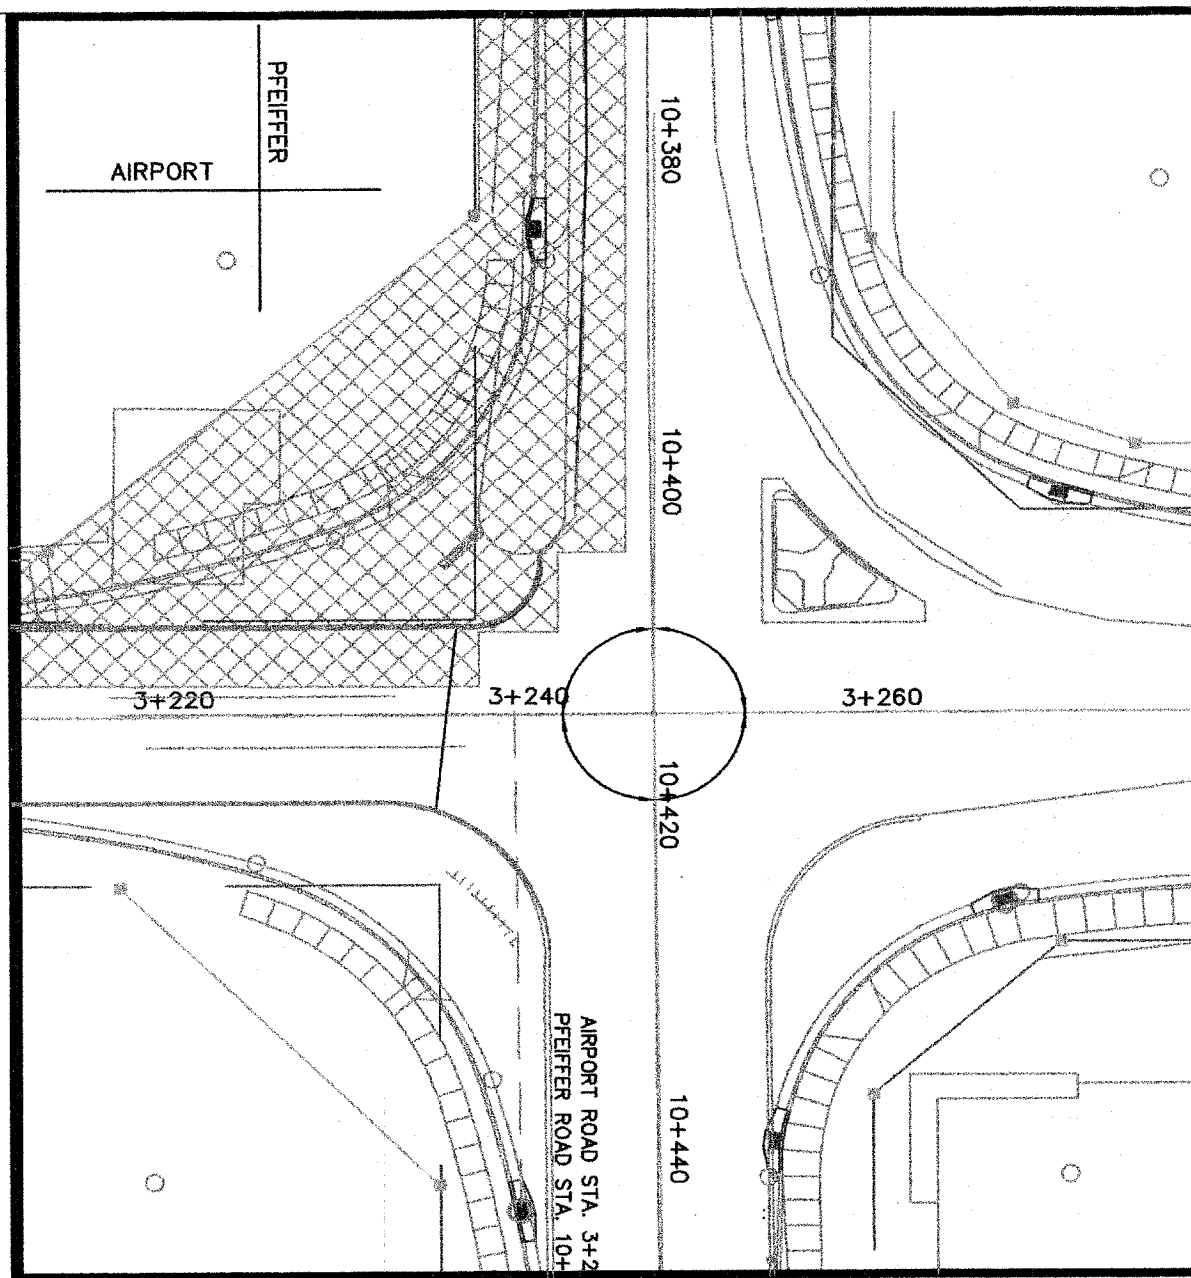

NOT TO SCALE
