

<u>TRAFFIC</u>


N.B. & S.B. I-55 WILL USE EXISTING LANES.

WEST FRONTAGE ROAD WILL BE CLOSED TO TRAFFIC.

CONSTRUCTION

- 1. REPAIR FRONTAGE ROAD BRIDGE AND RESURFACE WEST FRONTAGE ROAD.
- 2. INSTALL GUARDRAIL ON WEST FRONTAGE ROAD BRIDGE.
- 3. UTILIZING TRAFFIC CONTROL AND PROTECTION STANDARD 701401 CONSTRUCT TEMPORARY CROSSOVERS TO/FROM SB I-55 TO/FROM WEST FRONTAGE ROAD.
- 4. MILL AND RESURFACE I-55 LANES AT THE APPROACH AND DEPARTURE ENDS OF CROSSOVERS.
- 5. STAGE II SOUTHBOUND I-55 TRAFFIC CONTROL AS SHOWN ON SHEET 3 AND 4 OF 8 AND MOVE SOUTHBOUND I-55 TRAFFIC TO THE TEMPORARY CROSS OVER.
- 6. UTILIZING TRAFFIC CONTROL AND PROTECTION STANDARD 701401 FOR NORTH BOUND TRAFFIC AND THE SOUTHBOUND CROSSOVER CONSTRUCT TEMPORARY CROSSOVERS TO/FROM NB I-55 TO/FROM SB I-55.
- INSTALL TEMPORARY CONCRETE BARRIER ON SOUTH END OF EXISTING SB I-55 BRIDGE. OVERLAP MINIMUM 2' INSIDE BRIDGE PARAPET.
- 8. INSTALL STAGE II NORTHBOUND TRAFFIC CONTROL AS SHOWN ON SHEET 3 AND 4 OF 8 AND MOVE NORTHBOUND I-55 TRAFFIC TO THE TEMPORARY CROSSOVER.
- 9. INSTALL FRONTAGE ROAD CLOSED SIGN AT THE NEXT OVERPASS SOUTH OF THE FRONTAGE ROAD CLOSURE. PLACEMENT TO BE AS DIRECTED BY THE ENGINEER.

701400 701401

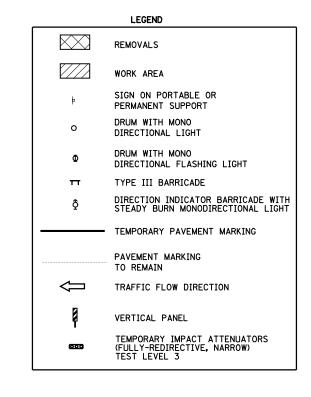

L							
I	FILE NAME =	USER NAME = laughlinrl	DESIGNED	-	REVISED -		
I	:\pw_work\PWIDOT\LAUGHLINRL\dØ110282\StageConstruction.dgn		DRAWN	-	REVISED -		
I		PLOT SCALE = 100.00000 '/ IN.	CHECKED	-	REVISED -		
l		PLOT DATE = Dec-03-2008 07:33:37AM	DATE	-	REVISED -		

STATE OI	FILLINOIS
DEPARTMENT OF	TRANSPORTATION

STAGE I CONSTRUCTION				F.A. RTE.	SEC.	TION	COUNTY	TOTAL SHEETS	SHEET NO.
					68-4B-1	& 111BR	MONTGOMERY	145	22
					* FAI 55 & FAS 1769		CONTRACT	NO. 7	72A63
SCALE:	SHEET NO. 2 OF 8 SHEETS	STA. 1076+00	TO STA. 1086+00	FED. RO	AD DIST. NO.	ILLINOIS FED. A	ID PROJECT		
