


STAGE 3 - PEACE ROAD
 SWITCH TRAFFIC SIGNAL OPERATIONS AT PLEASANT STREET TO THE TEMPORARY TRAFFIC SIGNALS. SHIFT TRAFFIC ONTO THE EAST HALF OF PEACE ROAD AND THE TEMPORARY PAVEMENT CONSTRUCTED IN STAGE 2. MAINTAIN ONE THROUGH LANE IN EACH DIRECTION NEAR THE BRIDGE AND ONE THROUGH LANE AND ONE LEFT TURN LANE IN EACH DIRECTION AT PLEASANT STREET. MAINTAIN ONE RIGHT TURN LANE ON SOUTHBOUND PEACE ROAD AT PLEASANT STREET. MAINTAIN TWO-WAY TRAFFIC WITH FLAGGERS DURING CONSTRUCTION OF THE STORM SEWER LATERAL AT STATION 138+00 (SEE ITEM 3 BELOW). MAINTAIN TWO-WAY TRAFFIC AT ALL OTHER TIMES OF STAGE 3 CONSTRUCTION.

1. CONSTRUCT WIDENING, STORM SEWER, HMA PAVEMENT PATCHING, GUARDRAIL AND CURB AND GUTTER ON THE WEST HALF OF PEACE ROAD.
2. CONSTRUCT HMA BINDER ON THE WEST HALF OF PEACE ROAD. THE HMA BINDER SHALL MATCH THE ADJACENT EXISTING PAVEMENT ELEVATION ALONG THE ENTIRE LENGTH OF THE IMPROVEMENTS.
3. CONSTRUCT THE STORM SEWER LATERAL AT STATION 138+00 TO THE CENTERLINE OF PEACE ROAD AND INSTALL HMA PAVEMENT PATCHING OVER TRENCH. MAINTAIN TWO-WAY TRAFFIC WITH FLAGGERS DURING INSTALLATION OF THE LATERAL AND PATCH. THIS WORK SHALL BE RESTRICTED TO ONE DAYTIME LANE CLOSURE WITH FLAGGERS BETWEEN THE HOURS OF 9AM AND 3PM INCLUDING THE HMA PAVEMENT PATCH. FAILURE TO OPEN THE ROAD BY 3 PM WILL RESULT IN A TRAFFIC CONTROL DEFICIENCY DEDUCTION IN ACCORDANCE WITH SECTION 105.03 (B) OF THE STANDARD SPECIFICATIONS. PEACE ROAD WILL REMAIN OPEN TO TWO-WAY TRAFFIC AT ALL OTHER TIMES OF STAGE 3 CONSTRUCTION.
4. CONSTRUCT TEMPORARY PAVEMENT ON THE SOUTHWEST SHOULDER OF PEACE ROAD AT THE BRIDGE TO BE USED AS A TEMPORARY RUNAROUND DURING STAGE 4.

LEGEND

- DIRECTION OF TRAFFIC
- TYPE II BARRICADES OR DRUMS
- EXISTING ELEMENTS
- PROPOSED ELEMENTS (PRIOR STAGES)
- PROPOSED ELEMENTS (CURRENT STAGE)
- EXISTING PAVEMENT MARKINGS
- TEMPORARY PAVEMENT MARKINGS
- REMOVAL

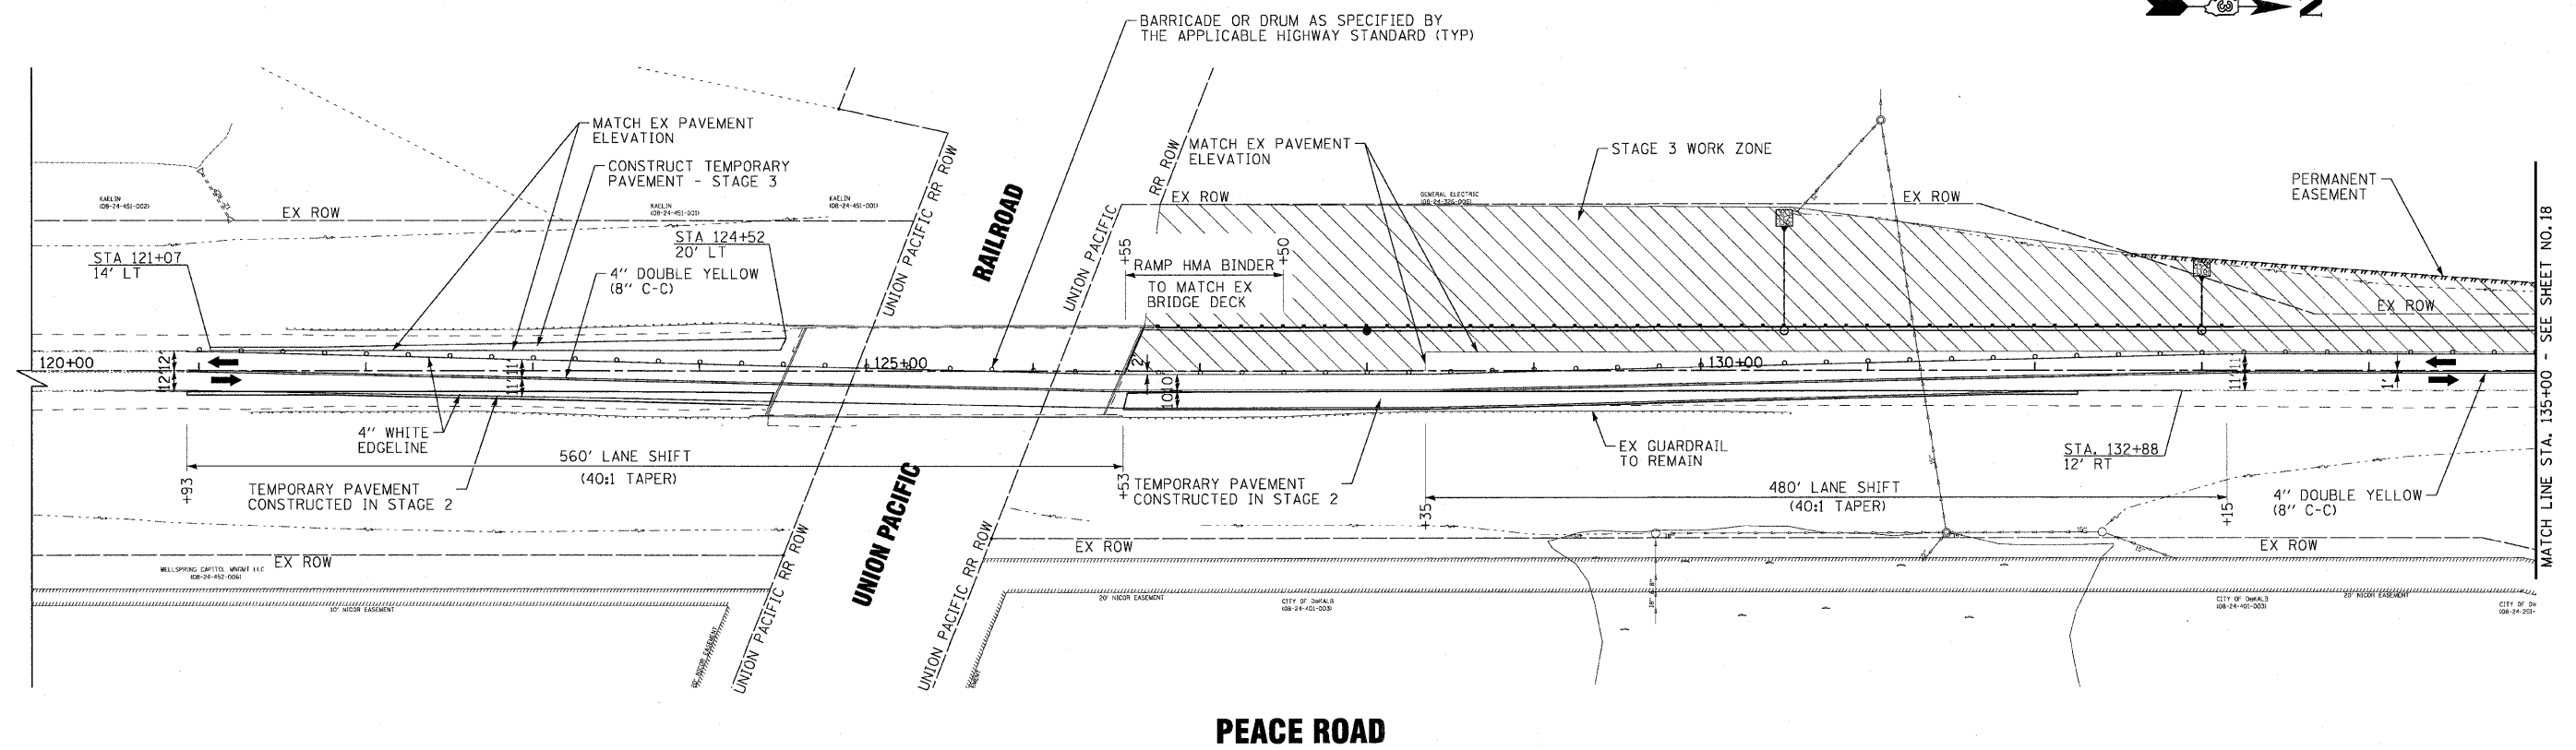

COPYRIGHT © 2008 BY BAXTER & WOODMAN, INC.
 ALL RIGHTS RESERVED.
 LICENSE NO. 184-00181 - EXPIRES 4/30/2011
 8/4/2010 10:24:43 AM
 PROJECT: 081068-MOT-STG3.dgn
 DRAWN: UKB
 CHECKED: RWL
 DATE: 05-03-2010
 FILE NAME: 081068-MOT-STG3.dgn



DESIGNED - DJS	REVISED - 08-4-2010 IDOT REVIEW
DRAWN - UKB	REVISED -
CHECKED - RWL	REVISED -
DATE - 05-03-2010	FILE NAME - 081068-MOT-STG3.dgn

**CITY OF DeKALB, ILLINOIS
 PEACE ROAD
 IMPROVEMENTS**

**SUGGESTED MAINTENANCE OF TRAFFIC - STAGE 3
 PEACE ROAD**

SCALE: 1"=50'
 STA. 120+00 TO STA. 135+00

F.A.U. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
5369	06-00172-00-WR	DeKALB	64	18
				CONTRACT NO. 87465
FED. ROAD DIST. NO. 3 ILLINOIS FED. AID PROJECT M-5017 (043)				
