LETTING ITEM NO. 09A IDOT LETTING APRIL 26. 2024

WAUKEGAN PORT DISTRICT WAUKEGAN, LAKE COUNTY, ILLINOIS

INDEX TO SHEETS

- 1. COVER SHEET
- 2. SUMMARY OF QUANTITIES
- 3. SITE PLAN / PROJECT CONTROL
- 4. CONSTRUCTION ACTIVITY PLAN
- 5 **CONSTRUCTION ACTIVITY PLAN NOTES - 1** CONSTRUCTION ACTIVITY PLAN NOTES - 2 6
- 7. EXISTING CONDITIONS AND PROPOSED REMOVALS 1
- **EXISTING CONDITIONS AND PROPOSED REMOVALS 2**
- EXISTING CONDITIONS AND PROPOSED REMOVALS 3 9.
- 10. FENCING PLAN 1
- 11. FENCING PLAN 2
- 12. FENCING PLAN 3 AND ELECTRICAL PLAN
- 13. LANDSCAPING AND EROSION CONTROL PLAN 1
- 14. LANDSCAPING AND EROSION CONTROL PLAN 2
- 15. LANDSCAPING AND EROSION CONTROL PLAN 3 MARKING/SIGNAGE/GRADING PLAN - AVIATION DR
- 16. STORMWATER POLLUTION PREVENTION PLAN
- 17. STORMWATER POLLUTION PREVENTION DETAILS
- 18. FENCING DETAILS 1
- 19. FENCING DETAILS 2
- 20. CANTILEVER GATE DETAILS
- 21. ELECTRIC GATE DETAILS
- 22. MISCELLANEOUS DETAILS 1
- 23. MISCELLANEOUS DETAILS 2


CONSTRUCTION PLANS FOR WAUKEGAN NATIONAL AIRPORT

CONSTRUCT PERIMETER FENCING - PHASE 5 (NORTHWEST AREA)

ILLINOIS PROJECT: UGN-4848 S.B.G. PROJECT: 3-17-SBGP-XX

JANUARY 12, 2024

LAKE MICHIGAN

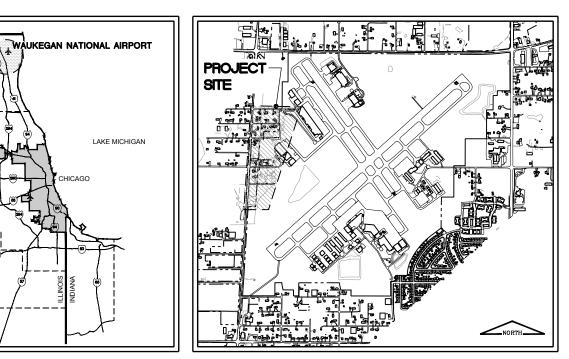

WAUKEGAN NATIONAL AIRPORT TOWNSHIP: 46 NORTH RANGE: 12 EAST SECTION: 31 AND 32 COUNTY: LAKE TOWNSHIP: BENTON **DESIGN INFORMATION** DESIGN AIRCRAFT APPROACH CATEGORY C DESIGN AIRCRAFT GROUP III (GULFSTREAM 450) JULIE 81 what's below JOINT UTILITY LOCATING Call before you dig INFORMATION FOR EXCAVATORS www.illinois1call.com THE LOCATION, SIZE AND TYPE OF MATERIAL OF EXISTING UNDERGROUND UTILITIES INDICATED ON THE PLANS IS NOT REPRESENTED AS BEING ACCURATE DEFICIENT OR COMPLETE IT SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO DETERMINE ACTUAL LOCATIONS OF ALL SUCH FACILITIES, INCLUDING SERVICE CONNECTIONS TO UNDERGROUND UTILITIES. PRIOR TO CONSTRUCTION, THE CONTRACTOR SHALL NOTIFY UTILITY COMPANIES OF HIS OPERATIONAL PLANS OBTAIN FROM RESPECTIVE UTILITY COMPANIES DETAILED INFORMATION AND ASSISTANCE RELATIVE TO THE LOCATION OF THEIR FACILITIES AND THE WORKING SCHEDULE OF THE COMPANIES FOR REMOVAL OR ADJUSTMENT WHERE BEOLIJBED IN THE EVENT AN UNEXPECTED UTILITY INTERFERENCE IS ENCOUNTERED DURING CONSTRUCTION, THE CONTRACTOR SHALL IMMEDIATELY NOTIFY THE UTILITY COMPANY OF JURISDICTION AND THE ONE-CALL NOTICE SYSTEM. THE ENGINEER

CALL J.U.L.I.E. BEFORE

EXCAVATING AT 811

SHALL ALSO BE IMMEDIATELY NOTIFIED. ANY SUCH UTILITY OR SERVICES SHALL BE RESTORED TO SERVICE AT ONCE AND PAID FOR BY THE CONTRACTOR AT NO ADDITIONAL COST TO THE CONTRACT

CALL J.U.L.I.E. FOR UTILITY INFORMATION AT 811.



WISCONSIN

LAKE

ILL INOIS

PROJECT

LOCATION

SITE PLAN

WA076 TOTAL SHEETS = 23






SUMMARY OF CONTRACT QUANTITIES

	ITEM	DESCRIPTION	UNIT	TOTAL ESTIMATED QUANTITY	TOTAL RECORD QUANTITY	ESTIMATED QUANTITY F/S/L	RECORD QUANTITY F/S/L	ESTIMATED QUANTITY LOCAL ONLY	RECORD QUANTITY LOCAL ONLY
в	BASE BID								
*	AR108404	1/C #4 600V UG CABLE	FOOT	535	5.	535			
*	AR108408	1/C #8 600V UG CABLE	FOOT	175		175			
*	AR108410	1/C #10 600V UG CABLE	FOOT	1,090		50		1,040	
*	AR110011	1" DIRECTIONAL BORE	FOOT	265		45		220	
*	AR110117	1-1/2" PVC DUCT, DIRECT BURY	FOOT	655		135		520	
*	AR110201	1" PVC DUCT, DIRECT BURY	FOOT	530		80		450	
	AR150510	ENGINEER'S FIELD OFFICE	L SUM	1		1			
	AR150520	MOBILIZATION	L SUM	1		1			
	AR151420	CLEARING TREES 0-2.5' BUTT. DIA.	EACH	8		8			
	AR151450	CLEARING AND GRUBBING	ACRE	1.41		1.41			
	AR152410	UNCLASSIFIED EXCAVATION	CU YD	232		200		32	
	AR156510	SILTFENCE	FOOT	200		200			
	AR156520	INLET PROTECTION	EACH	2		2			
	AR156530	TEMPORARY SEEDING	ACRE	1.41		1.41			
	AR156531	EROSION CONTROL BLANKET	SQ YD	350		350			
	AR161900	REMOVE CLASS C FENCE	FOOT	2,163		2,163			
	AR162216	CLASS E MANUAL SLIDE GATE - 16'	EACH	1		1			
	AR162220	CLASS E MANUAL SLIDE GATE - 20'	EACH	1		1			
	AR162228	CLASS E MANUAL SLIDE GATE - 28'	EACH	1		1			
	AR162401	VINYL FENCE UPGRADE	FOOT	130				130	
	AR162402	VINYL GATE UPGRADE	EACH	4	- 			4	
	AR162612	CLASS E GATE 12'	EACH	2		2			
	AR162810	CLASS E FENCE 10' W/ 2' BURY	FOOT	1,985		1,985			
	AR162900	REMOVE CLASS E FENCE	FOOT	740		740			
	AR162908	REMOVE ELECTRIC GATE	EACH	3		3			
F	AR163000	TEMPORARY CONSTRUCTION FENCE	FOOT	525		525			
	AR208515	POROUS GRANULAR EMBANKMENT	CU YD	105		85		20	
	AR208606	6" AGGREGATE BASE COURSE	SQ YD	320		265		55	
	AR401613	BIT. SURF. CSE METHOD I, SUPERPAVE	TON	28		23		5	
F	AR401900	REMOVE BITUMINOUS PAVEMENT	SQ YD	385		385			
F	AR403613	BIT. BASE CSE METHOD I, SUPERPAVE	TON	47		39		8	
	AR602510	BITUMINOUS PRIME COAT	GALLON	97		80		17	
F	AR603510	BITUMINOUS TACK COAT	GALLON	33		27		6	
F	AR620520	PAVEMENT MARKING-WATERBORNE	SQ FT	120		120			
\vdash	AR620900	PAVEMENT MARKING REMOVAL	SQ FT	40		40			
\vdash	AR754410	COMB CONCRETE CURB & GUTTER	FOOT	50		50		1	
*	AR800017	LIGHT POLE WITH LED LUMANAIRE	EACH	3				3	
*	AR800020	1-1/2" DIRECTIONAL BORE	FOOT	180		40		140	
\vdash	AR800173	WILDLIFE DETERRENT BARRIER - PAD	SQ FT	160		160			
*		FIBER OPTIC CABLE	FOOT	630				630	
*	AR800186	ELECTRIC GATE OPERATOR	EACH	1		1		200	
*	AR800188	GATE ACCESS CONTROL SYSTEM	LSUM	1				1	
\vdash	AR901510	SEEDING	ACRE	1.78		1.78			
\vdash	AR905530	TOPSOLING	SQ YD	370		370			
\vdash	AR908514	LIGHT-DUTY HYDRAULIC MULCH	ACRE	1.47		1.47			
\vdash	AR900314 AR910200	ROADWAY SIGN	EACH	7		4		3	
L	AR910200 AR910900	REMOVE ROADWAY LIGHT POLE	EACH	1		4		5	


Image: model model (model model) Image: model mode		SUMMARY OF CONTRACT QUANTITIES									ITEM: UGN-4	•••
	ITEM		UNIT	ESTIMATED	RECORD	QUANTITY	QUAN TITY	QUANTITY	QUAN TITY			
			FOOT	125				125		R	EVISIO	ONS
										NUMBER	BY	DATE
	AS110201											
Restance <	AS151450	CLEARING AND GRUBBING	ACRE	0.05		0.05					-	
	AS156530	TEMPORARYSEEDING	ACRE	0.05		0.05						
	AS161900	REMOVE CLASS C FENCE	FOOT	187		187						
	AS162905	REMOVE GATE	EACH	2		2						
Single Below Felcence Carbonance C	AS162664	CLASS E MANUAL SLIDE GATE - 24'	EACH	1		1						2
1. Second 1. Second	AS162810	CLASS E FENCE 10' W/ 2' BURY	FOOT	307		307						
Return terms to a function of the local to function of the local to function of the local 	AS162908	REMOVE ELECTRIC GATE	EACH	1		1					22 00/12	
Bandbark Control curtury monocol curves Control curves Contro curves Contro curves C	AS800186	ELECTRIC GATE OPERATOR	EACH	1				1				
	AS901510	SEEDING	ACRE	0.05		0.05						
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000	AS908514	LIGHT-DUTY HYDRAULIC MULCH	ACRE	0.05		0.05						S
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000								1		1		Щ
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000										2		E
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000	AT151420		_							ш		E
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000										AS		Z
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000										L I		٦L
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000										5 -		ğ
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000			_							<u>ن</u> م م		ш.
THEMPORANCONSTRUCTION FERCE FOOT 385 1000 1000000000000000000000000000000000000											a	ō
Stressel I. LIGHT-DUTY-HYDRAULIC MULCH ACRE 0.28 </td <td></td> <td>Щ I</td> <td>Š</td>											Щ I	Š
Stressel I. LIGHT-DUTY-HYDRAULIC MULCH ACRE 0.28 </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>-</td> <td></td> <td>ĪĀIĒ</td> <td>A I</td> <td>Ŕ</td>								-		ĪĀIĒ	A I	Ŕ
UNITE ASTERNISK DENOTES SPECIALTY ITEM NOTE:												≤
UNITE ASTERNISK DENOTES SPECIALTY ITEM NOTE:	711500011		Monte	0.20		0.20				I Ľ Ľ Ľ	S	Σ
UNITE ASTERNISK DENOTES SPECIALTY ITEM NOTE:	DITIVE ALTI	ERNATE NO. 3								I A A F	3	Σ
UNITE ASTERNISK DENOTES SPECIALTY ITEM NOTE:	AU151450	CLEARING AND GRUBBING	ACRE	0.42		0.42					Ξ	ີ
UNITE ASTERNISK DENOTES SPECIALTY ITEM NOTE:	AU156530	Contract States Fire & Description and States States								AAA	2	~
UNITE ASTERNISK DENOTES SPECIALTY ITEM NOTE:	AU161900	REMOVE CLASS C FENCE	FOOT	820		820				L AL	9	S
DIRECTIONAL DRILLING CONTINGENCY PLAN Rectional DRILLING CONTINGENCY PLAN IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHALLS STOP DRILLING IMEDITARY AND WORK TO CONTAIN THE DRILLING MUD. THE BASE HETHOD DC CONTAINMENT IS WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAIN THE CONTRACTOR WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAIN THE ADD TO CONTAINTED THE WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAINTED FRACE WICE AD ADDRESS THE ADDRESS AND DRIVE THE ADDRESS AND WORKNO KOAK ALL BE REQUIRED TO ADRESS AND WARK TO CONTAIN HER BASE IN LIGS CONTAINT THE FAC OUT CONTAINABILITY WARKS TO SUPPORTED THE CONTRACTOR SHALL BE SUPPORTED TO CONTAIN THE WARKS WARKS AND ALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO TO REALL WARKS WA	AU162810	CLASS E FENCE 10' W/ 2' BURY	FOOT	805		805				<u>7</u> > L	٤	Ĥ
DIRECTIONAL DRILLING CONTINGENCY PLAN Rectional DRILLING CONTINGENCY PLAN IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHALLS STOP DRILLING IMEDITARY AND WORK TO CONTAIN THE DRILLING MUD. THE BASE HETHOD DC CONTAINMENT IS WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAIN THE CONTRACTOR WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAIN THE ADD TO CONTAINTED THE WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAINTED FRACE WICE AD ADDRESS THE ADDRESS AND DRIVE THE ADDRESS AND WORKNO KOAK ALL BE REQUIRED TO ADRESS AND WARK TO CONTAIN HER BASE IN LIGS CONTAINT THE FAC OUT CONTAINABILITY WARKS TO SUPPORTED THE CONTRACTOR SHALL BE SUPPORTED TO CONTAIN THE WARKS WARKS AND ALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO TO REALL WARKS WA	AU163000	TEMPORARY CONSTRUCTION FENCE	FOOT	640		640				15 5		H
DIRECTIONAL DRILLING CONTINGENCY PLAN Rectional DRILLING CONTINGENCY PLAN IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHALLS STOP DRILLING IMEDITARY AND WORK TO CONTAIN THE DRILLING MUD. THE BASE HETHOD DC CONTAINMENT IS WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAIN THE CONTRACTOR WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAIN THE ADD TO CONTAINTED THE WHEN WORKNO KOAK WARK ALL BE SUPPORTED TO CONTAINTED FRACE WICE AD ADDRESS THE ADDRESS AND DRIVE THE ADDRESS AND WORKNO KOAK ALL BE REQUIRED TO ADRESS AND WARK TO CONTAIN HER BASE IN LIGS CONTAINT THE FAC OUT CONTAINABILITY WARKS TO SUPPORTED THE CONTRACTOR SHALL BE SUPPORTED TO CONTAIN THE WARKS WARKS AND ALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO CONTAIN THE FAC OUT CONTAINABILITY WARKS HALL BE REQUIRED TO TO REALL WARKS WA	AU901510	SEEDING	ACRE	0.42		0.42				RU VA		Ξ
NOTE: ASTERISK DENOTES SPECIALTY ITEM MINING CONTINUES AND RECORD THE SOURCE ADDRESS AND POOLSE AND RECORD THE SOURCE POIL AND R	AU908514	LIGHT-DUTY HYDRAULIC MULCH	ACRE	0.42		0.42						S
 IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHALL STOP DRILLING IMEDITALY AND WORK TO CONTAIN THE DRILLING MUTE DO CONTAININENT IS SHALL BE APPROVED BY THE ARRONT AND THE RESIDENT ENGINEER. I. AT LEAST ONE VACUUM TRUCK MUST BE ONSITE DURING ALL DRILLING OPERATIONS AND AT LEAST ONE ADDITIONAL VACUUM TRUCK SHALL BE READILY AVAILABLE OR ON STAND BY AT A NABBEN DY AT A NABBEN DY CARTS ON ADDITIONAL VACUUM TRUCK SHALL BE READILY AVAILABLE OR ON STAND PAT A DATE AREA DY THE ARRONT AND THE RESIDENT CURTAIN OR CONTRACTOR SHALL BE REQUIRED TO ONAVE AT LEAST ONE ADDITIONAL VACUUM TRUCK SHALL BE READILY AVAILABLE OR ON STAND PAT A DATE AREA DY CARTS ON A TRUCK ON COORDINATE REMEDIATION. CONTRACTOR SHALL BE REQUIRED TO PROVIDE VERIFICATIONS OF ADDEQUATE PROVIDED TO THE SWA READ TO CONTAIN THE FRAC OUT. CONTAINED ANNONCE POLYMERE TO CONTAINED THE FRAC OUT. CONTAINED ANNONCE POLYMERE TO CONTAINED THE FRAC OUT. CONTAINED ANNONCE POLYMERE TO CONTAINE THE CONTINGENCY PLAN FOR APPROVAL BY RE & SMC. CONTRACTOR SHALL BE REQUIRED TO PROVIDE VERIFICATIONS OF ADEQUATE PROCURED THE FIRST IS USED. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A WEEKLY REPORT TO THE SHALL BE REQUIRED TO UPDATE THE CONTINUE POLYMER TO THE SWAC AND THE ARRONT. CONTRACTOR SHALL BE REQUIRED TO DE SUMMARIZED IN THE WEEKLY REPORT TO A SHALL BE REQUIRED TO THE SWAC AND THE ARRONT. CONTRACTOR SHALL BE REQUIRED TO THE SWAC AND THE ARRONT. CONTRACTOR. CONTRACTOR SHALL BE REQUIRED TO THE SWAC AND THE ARRONT. CONTRACTOR. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD SCIENT TO THE SHALL BE REQUIRED TO THE SWAC AND THE ARRONT. CONTRACTOR SHALL BE REQUIRED TO THE SWAC AND THE ARRONT. CONTRACTOR SHALL BE REQUIRED TO THE SWAC AND THE ARRONT. C										0		NDEX
 AND WORK TO CONTAIN THE DRILLING MUD. THE BEST METHOD OF CONTAINMENT IS WITH OR PARABET STARTING TO ADD THE RESTORT TO DOTATION TO CONTAINABLE SUBJECTION TO ADD THE RESIDENT ENGINEER. WHEN WORKING NEAR WETLANDS OR OPEN WATER, THE USE OF A TURBIDITY CURTAIN OR CONTAINABLE OR ON STADBE VIA A LARGE TO AND STABLE SEAD OF (1) FULL TIME PERSON TO WALK THE DRILLING ROUTE AND DEAD OF A A CONTAINABLE OR ON STADBE VIA A LARGE TO AND A SAPEROPRIATE. CONTRACTOR SHALL BE REQUIRED TO ONTAIN THE FRAC OUT. CONTAINABLE OR ON STADBE TO TRACTAR SHALL BE REQUIRED TO PROVIDE VERIFICATIONS OF ADEQUATE TO WALK THE DRILLING ROUTE AND DEAD AFTER A VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONTINGENCY PLAN FOR APPROVAL BY RE & SMC. CONTRACTOR SHALL BE REQUIRED TO PROVIDE VERIFICATIONS OF ADEQUATE PROCEED IT THE FIRST IS USED. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A WEEKLY BERORT TO THE AT ADDITIONAL POLYMER WILL BE REQUIRED TO PROVIDE VERIFICATIONS OF ADEQUATE PROCEED IT THE INFORMATION REQUIREMENTS CONTRACTOR SHALL BE REQUIRED TO PROVIDE A WEEKLY BERORT TO THE AT ADDITIONAL POLYMER WILL BE REQUIRED TO PROVIDE VERIFICATIONS OF ADEQUATE PROCEED IT THE INFORMATION REQUIREMENTS CONTRACTOR SHALL BE REQUIRED TO PROVIDE A WEEKLY BERORT TO THE AND THE SMC AND THE AND APPROVED THE MARK ADDRESS, AND PHONE NUMBER OF THE ANALOUND OR STATILLY AND APPROVED AND AND ADDRESS AND PHONE NUMBER OF THE AND ACTION THE SMC AND THE AND THE SMC AND THE AND ACTION THE SMC AND THE AND ADDRESS AND PHONE NUMBER OF THE ANALOUND OR STATILES TO REACH AND AND AND ADDRESS AND PHONE NUMBER OF THE ANALOUND OR STATILES TO REACH AND THE AND A												-
 APPROVAL BY RE & SMC. APPROVAL BY RE & SMC. APPROVAL BY RE & SMC. A THE CONTRACTOR SHALL PROVIDE THE NAME, ADDRESS, AND PHONE NUMBER OF THE ONSITE DRILLING. CONTRACTOR SHALL PROVIDE THE NAME, ADDRESS, AND PHONE NUMBER OF TRIOR TO DRILLING. CONTRACTOR SHALL PROVIDE DIVENTS SHALL BE PROVIDED BY THE CONTRACTOR. CONTRACTOR SHALL SAFETY DATA SHEETS (MSDS) FOR DRILLING MUD CONSTITUENTS SHALL BE PROVIDED BY THE CONTRACTOR. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC AND THE ARIPORT. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC AND THE SINGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONATION DRILING DUIL DIRECTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONATION DRILLING DIRECTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONATION. 		DIRECTIONAL DRILLING CONTINGENCY PLAN			DIRECTIONAL DE	RILLING MINIMUM O	PERATIONAL REQU	IREMENTS				_
 THE ONSITE DRILLING COMPANY REPRESENTATIVE TO THE SMC AND THE AIRPORT PRIOR TO DRILLING. S. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLING MUD CONSTITUENTS SHALL BE PROVIDED BY THE CONTRACTOR. S. THE NAME, ADDRESS AND PHONE NUMBER OF THE ANIONIC POLYMER VENDOR SHALL BE PROVIDED TO THE SMC AND THE AIRPORT. C. CATALOG CUT SHEETS FOR EACH RECOMMENDED POLYMER WITH DIRECTIONS FOR USE AND ANY LIMITATIONS WILL BE REQUIRED TO BE PROVIDED BY THE CONTRACTOR. S. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH I LIKLY PROBLEM LOCATIONS AND THE PROVOSED METHODS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS NO NOT OCCUR OR ARE PROPERLY CONTAINED. S. CONTRACTOR SHALL BE REQUIRED TO DROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH I LIKLY PROBLEM LOCATIONS AND LOCATIONS AND LORATIONS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS ON ONT OCCUR OR ARE PROPERLY CONTAINED. S. CONTRACTOR SHALL BE REQUIRED TO DROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH I LIKLY PROBLEM LOCATIONS AND LORATIONS OF DIRECTIONAL DRILLING. S. CONTRACTOR SHALL BE REQUIRED TO DROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKLY PROBLEM LOCATIONS AND LORATIONS OF DIRECTIONAL DRILLING. S. CONTRACTOR SHALL BE REQUIRED TO DROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKLY PROBLEM CONTRACTOR. S. CONTRACTOR SHALL BE REQUIRED TO REAR PROPERLY CONTAINED. S. CONTRACTOR SHALL BE REQUIRED TO RECOVER AND FRACE AND THE MEDINES DUE TO THE CONTRACTOR. S. CONTRACTOR SHALL BE REQUIRED TO REAR PROPERLY CONTAINED. S. CONTRACTOR SHALL BE REQUIRED TO REAR PROPERLY CONTAINED. S. CONTRACTOR SHALL BE REQUIRED TO REAR PROPERLY CONTAINED. S. CONTRACTOR SHALL BE		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF, CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TH ANIONIC POLYMERS AND VACUUM TRUCK.	IETHOD OF CON IFFICIENT IN CON DENT ENGINEER A FRAC OUT OC A TURBIDITY CUR FRAC OUT. CON UCK OR COMBIN	FAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTO TO WALK TH REMEDIATIO 3. CONTRACTO POLYMER S' STREAMS W	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT / DR SHALL BE REQUIRE HE DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSITE TO TRI /ITH THE UNDERSTAN	AUST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER EAT AT LEAST ONE I	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE IT ONE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQ RELEASE INTO WETLA	PERSON ITE JATE NDS OR	© 10RPHY & ENGINEER	84-000613	KEGAN IONAL PORT
A FRAC OUT, THE OWNER SHALL CLEANUP OR STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE OWNER TO CLEAN-UP AND STABILIZE THE IMPACTED AREAS. ALL MONIES EXPENDED BY THE SOLUTIONS WILL BE REQUIRED TO BE PROVIDED BY THE CONTRACTOR. DATE: 4/16/2021 JOB No: 190226-02 TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED.		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF A CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TF ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUIN	IETHOD OF CON FFICIENT IN CON DENT ENGINEER A A FRAC OUT OC A TURBIDITY CUR FRAC OUT. CON UCK OR COMBIN INGENCY PLAN F	TAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT / DR SHALL BE REQUIRE 4 DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSITE TO TRI TITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQ JING THE AMOUNT OI ING THE AMOUNT OI	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER CAT AT LEAST ONE F DING THAT ADDITI- UIRED TO PROVIDE P DRILLING MUD RB	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIAT TONE (1) FULL TIME OUTS AND COORDIN. IFICATIONS OF ADEQU RELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI- LEASED, THE METHO	PERSON ITE NDS OR BE D THE D OF	© 10RPHY & ENGINEER	2	KEGAN IONAL PORT
SHALL BE PROVIDED TO THE SMC AND THE AIRPORT. IMPACTED AREAS SHALL BE HELD FROM THE MONIES DUE TO THE CONTRACTOR. CHECKED BY: DKP 4. CATALOG CUT SHEETS FOR EACH RECOMMENDED POLYMER WITH DIRECTIONS FOR USE AND ANY LIMITATIONS WILL BE REQUIRED TO BE PROVIDED BY THE CONTRACTOR. S. CONTRACTOR. CHECKED BY: DKP 5. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED. DATE: 4/16/2021		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF , CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TF ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUII 1. CONTRACTOR SHALL PROVIDE THE NAME, ADDRESS, THE ONSITE DRILLING COMPANY REPRESENTATIVE T PRIOR TO DRILLING. 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLIN	IETHOD OF CON FFICIENT IN CON DENT ENGINEER PARC OUT OC TURBIDITY CUB FRAC OUT CON UCK OR COMBIN INGENCY PLAN F REMENTS AND PHONE NU D THE SMC AND	TAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF OR MBER OF THE AIRPORT	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATT 5. CONTRACTC AFFECTED. WEEKLY REF	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT / DR SHALL BE REQUIRE 4 DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSITE TO TRI /ITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQ UNG THE AMOUNT OI ENT, THE REMEDIATIC ON. DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER AT AT LEAST ONE I DING THAT ADDITI- UNRED TO PROVIDE F DRILLING MUD RE DN METHOD USED, SMC OF ANY FRAC VILL BE REQUIRED T TE FOUR (4).	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE TO TRE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQU IFICATIONS OF ADEQU ELEASEINTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED II	PERSON ITE JATE NDS OR BE D THE D OF L FILAND IS N THE	CTT CONSULTING ENGINEER	2	MATIONAL AIRPORT
4. CATALOG CUT SHEETS FOR EACH RECOMMENDED POLYMER WITH DIRECTIONS FOR USE AND ANY LIMITATIONS WILL BE REQUIRED TO BE PROVIDED BY THE CONTRACTOR. 5. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED. CONTRACTOR SHALL BE REQUIRED TO DE NOT OCCUR OR ARE PROPERLY CONTAINED. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND THE PROPOSED METHODS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED.		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF , CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TF ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUI 1. CONTRACTOR SHALL PROVIDE THE NAME, ADDRESS, THE ONSITE DRILLING. 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLING SHALL BE PROVIDED BY THE CONTRACTOR.	IETHOD OF CON FFICIENT IN CON FFICIENT IN CON DENT ENGINEER A FRAC OUT OC I TURBIDITY CUR FRAC OUT CON UCK OR COMBIN INGENCY PLAN F REMENTS AND PHONE NU D THE SMC AND G MUD CONSTIT	TAINMENT IS TAINMENT CURS AND TAINO OR TAINED TAINED TAINO OF OR MBER OF THE AIRPORT UENTS	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATH 5. CONTRACTC AFFECTED. WEEKLY REI 6. IF THE CONT A FRAC OUT	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT /, OR SHALL BE REQUIRE HE DRILLING ROUTE A DR SHALL BE REQUIRE HE DRILLING ROUTE A DR SHALL BE REQUIRE ITHE HE UNDERSTAM. IF THE FIRST IS USED. ACTOR SHALL BE REQ ING THE AMOUNT OI ON. DR SHALL NOTIFY THE THIS INFORMATION W PORT DETAILED IN NC IRACTOR FAILS TO TA T, THE OWNER SHALL	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER CAT AT LEAST ONE I DING THAT ADDITI- UIRED TO PROVIDE F DRILLING MUD RE DN METHOD USED, SMC OF ANY FRAC VILL BE REQUIRED T TE FOUR (4). KE IMMEDIATE COI CLEANUP OR STABI	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIAT TONE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQI RELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED I RRECTIVE ACTION TO LIZE THE IMPACTED A	PERSON ITE NDS OR BE D THE D OF L TLAND IS NTHE REMEDY REAS.	CCANFORD, MURPHY & CONSULTING ENGINEER	2	WAUKEGAN NATIONAL AIRPORT
CONTRACTOR. 5. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A METHOD OF COMPLETION TO BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED.		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TF ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUII 1. CONTRACTOR SHALL BE ROUIDE THE NAME, ADDRESS, THE ONSITE DRILLING COMPANY REPRESENTATIVE T PRIOR TO DRILLING. 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLIN SHALL BE PROVIDED BY THE CONTRACTOR. 3. THE NAME, ADDRESS AND PHONE NUMBER OF THE JA	IETHOD OF CON FFICIENT IN CON DENT ENGINEER DA FRAC OUT OC TURBIDITY CUB FRAC OUT CON UCK OR COMBIN INGENCY PLAN F AND PHONE NU D THE SMC AND G MUD CONSTIT ANIONIC POLYMI	TAINMENT IS TAINMENT CURS AND TAINO OR TAINED TAINED TAINO OF OR MBER OF THE AIRPORT UENTS	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATT 5. CONTRACTC AFFECTED. ' WEEKLY REI 6. IF THE CONT A FRAC OUT A FRAC OUT A LMONIES	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT , DR SHALL BE REQUIRE HE DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSTRE TO TRI /ITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQUIRE CON. DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE AND THE SHALL ON NOTIFY THE DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE SCHOUNDER SHALL SEXPENDED BY THE C	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER AT AT LEAST ONE I DING THAT ADDITI- DING THAT ADDITI-	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE T OTRE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQU VELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED II RECTIVE ACTION TO LIZE THE IMPACTED A P AND STABLIZE THE	PERSON ITE JATE NDS OR BE D THE D OF L TLAND IS N THE REMEDY REAS.	BESIGN BY: CONSULTING ENGINEER	License No.	MATIONAL AIRPORT OBE
BE ACCEPTED BY THE SUC, AIRPORT, AND RESIDENT ENGINEER IN WHICH LIKELY PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONAL DRILLING TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED.		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF , CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TF ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUIN 1. CONTRACTOR SHALL PROVIDE THE NAME, ADDRESS, THE ONSITE DRILLING. 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLIN SHALL BE PROVIDED BY THE CONTRACTOR. 3. THE NAME, ADDRESS AND PHONE NUMBER OF THE A SHALL BE PROVIDED TO THE SMC AND THE AIRORT. 4. CATALOG CUT SHEETS FOR EACH RECOMMENDED PC	IETHOD OF CON FFICIENT IN CON FFICIENT IN CON ENT ENGINEER A FRAC OUT OC I TURBIDITY CUR FRAC OUT OC INGENCY PLAN F INGENCY PLAN F INGENCY PLAN F CONTROLOGIE AND PHONE NU D THE SMC AND G MUD CONSTIT ANIONIC POLYMI	TAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF OR MBER OF THE AIRPORT UENTS :R VENDOR RECTIONS	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATT 5. CONTRACTC AFFECTED. ' WEEKLY REI 6. IF THE CONT A FRAC OUT A FRAC OUT A LMONIES	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT , DR SHALL BE REQUIRE HE DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSTRE TO TRI /ITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQUIRE CON. DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE AND THE SHALL ON NOTIFY THE DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE SCHOUNDER SHALL SEXPENDED BY THE C	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER AT AT LEAST ONE I DING THAT ADDITI- DING THAT ADDITI-	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE T OTRE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQU VELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED II RECTIVE ACTION TO LIZE THE IMPACTED A P AND STABLIZE THE	PERSON ITE JATE NDS OR BE D THE D OF L TLAND IS N THE REMEDY REAS.	BESIGN BA CHECKED MURPHY & CHECKED BA CONSULTING ENGINEER	License No.	MATIONAL AIRPORT DRb
PROBLEM LOCATIONS AND THE PROPOSED METHODS OF DIRECTIONAL DRILLING JUB NO: 190226-02 TO ENSURE THAT FRAC OUTS DO NOT OCCUR OR ARE PROPERLY CONTAINED.		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER, AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF J CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING ETHER A VACUUM TE ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUII 1. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING COMPANY REPRESENTATIVE T PRIOR TO DRILLING. 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLIN SHALL BE PROVIDED BY THE CONTRACTOR. 3. THE NAME, ADDRESS AND PHONE NUMBER OF THE SHALL BE PROVIDED TO THE SMC AND THE AIRPORT. 4. CATALOG CUT SHEETS FOR EACH RECOMMENDED PC FOR USE AND ANY LIMITATIONS WILL BE REQUIRED TO	IETHOD OF CON FFICIENT IN CON FFICIENT IN CON ENT ENGINEER A FRAC OUT OC I TURBIDITY CUR FRAC OUT OC INGENCY PLAN F INGENCY PLAN F INGENCY PLAN F CONTROLOGIE AND PHONE NU D THE SMC AND G MUD CONSTIT ANIONIC POLYMI	TAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF OR MBER OF THE AIRPORT UENTS :R VENDOR RECTIONS	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATT 5. CONTRACTC AFFECTED. ' WEEKLY REI 6. IF THE CONT A FRAC OUT A FRAC OUT A LMONIES	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT , DR SHALL BE REQUIRE HE DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSTRE TO TRI /ITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQUIRE CON. DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE AND THE SHALL ON NOTIFY THE DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE SCHOUNDER SHALL SEXPENDED BY THE C	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER AT AT LEAST ONE I DING THAT ADDITI- DING THAT ADDITI-	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE T OTRE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQU VELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED II RECTIVE ACTION TO LIZE THE IMPACTED A P AND STABLIZE THE	PERSON ITE JATE NDS OR BE D THE D OF L TLAND IS N THE REMEDY REAS.	DESIGN BY: DRAWN BY: CHECKED BY: CHECKED BY: APPROVED BY	License No.	AIRPORT AIRPORT ABU ABU ABU ABU ABU ABU
		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF A CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TR ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UDPATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUIN 1. CONTRACTOR SHALL BE REQUIRED TO UDPATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUIN 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLIN SHALL BE PROVIDED BY THE CONTRACTOR. 3. THE NAME, ADDRESS AND PHONE NUMBER OF THE SHALL BE PROVIDED TO THE SMC AND THE AIRPORT. 4. CATALOG CUT SHEETS FOR EACH RECOMMENDED PO FOR USE AND ANY LIMITATIONS WILL BE REQUIRED TO CONTRACTOR.	IETHOD OF CON FFICIENT IN CON FFICIENT IN CON ENT ENGINEER A FRAC OUT OC I TURBIDITY CUB FRAC OUT CON UCK OR COMBIN INGENCY PLAN F REMENTS AND PHONE NU D THE SMC AND G MUD CONSTIT INIONIC POLYMI DUYMER WITH DI O BE PROVIDED ETHOD OF COMF	TAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF OR MBER OF THE AIRPORT UENTS ER VENDOR RECTIONS BY THE LETION TO	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATT 5. CONTRACTC AFFECTED. ' WEEKLY REI 6. IF THE CONT A FRAC OUT A FRAC OUT A LMONIES	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT , DR SHALL BE REQUIRE HE DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSTRE TO TRI /ITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQUIRE CON. DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE AND THE SHALL ON.	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER AT AT LEAST ONE I DING THAT ADDITI- DING THAT ADDITI-	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE T OTRE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQU VELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED II RECTIVE ACTION TO LIZE THE IMPACTED A P AND STABLIZE THE	PERSON ITE JATE NDS OR BE D THE D OF L TLAND IS N THE REMEDY REAS.	DESIGN BY: DRAWN BY: CHECKED BY: APPROVED BY DATE:	License No.	AIRPORT ALRPORT ALRPORT
		IN THE INSTANCE OF A FRAC OUT, THE CONTRACTOR SHA AND WORK TO CONTAIN THE DRILLING MUD. THE BEST N WITH USE OF A BARRIER. THE BARRIER USED SHALL BE SL AND MUST BE APPROVED BY THE AIRPORT AND THE RESI WHEN WORKING NEAR WETLANDS OR OPEN WATER AND INFILITRATES A WETLAND OR OPEN WATER, THE USE OF CONTAINMENT BOX WILL BE REQUIRED TO CONTAIN THE WATER SHALL BE REMOVED USING EITHER A VACUUM TE ANIONIC POLYMERS AND VACUUM TRUCK. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUII 1. CONTRACTOR SHALL BE REQUIRED TO UPDATE THE CONT APPROVAL BY RE & SMC. DIRECTIONAL DRILLING GENERAL INFORMATION REQUII SHALL BE PROVIDED THE NAME, ADDRESS, THE ONSITE DRILLING COMPANY REPRESENTATIVE T PRIOR TO DRILLING. 2. MATERIAL SAFETY DATA SHEETS (MSDS) FOR DRILLIN SHALL BE PROVIDED BY THE CONTRACTOR. 3. THE NAME, ADDRESS AND PHONE NUMBER OF THE . SHALL BE PROVIDED TO THE SMC AND THE AIRPORT. 4. CATALOG CUT SHEETS FOR EACH RECOMMENDED PP FOR USE AND ANY LIMITATIONS WILL BE REQUIRED TO CONTRACTOR. 5. CONTRACTOR SHALL BE REQUIRED TO PROVIDE A MI BE ACCEPTED BY THE SMC, AIRPORT, AND RESIDENT PROBLEM LOCATIONS AND THE PROPOSED METHOD	IETHOD OF CON FFICIENT IN CON DENT ENGINEER A FRAC OUT OC TURBIDITY CUB FRAC OUT OC TURBIDITY CUB FRAC OUT. CON UCK OR COMBIN INGENCY PLAN F REMENTS AND PHONE NU D THE SMC AND D THE SMC AND G MUD CONSTIT ANIONIC POLYMI DUYMER WITH DI TO BE PROVIDED ETHOD OF COMBE S OF DIRECTION.	TAINMENT IS TAINMENT CURS AND TAIN OR TAINED IATION OF OR MBER OF THE AIRPORT UENTS CR VENDOR RECTIONS BY THE LETION TO IICH LIKELY LA DRILLING	1. AT LEAST OI OPERATION AVAILABLE 2. CONTRACTC TO WALK TH REMEDIATIC 3. CONTRACTC POLYMER S' STREAMS W PROCURED 4. THE CONTR SMC DETAIL CONTAINMI INFORMATT 5. CONTRACTC AFFECTED. ' WEEKLY REI 6. IF THE CONT A FRAC OUT A FRAC OUT A LMONIES	NE VACUUM TRUCK N IS AND AT LEAST ONE OR ON STAND-BY AT , DR SHALL BE REQUIRE HE DRILLING ROUTE A DN. DR SHALL BE REQUIRE TORED ONSTRE TO TRI /ITH THE UNDERSTAN IF THE FIRST IS USED. ACTOR SHALL BE REQUIRE CON. DR SHALL NOTIFY THE THIS INFORMATION V PORT DETAILED IN NC TRACTOR FIALS TO TAILS TO THE AND THE SHALL ON.	UST BE ONSITE DL ADDITIONAL VACU A NEARBY LOCATIO D TO HAVE AT LEAS ND IDENTIFY FRAC D TO PROVIDE VER AT AT LEAST ONE I DING THAT ADDITI- DING THAT ADDITI-	RING ALL DRILLING UM TRUCK SHALL BE N, AS APPROPRIATE T OTRE (1) FULL TIME OUTS AND COORDIN, IFICATIONS OF ADEQU VELEASE INTO WETLA DNAL POLYMER WILL A WEEKLY REPORT TI LEASED, THE METHO AND ANY ADDITIONA OUT IN WHICH A WE O BE SUMMARIZED II RECTIVE ACTION TO LIZE THE IMPACTED A P AND STABLIZE THE	PERSON ITE JATE NDS OR BE D THE D OF L TLAND IS N THE REMEDY REAS.	DESIGN BY: DRAWN BY: CHECKED BY: APPROVED BY DATE:	License No.	AM JRO DKP ARM 4/16/2021


THE DEPTH OF THE DIRECTIONAL BORE SHALL BE NO LESS THAN 4.0' FROM THE PAVEMENT SURFACE AND SHALL NOT DISTURB EXISTING UNDERDRAINS/UTILITIES OR NEW LIGHTS/CABLING.
 REFER TO LIGHTING PLANS FOR ADDITIONAL CABLE AND CONDUT INFORMATION.
 THE MAXIMUM PAY LENGTH SHALL BE THE PAVEMENT WIDTH PLUS FOUR FEET PAST THE EDGE OF PAVEMENT OR AS NOTED ON THE PLANS.

NOTE: ASTERISK DENOTES SPECIALTY ITEM



SHEET 2 OF 23 SHEETS

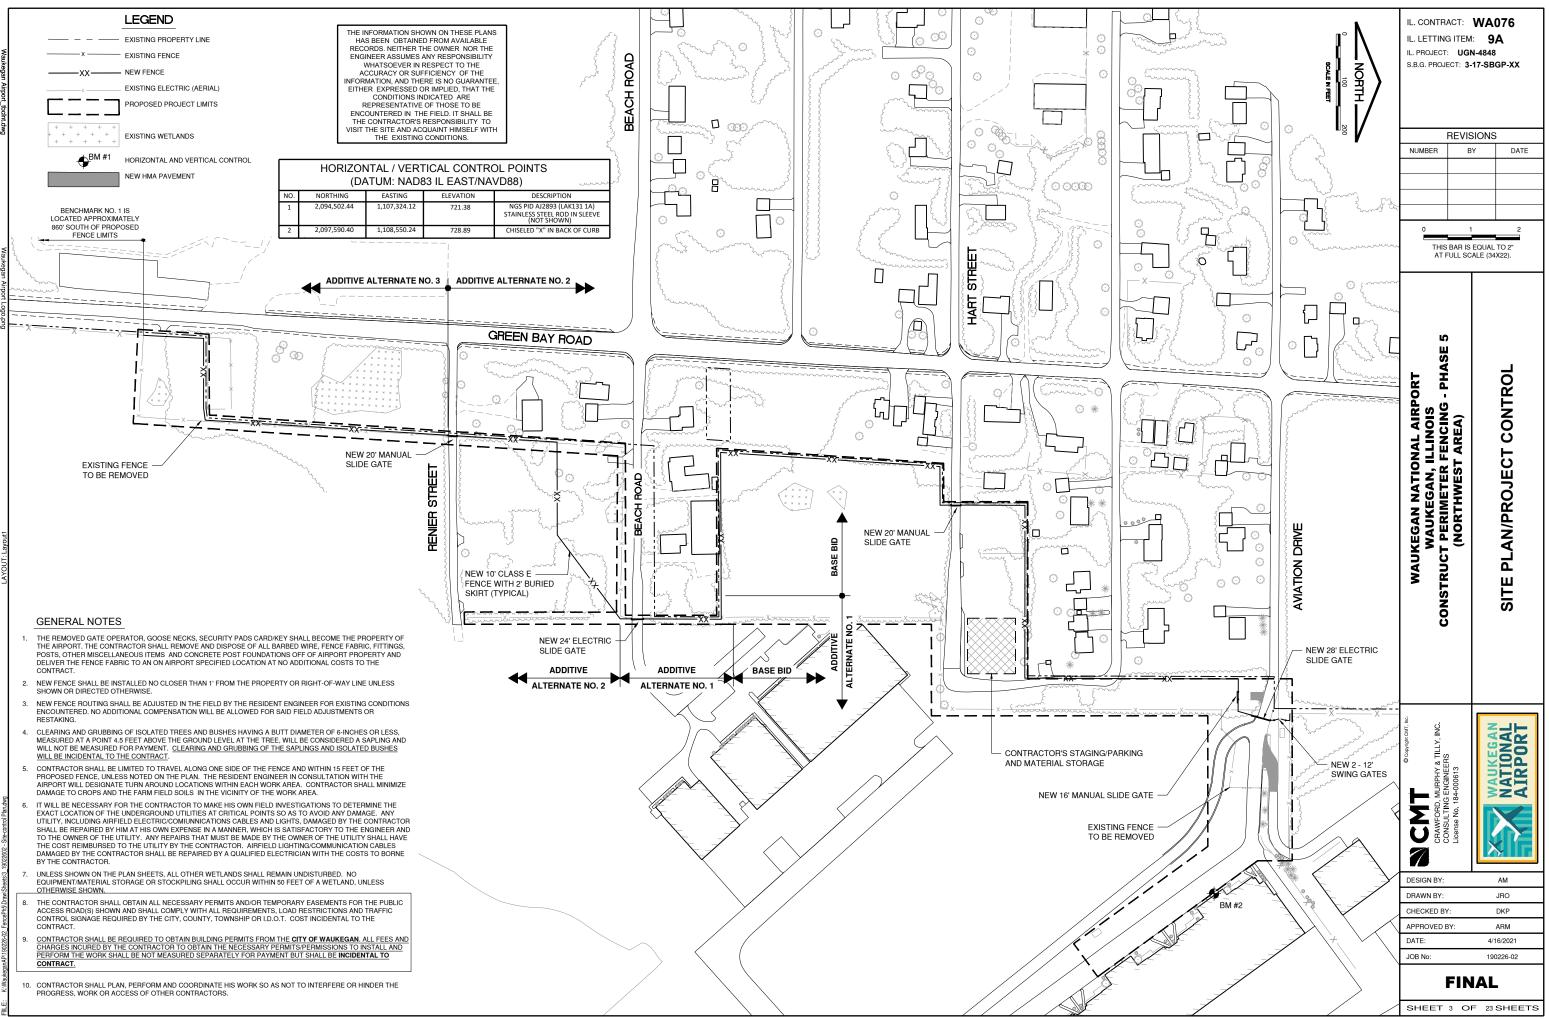

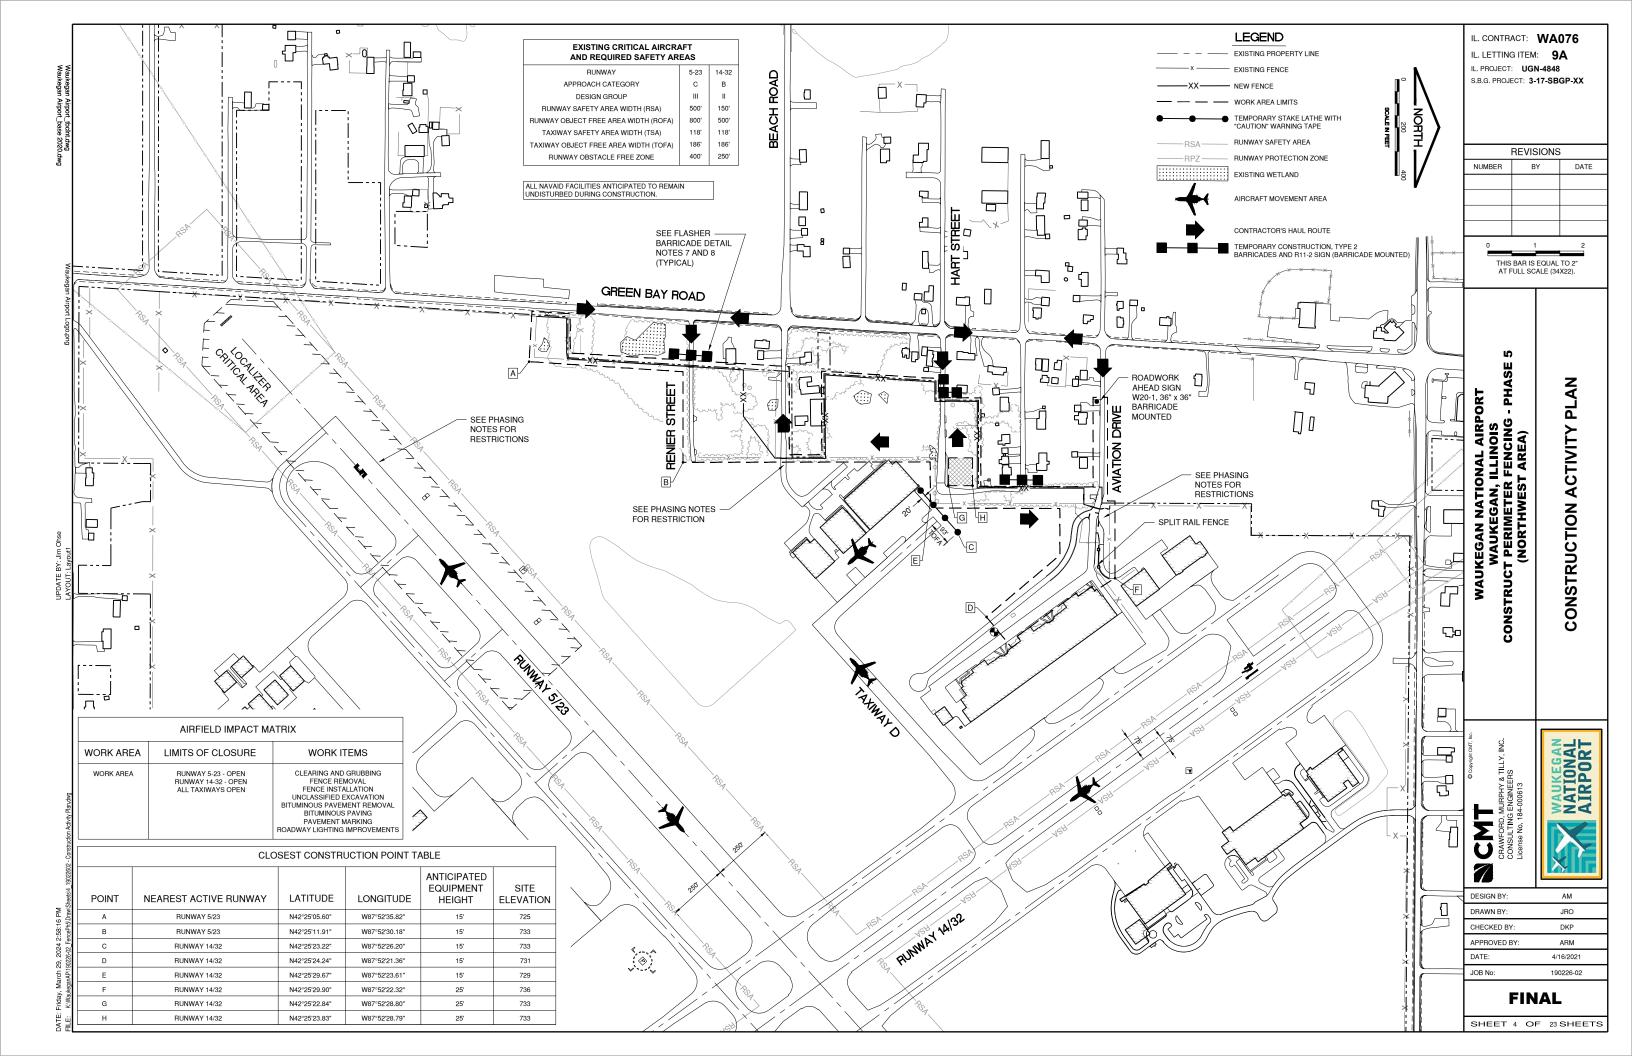

GENERAL

- THE CONTRACTOR AND ALL SUBCONTRACTORS SHALL FOLLOW THE REQUIREMENTS OF THE AIRPORT'S APPROVED CONSTRUCTION SAFETY AND PHASING PLAN (CSPP), FAA AC 150/5370-2G OR LATEST EDITION, AND ALL AIRPORT SAFETY AND SECURITY REQUIREMENTS.
- PRIOR TO THE NOTICE TO PROCEED, THE CONTRACTOR SHALL 2. SUBMIT TO THE AIRPORT THROUGH THE RESIDENT ENGINEER, FOR APPROVAL A SAFETY PLAN COMPLIANCE DOCUMENT (SPCD) IN ACCORDANCE WITH FAA AC 150/5370-2G OR LATEST EDITION. NO CONSTRUCTION ACTIVITY SHALL BEGIN UNTIL THE AIRPORT HAS APPROVED THE SPCD.
- THE CSPP COVERS OPERATIONAL SAFETY. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE INDIVIDUAL SAFETY OF HIS/HER З. PERSONNEL AND MEETING OSHA REQUIREMENTS.
- A MINIMUM OF 10 DAYS PRIOR TO THE NOTICE TO PROCEED THE 4. CONTRACTOR SHALL PROVIDE A LIST OF SUBCONTRACTORS AND MATERIAL SUPPLIERS
- ALL CONTRACTOR COSTS ASSOCIATED WITH THE REQUIREMENTS LISTED ON THIS SHEET SHALL BE CONSIDERED INCIDENTAL TO THE CONTRACT.
- EXISTING ELECTRICAL GATES ARE TO REMAIN IN OPERATION UNTIL NEW GATE AND OPERATOR ARE INSTALLED AND READY FOR 6. SERVICE. THE CONTRACTOR SHALL NOTIFY THE RESIDENT ENGINEER AND AIRPORT A MINIMUM OF 2 CALENDAR DAYS ADVANCE NOTICE OF THE GATE SWITCH OVER TO COORDINATE WITH TENANTS

1. COORDINATION

- PRIOR TO THE START OF CONSTRUCTION THE CONTRACTOR SHALL ATTEND A PRE-CONSTRUCTION CONFERENCE WITH THE AIRPORT, RESIDENT ENGINEER, AND ILLINOIS DIVISION OF AERONAUTICS (IDA). THE COST OF PREPARING FOR AND ATTENDING THE PRE-CONSTRUCTION CONFERENCE SHALL BE INCIDENTAL TO THE CONTRACT.
- ON OR BEFORE THE PRE-CONSTRUCTION CONFERENCE, THE CONTRACTOR SHALL SUBMIT A PROPOSED SCHEDULE FOR THE PROJECT THE SCHEDULE SHALL INCLUDE A START AND COMPLETION DATE FOR EACH ITEM OF WORK. THE SCHEDULE SHALL BE UPDATED ON A WEEKLY BASIS. ALL COSTS ASSOCIATED WITH THE SCHEDULE SHALL BE INCIDENTAL TO THE CONTRACT.
- DURING CONSTRUCTION THE CONTRACTOR SHALL ATTEND A 3. WEEKLY COORDINATION MEETING WITH THE AIRPORT STAFF AND RESIDENT ENGINEER. ALL COSTS ASSOCIATED WITH ATTENDING THE WEEKLY MEETING SHALL BE INCIDENTAL TO THE CONTRACT

2. PHASING

UPDATE

- TOTAL CONTRACT TIME SHALL BE 52 CALENDAR DAYS.
- WORK SHALL BE COMPLETED UNDER ONE PHASE AS SHOWN ON 2. THE CONSTRUCTION ACTIVITY PLAN (CAP) SHEETS.
- WORK AREAS AND DESCRIPTIONS

COMPLETE INITIAL MOBILIZATION, STAGING AREA PREPARATION, AND LAYOUT IN ORDER TO CLEAR AND GRUB EXISTING TREES AND BRUSH. CLEAR EXISTING TREES AND BRUSH WITHIN THE LIMITS OF FENCE LAYOUT. INSTALL WETLAND PROTECTIONS AND INITIAL EROSION CONTROL MEASURES.

ONCE CLEARING AND GRUBBING OPERATIONS ARE COMPLETE AND WETLAND PROTECTIONS ARE IN PLACE COMPLETE FENCE REMOVAL, FENCE INSTALLATION, PAVEMENT REMOVAL, NEW PAVEMENT, LANDSCAPING AND GENERAL IMPROVEMENTS

RESTRICTIONS 4.

CLEARING AND GRUBBING OF TREES

NO CUTTING OR TRIMMING OF TREES SHALL OCCUR BETWEEN APRIL 1 AND SEPTEMBER 30, BOTH DAYS INCLUSIVE, DUE TO POTENTIAL IMPACT TO THE NORTHERN LONG EARED BAT.

AVIATION DRIVE AND FORTUNE DRIVE

THE CONTRACTOR SHALL PHASE THE ROADWAY IMPROVEMENTS TO MAINTAIN ACCESS TO AIRFIELD HANGARS. ANY TEMPORARY IMPROVEMENTS TO MAINTAIN HANGAR ACCESS SHALL BE INCIDENTAL TO THE CONTRACT. SHOULD THE CONTRACTOR NEED TO BLOCK ACCESS TO THE HANGARS FOR AN IMPROVEMENT, THE CONTRACTOR SHALL NOTIFY THE RESIDENT ENGINEER AND THE AIRPORT A MINIMUM OF 2 CALENDAR DAYS IN ADVANCE. THE CONTRACTOR WILL ONLY BE ALLOWED TO BLOCK HANGAR ACCESS A MAXIMUM OF 4-HOURS ON ANY GIVEN OCCURRENCE. THE CONTRACTOR SHALL PLACE TYPE II BARRICADES AT PAVEMENT DROP OFFS THE BABBICADES SHALL BE SPACED AT A MAXIMUM 5 FOOT SPACING EXISTING POWERED SLIDE GATES TO REMAIN IN SERVICE UNTIL NEW POWERED SLIDE GATE IS READY FOR OPERATION. EXISTING POWERED SLIDE GATE TO REMAIN IN SERVICE UNTIL NEW POWERED SLIDE GATE IS READY FOR OPERATION. EXISTING POWERED SLIDE GATE TO REMAIN IN SERVICE UNTIL NEW POWERED SLIDE GATE IS READY FOR OPERATION.

BEACH ROAD

EXISTING POWERED SLIDE GATE TO REMAIN IN SERVICE UNTIL NEW POWERED SLIDE GATE IS READY FOR OPERATION.

5. DURATIONS AND MILESTONES:

MILESTONE 1

SUBSTANTIALLY COMPLETE MOBILIZATION, INCLUDING CLEARING AND GRUBBING AND ANY REQUIRED PRE-CONSTRUCTION FIELD WORK BETWEEN OCTOBER 1ST AND MARCH 31ST

MILESTONE 2

SUBSTANTIALLY COMPLETE REMAINING WORK, EXCLUDING CLEARING AND GRUBBING.

3. AREAS AND OPERATIONS AFFECTED BY THE CONSTRUCTION ACTIVITY

- ALL RUNWAYS, TAXIWAYS AND APRONS SHALL BE KEPT OPEN TO AIRCRAFT TRAFFIC DURING CONSTRUCTION EXCEPT AS NOTED ON THE PHASING PLAN.
- WHEN CONFLICTS ARISE BETWEEN CONSTRUCTION ACTIVITIES AND AIRCRAFT OPERATIONS AND SAFETY, AIRCRAFT OPERATIONS AND SAFETY SHALL TAKE PRECEDENCE AND SHALL GOVERN. FINAL AUTHORITY IN THE APPROVAL OF CONSTRUCTION SEQUENCING LIES WITH THE AIRPORT
- ALL CONSTRUCTION TRAFFIC SHALL IMMEDIATELY YIELD TO З. ONCOMING AIRCRAFT AT ALL TIMES.

4. NAVAIDS THAT COULD BE AFFECTED

- THE CONTRACTOR MUST COORDINATE WITH AIRPORT OPERATIONS/ENGINEER IN ADVANCE FOR ANY WORK WITHIN A NAVAID CRITICAL AREA OR AFFECTING THE VISUAL, TRANSMITTED SIGNAL OR POWER SUPPLY OF A NAVAID.
- 2. EDGE LIGHTS, THRESHOLD LIGHTS, VISUAL AIDS AND ALL ILS EQUIPMENT SHALL BE SHUT OFF FOR THE DURATION OF A CLOSURE PERIOD ON ANY ASSOCIATED PAVEMENTS. IF THE LIGHTING CIRCUIT MUST BE ON FOR OPEN PAVEMENT AREAS. CLOSED PAVEMENT AREA LIGHTS SHALL BE COVERED COMPLETELY.
- 3. EXCEPT WHERE NOTED IN THE PLANS, EXISTING COMMUNICATIONS EQUIPMENT AND NAVIGATIONAL AIDS (NAVAIDS) SHALL NOT BE DISTURBED BY THE CONTRACTOR AND SHALL BE PROTECTED FROM DAMAGE
- 4. PRIOR TO BEGINNING SITE WORK, CONTRACTOR SHALL COORDINATE THROUGH AIRPORT OPERATIONS TO LOCATE, AND THE CONTRACTOR TO MARK ALL UNDERGROUND COMMUNICATIONS CABLES AND FACILITIES, WITHIN THE PROJECT AREA.
- 5. IF CONTRACTOR CAUSES INTERRUPTION OF POWER OR COMMUNICATIONS TO A NAVAID CONTRACTOR SHALL REPAIR WITHIN 24 HOURS AT THE CONTRACTOR'S COST, CONTRACTOR MUST COORDINATE REPAIR WITH AIRPORT OPERATIONS BEFORE ANY REPAIR IS MADE.

5. CONTRACTOR ACCESS

- CONTRACTOR ACCESS SHALL BE AS NOTED BELOW AND AS SHOWN ON THE SITE PLAN AND CONSTRUCTION ACTIVITY PLAN SHEETS, ALL COSTS RELATING TO CONTRACTOR'S ACCESS AND SECURITY SHALL BE THE RESPONSIBILITY OF THE CONTRACTOR
- THE CONTRACTOR IS TO ACCESS THE SITE USING THE ROUTES AND GATE(S) SHOWN. THE CONTRACTOR SHALL BE RESPONSIBLE FOR KEEPING THE ACCESS GATE CLOSED DURING WORK HOURS.
- CONTRACTOR SHALL OBTAIN ALL NECESSARY PERMITS AND TEMPORARY EASEMENTS FOR THE PUBLIC ACCESS ROAD(S) SHOWN AND SHALL COMPLY WITH ALL REQUIREMENTS, LOAD RESTRICTIONS, & TRAFFIC CONTROL SIGNAGE REQUIRED BY THE CITY, COUNTY, TOWNSHIP, OR I.D.O.T.
- CONTRACTOR'S VEHICLES AND FOUIPMENT SHALL BE MARKED AND FLAGGED PER SECTION 70-10 OF THE STANDARD SPECIFICATIONS. MAXIMUM HEIGHT OF CONTRACTOR'S FOUIPMENT WILL BE 25'.
- 5 DRIVERS OF TRUCKS CONTAINING MATERIAL DELIVERIES (AGGREGATE, ASPHALT, ETC.) NEED NOT OBTAIN AN AIRPORT ID BADGE BUT SHALL BE REQUIRED TO SUBMIT THEIR NAME, DRIVER'S LICENSE NUMBER, TRUCK LICENSE PLATE NUMBER AND NAME OF TRUCKING COMPANY TO THE PRIME CONTRACTOR PRIOR TO ENTERING THE JOBSITE. WHILE INSIDE THE AOA FENCE, THE TRUCK DRIVERS SHALL BE ESCORTED BY THE CONTRACTOR PERSONNEL THAT HAS OBTAINED PROPER DRIVING PRIVILEGES.
- CONTRACTOR WORK CREWS MUST MAINTAIN RADIO CONTACT WITH THE WAUKEGAN AIR TRAFFIC CONTROL TOWER GROUND CONTROL (121.65 MHZ) AT ALL TIMES WHEN INSIDE THE AIRPORT OPERATIONS AREA (AÓA). THE CONTRACTOR SHALL SUPPLY ALL APPROPRIATE RADIOS NEEDED FOR COMMUNICATIONS AND ONLY HIS PERSONNEL WHO HAVE SUCCESSFULLY SATISFIED THE AIRPORT OF THEIR COMPETENCE MAY OPERATE THESE RADIOS
- THE CONTRACTORS STORAGE AND STAGING AREAS WILL BE AS 7. SHOWN ON THE SITE PLAN.
- THE CONTRACTOR SHALL KEEP A RECORD OF THE NAMES OF ALL 8. EMPLOYEES ENTERING THE JOB SITE ON A DAILY BASIS. A RECORD OF EACH SUBCONTRACTOR ENTERING THE JOB SITE SHALL ALSO BE KEPT BY THE CONTRACTOR
- 9. WHEN THE CONTRACTOR IS NOT WORKING, EQUIPMENT SHALL BE STORED AT THE STAGING AREAS.
- 10. DURING ADVERSE WEATHER THE CONTRACTOR SHALL MAINTAIN ACCESS TO THE WORK AT NO ADDITIONAL COST TO THE CONTRACT NO EXTENSION OF THE CONTRACT TIME WILL BE CONSIDERED FOR DELAYS DUE TO LACK OF ADEQUATE ACCESS TO THE WORK SITE.
- 11. THE CONTRACTOR WILL BE PERMITTED TO STORE EQUIPMENT AND MATERIALS ONLY AT THE LOCATIONS SHOWN. PARKED EQUIPMENT AND MATERIAL STOCKPILES SHALL NOT PENETRATE SURFACES DEFINED BY F.A.R. TITLE 14 PART 77 - OBJECTS AFFECTINGNAVIGABLE AIRSPACE EXISTING TUBE AREAS DISTURBED BY THE CONTRACTOR'S OPERATIONS SHALL BE RESTORED BY HIM AT HIS EXPENSE TO THE SATISFACTION OF THE RESIDENT ENGINEER AND THE AIRPORT.
- 12. ALL CONSTRUCTION TRAFFIC OPERATING ON, OR CROSSING BUNWAYS TAXIWAYS AND APBONS OPEN TO AIBCRAFT TRAFFIC SHALL BE UNDER CONTROL BY A FLAGMAN OR ESCORT IN RADIO CONTACT WITH THE COMMON TRAFFIC ADVISORY FREQUENCY. THE CONTRACTOR SHALL PROVIDE HIS OWN FLAGMEN.
- THE CONTRACTOR SHALL THOROUGHLY CLEAN ALL 13. CONSTRUCTION AREAS AND HAUL ROUTES WHICH WILL BE OPENED TO VEHICLE AND AIR TRAFFIC TO THE SATISFACTION OF AIRPORT OPERATIONS OR THE RESIDENT ENGINEER. A POWER BROOM AND OPERATOR SHALL BE ON SITE AT ALL TIMES WHEN ACTIVE PAVEMENTS ARE UTILIZED FOR CONSTRUCTION TRAFFIC.
- 14. ALL PAVEMENTS, DRIVES OR ANY OTHER AREAS LITILIZED BY THE CONTRACTOR FOR HAUL ROADS OR STORAGE AREAS SHALL BE MAINTAINED AND REPAIRED TO THE SAME CONDITION OR BETTER THAN THEY WERE PRIOR TO BEGINNING CONSTRUCTION NO ADDITIONAL COMPENSATION WILL BE MADE TO THE CONTRACTOR FOR THIS WORK.
- ALL VEHICLE AND EQUIPMENT OPERATORS USED BY THE CONTRACTOR SHALL BE PROPERLY TRAINED BY THE 15. CONTRACTOR.
- THE CONTRACTOR SHALL NOTIFY THE AIRPORT IF CONSTRUCTION 16. ACTIVITY WILL REQUIRE THE BLOCKAGE OF EMERGENCY ACCESS TO THE AIRPORT

13. SPECIAL CONDITIONS INFORMATION

10. INSPECTION REQUIREMENTS

3

2.


3.

2

OPENED.

2.

12. PENALTIES

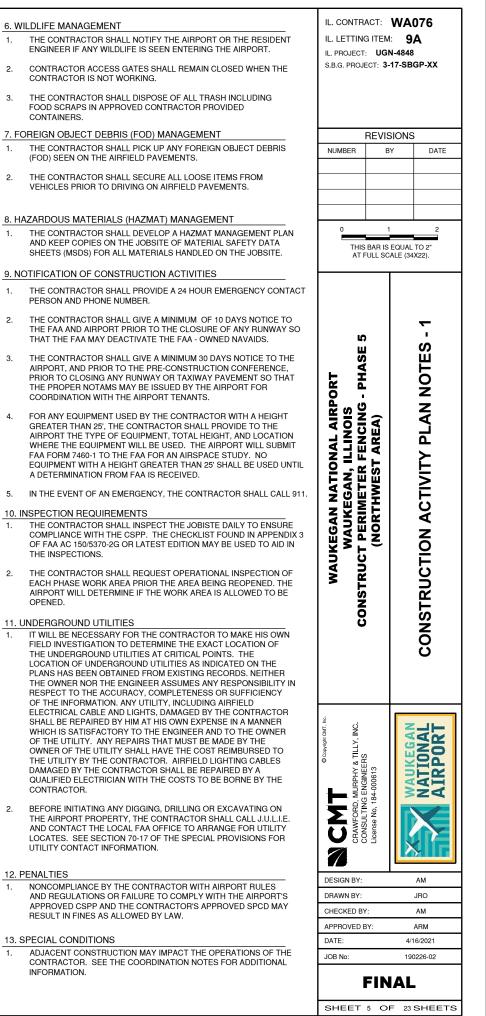

14. RUNWAY AND TAXIWAY VISUAL AIDS

1

- ALL RUNWAYS, TAXIWAYS, AND APRONS SHALL BE KEPT OPEN TO AIRPORT TRAFFIC DURING CONSTRUCTION EXCEPT AS NOTED IN THE CONSTRUCTION ACTIVITY PLAN.
- IF ANY RUNWAY OR TAXIWAY CLOSURES ARE REQUESTED BY THE CONTRACTOR AND APPROVED BY THE AIRPORT, THE CONTRACTOR SHALL USE MARKING, LIGHTING AND SIGNS THAT FOLLOWING THE REQUIREMENTS OF FAA AC 150/5370-2G OR LATEST EDITION.

15. MARKING AND SIGNS FOR ACCESS ROUTES

I. BARRICADES AND SIGNS SHALL BE USED ALONG THE CONTRACTOR'S ACCESS ROUTE AS DETAILED ON THE CONSTRUCTION ACTIVITY PLAN SHEETS.

16. HAZARD MARKING AND LIGHTING

- THE CONTRACTOR SHALL FURNISH, ERECT, AND MAINTAIN MARKINGS AND ASSOCIATED LIGHTING OF OPEN TRENCHES, EXCAVATIONS, TEMPORARY STOCKPILES, AND HIS/HER CONSTRUCTION EQUIPMENT.
- ALL CONSTRUCTION EQUIPMENT SHALL BE FLAGGED AND/OR LIGHTED IN ACCORDANCE WITH FAA ADVISORY CIRCULAR 150/5370-2G AND 150/5210-5C OR LATEST EDITION AT ALL TIMES WHILE OPERATING ON AIRPORT PROPERTY. THE MAXIMUM EQUIPMENT HEIGHT IS 25'.
- 3. BARRICADES SHALL BE PLACED AT THE LOCATIONS SHOWN ON THE CONSTRUCTION ACTIVITY PLAN SHEET OR AS DIRECTED BY THE ENGINEER.
- 4. THE CONTRACTOR SHALL INSPECT THE BARRICADES ONCE DURING EACH WORK DAY TO INSURE PROPER PLACEMENT AND PROPER OPERATION OF THE RED LIGHTS AND FLAG PLACEMENT.

17. WORK ZONE LIGHTING FOR NIGHTTIME CONSTRUCTION


- 1. WORK PERFORMED BY THE CONTRACTOR OUTSIDE OF DAYLIGHT HOURS SHALL BE DONE UNDER SUFFICIENT ARTIFICIAL AREA LIGHTING TO ALLOW FOR PROPER CONSTRUCTION METHODS AND INSPECTION.
- 2. LIGHTS SHALL CONSIST OF VEHICLE OR MOVABLE POLE MOUNTED FLOODLIGHTS AND/OR SPOTLIGHTS OF SUFFICIENT NUMBER TO ILLUMINATE THE WORK AREA. VEHICLE HEADLIGHTS WILL BE ALLOWED ONLY IN ADDITION TO OTHER LIGHTS MENTIONED ABOVE. LIGHTING SHALL NOT INTERFERE WITH AIR OPERATIONS. ANY WORK BEING PERFORMED UNDER INSUFFICIENT ARTIFICIAL LIGHTING, IN THE RESIDENT ENGINEER'S JUDGEMENT, SHALL BE STOPPED UNTIL SUCH TIME AS ADDITIONAL LIGHTING IS PROVIDED. ALL WORK PERFORMED DURING THAT TIME WILL NOT BE ACCEPTABLE UNTIL PROPER INSPECTION AND TESTING CAN BE MADE.

18. PROTECTION

- 1. ALL WORK REQUIRED INSIDE OF A RUNWAY SAFETY AREA, WILL REQUIRE THE RUNWAY TO BE CLOSED.
- 2. ALL WORK REQUIRED ON AN ACTIVE TAXIWAY OR INSIDE OF AN ACTIVE TAXIWAY OBJECT FREE AREA, WILL REQUIRE THE TAXIWAY TO BE CLOSED.


19. OTHER LIMITATIONS ON CONSTRUCTION

- . IF, DURING CONSTRUCTION, AN EMERGENCY IS DECLARED BY THE AIRPORT, THE CONTRACTOR SHALL IMMEDIATELY CLEAR THE PAVEMENT OF ALL VEHICLES, PERSONNEL AND EQUIPMENT IF DIRECTED BY THE AIRPORT.
- BROKEN CONCRETE, BROKEN ASPHALT, RUBBISH FROM DEMO, AND OTHER MISCELLANEOUS DEBRIS SHALL BE DISPOSED OF OFF AIRPORT PROPERTY, UNLESS OTHERWISE SPECIFIED.
- THE CONTRACTOR WILL BE RESPONSIBLE FOR COORDINATING THE AIRSPACE FOR THE CONSTRUCTION EQUIPMENT THAT IS TALLER THAN THAT SPECIFIED ON THE PLANS WITH THE FAA. THIS PROCESS MAY TAKE UP TO 12 WEEKS TO COMPLETE.
- THE CONTRACTOR SHALL BE RESPONSIBLE FOR MEGGAR TESTING ALL EXISTING CIRCUITS PRIOR TO CONSTRUCTION AND FOLLOWING CONSTRUCTION AS SPECIFIED IN THE CONTRACT DOCUMENTS.



LATHING AND WARNING TAPE DETAIL

NOT TO SCALE MATERIALS ARE TO BE APPROVED BY ENGINEER PRIOR TO INSTALLATION. COST OF MATERIALS, INSTALLATION, RELOCATION AND MAINTENANCE OF LATHING AND WARNING TAPE SHALL BE INCIDENTAL TO THE CONTRACT.




AND TRUCK SIGNAL FLAG



TYPICAL PROFILE F.A.R. PART 77 IMAGINARY SURFACES

NO SCALE


RUNWAY END	ELEVATION	APPROACH SLOPE
5	724.7	34:1
23	723.1	50:1
14	727.6	20:1
32	712.1	20:1



TYPICAL SECTION F.A.R. PART 77 IMAGINARY SURFACES

NO SCALE

NOTE: IMAGINARY SURFACE REQUIREMENTS FOR EXISTING ACTIVE RUNWAYS (R/W) ARE SIMILAR EXCEPT PRIMARY SURFACE (PS) DIMENSIONS VARY RUNWAY 14-32 250' PS (125' LT & RT OF CENTERLINE) RUNWAY 5-23 1000' PS (500' LT & RT OF CENTERLINE)



FLASHER BARRICADE DETAIL

NOT TO SCALE

NOTES


- 1. FLASHERS TO BE BATTERY OPERATE AND BE ABLE TO ROTATE 90 DECRI FLASHER LENSES SO THAT EVERY O ROTATED 90'.
- SANDBAGS TO BE PLACED ON EACH REQUIRED TO PREVENT DISPLACEMEN PROP BLAST.
- NO SEPARATE PAYMENT WILL BE MA COSTS SHALL BE CONSIDERED INCID PROJECT.
- 4. PLACE AT FIVE (5') INTERVALS.
- ONE 20"x20" ORANGE FLAG TO BE BARRICADE.
- CONTRACTOR SHALL BE RESPONSIBL BARRICADES AT ALL TIMES TO THE AIRPORT MANAGER.
- BARRICADES PLACED TO BLOCK ACC EXISTING ROADS SHALL ALSO HAVE STRUNG BETWEEN BARRICADES. THE ALSO HAVE RIBBON STRUNG FROM VISIBILITY OF ROPE/CABLE.
- BARRICADES PLACED TO BLOCK ACC EXISTING ROADS SHALL HAVE AT LE SIGN ATTACHED TO A CENTER BARF


- GATE ACCESS CONTROL CONTRAC
- REHABILITATE AIRFIELD LIGHTING
- GROUND CONTROL FREQUENCY: 121.6


MAXIMUM ANTICIPATED HEIGHT OF CO EQUIPMENT: DUMP TRUCK IN DUMP PO

IN THE EVENT THE CONTRACTOR PROF CONSTRUCTION EQUIPMENT THAT IS T LISTED, THE CONTRACTOR WILL BE RE FAA FORM 7460 FOR AIRSPACE APPRO ENGINEER WILL PROVIDE BASE AIRPOF THE CONTRACTOR'S USE.


20" x 20" ORANGE FLA	cs	IL. CONTRA IL. LETTING IL. PROJECT: S.B.G. PROJEC	ITEM: UGN-48	9A ⁴⁸
		F	EVISION	IS
	-	NUMBER	BY	DATE
L (IDOT TYPE 2)	-			
				2
TED. LENS TO BE RED REES. ALTERNATE OTHER LENS IS			BAR IS EQU	
CH SUPPORT BRACE AS IENT BY WIND, JET OR				
MADE FOR THIS ITEM. IDENTAL TO THE		SE 5		ES - 2
E INSTALLED ON EACH		ORT - PHASI		ITON
BLE FOR MAINTAINING SATISFACTION OF THE		IS IS		Z
CCESS BY VEHICLES ON E A ROPE/CABLE IE ROPE/CABLE WILL 1 IT TO INCRESE		NAL A LLINO FENCI	NORTHWEST AREA	Y PL/
CCESS BY VEHICLES ON EAST ONE (1) R11-2 RRICADE.		IATIO 3AN, I ETER	WEST	τινιτ
FORM HIS WORK SO AS PROGRESS, WORK OR IRACTORS (SEE SPECIAL IME CONTRACTOR WILL ONSTRUCTION LL ON-SITE IT IS ANTICIPATED THE ER CONSTRUCTION T. NO ADDITIONAL ED FOR ANY EFFORTS		WAUKEGAN NATIONAL AIRPORT WAUKEGAN, ILLINOIS CONSTRUCT PERIMETER FENCING - PH	(NORT	CONSTRUCTION ACTIVITY PLAN NOTES
AXIWAY SITE DUE TO	-	ń		
ACTOR		CAPT Compared to the compared of the compared		APA
G - PHASE 1 AND 2		© copyrig TILLY 3S		NON
		PHY &	0613	LI II
.65 MHz			184-00	AZA
ONSTRUCTION			e No	X
POSITION - 25'			Licens	
DPOSES TO UTILIZE TALLER THAN WHAT IS		7		\mathbf{b}
RESPONSIBLE TO SUBMIT OVAL. THE RESIDENT		DESIGN BY:		AM
ORT INFORMATION FOR		DRAWN BY:		JRO
		CHECKED BY:		AM
	ŀ	APPROVED BY		ARM
	-	DATE: JOB No:		4/16/2021
			INA	
	-	SHEET 6	OF	3 SHEETS
		SHEET 6	, 57 ;	STIEL 13

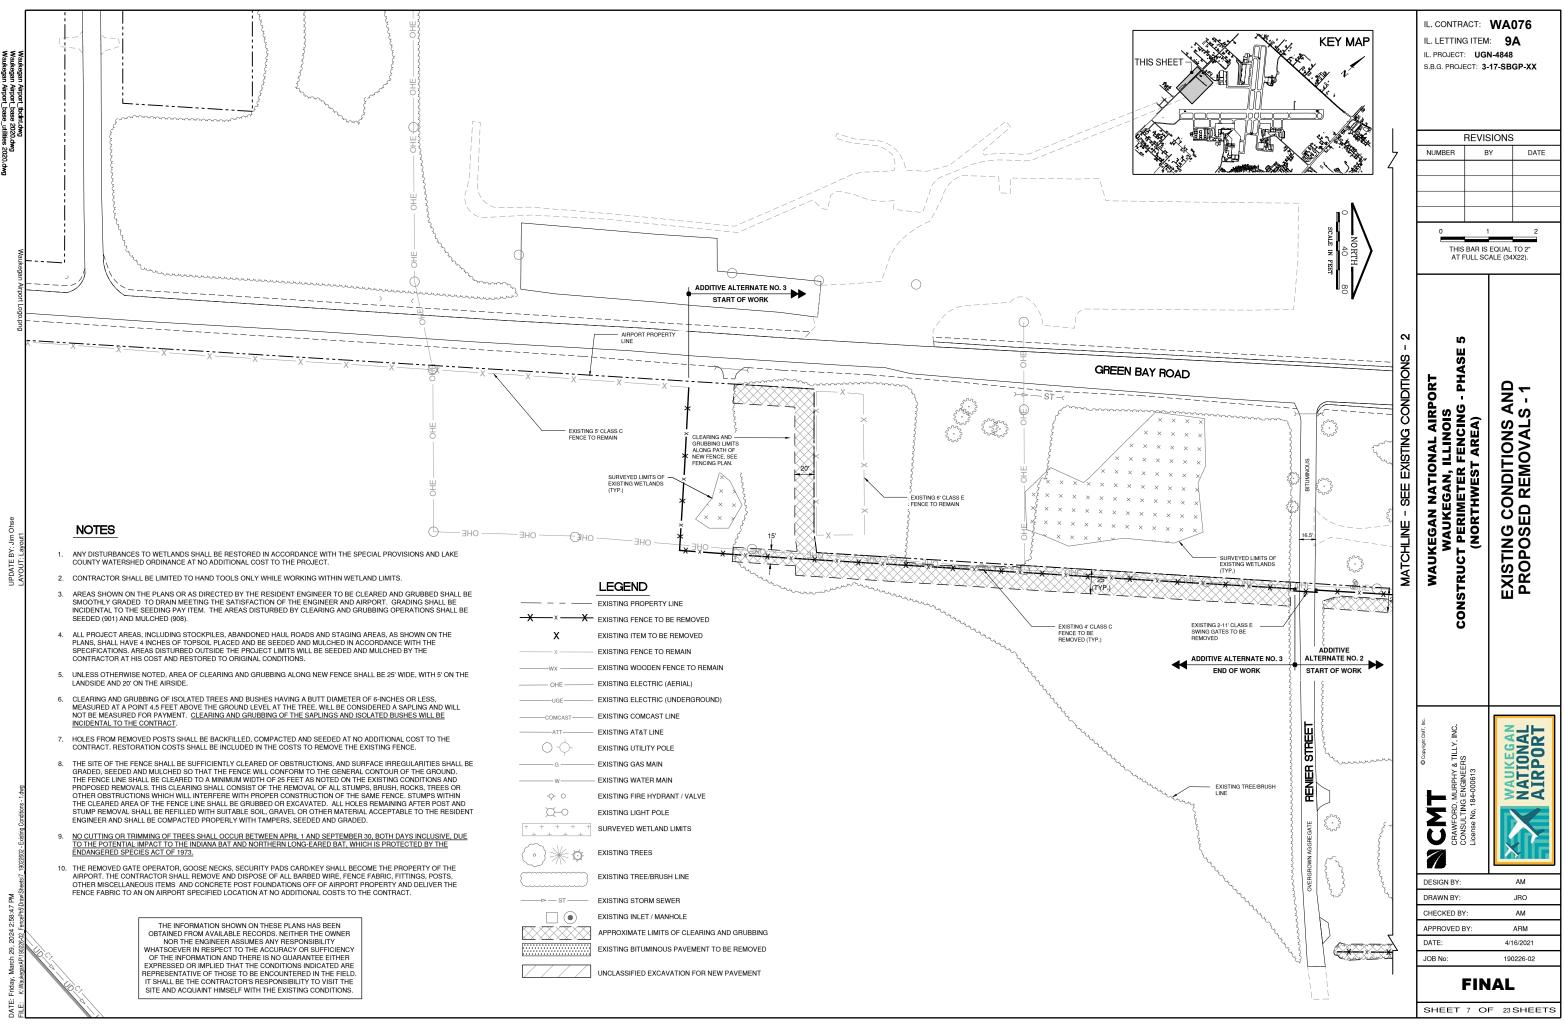

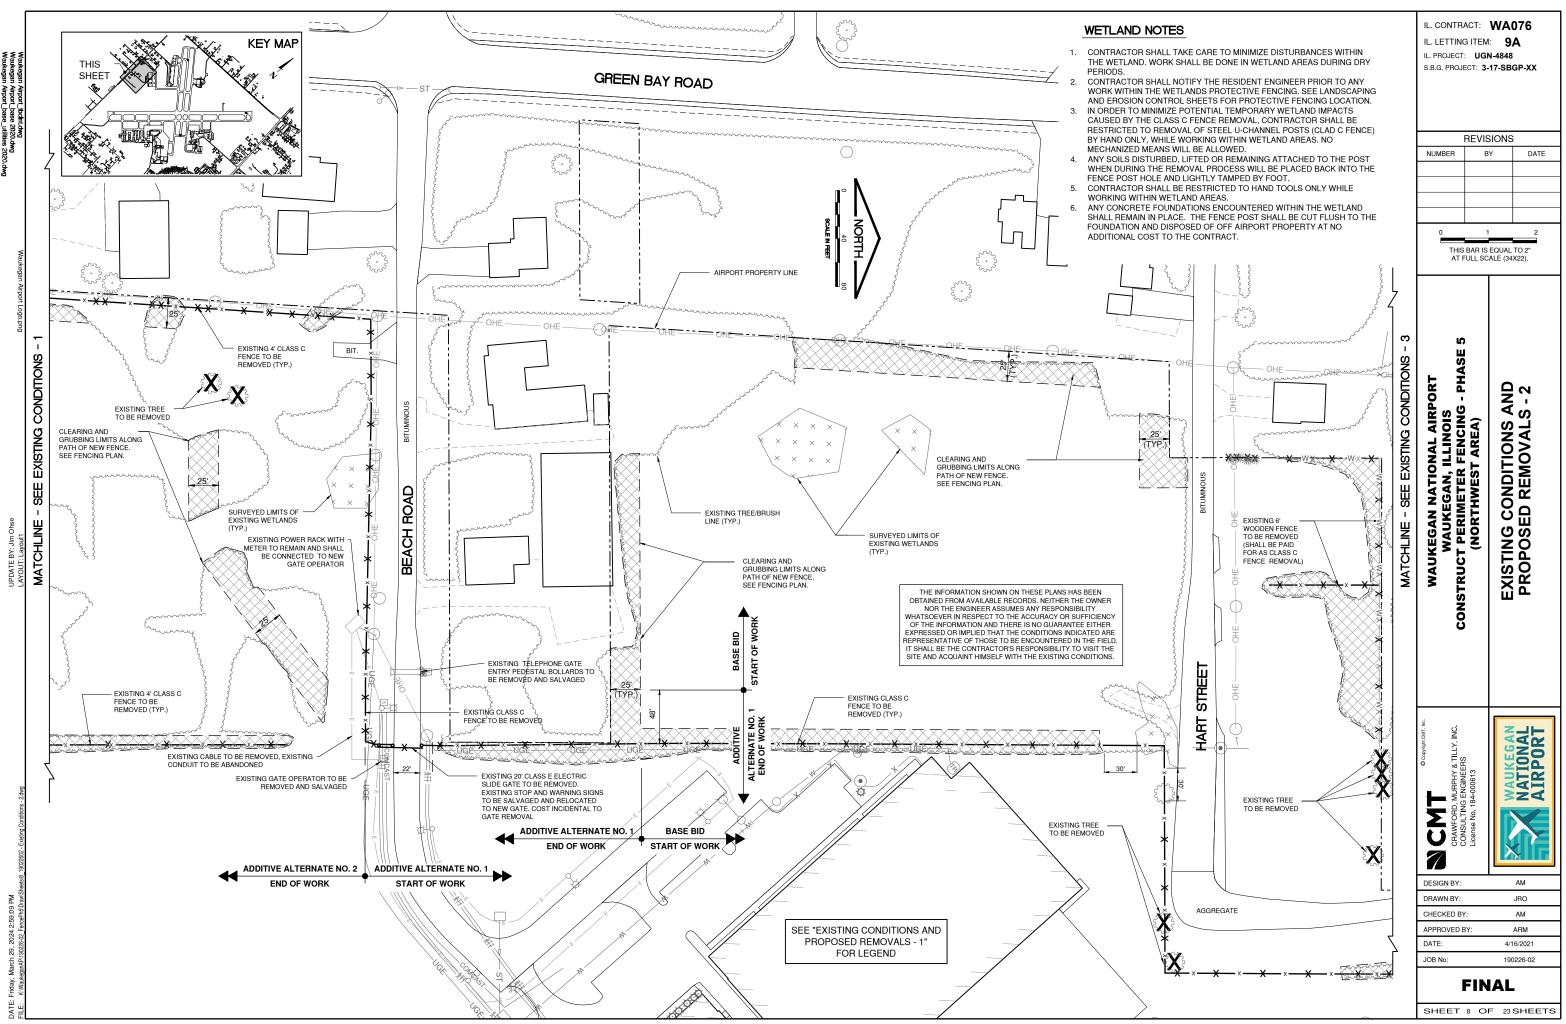


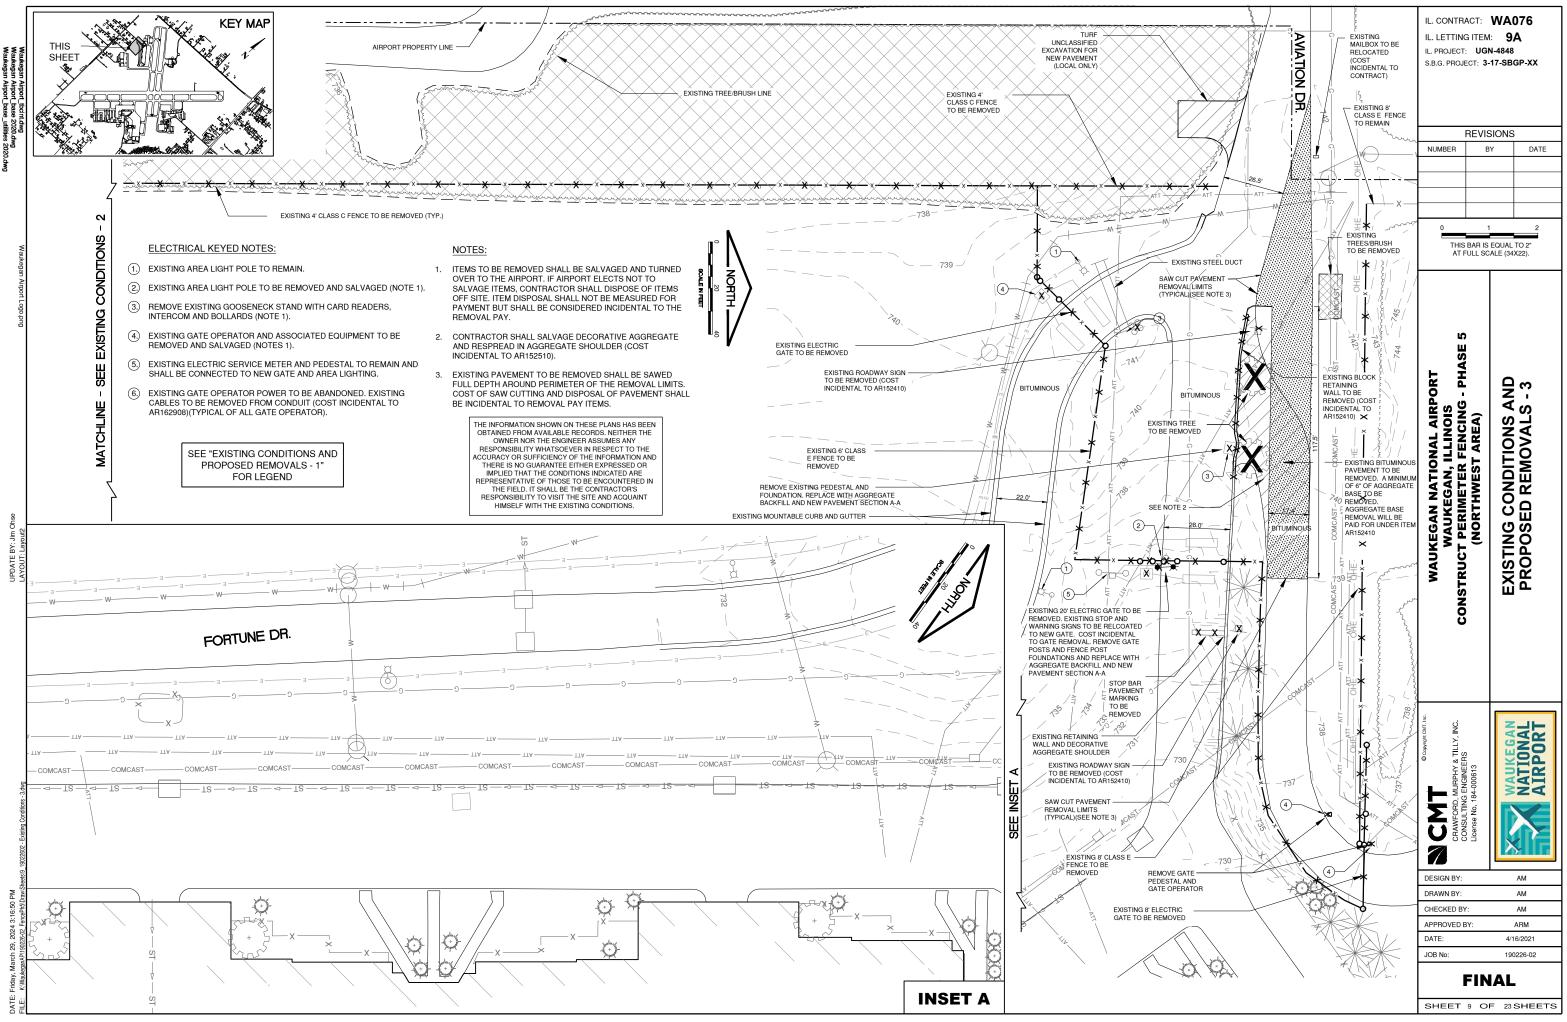




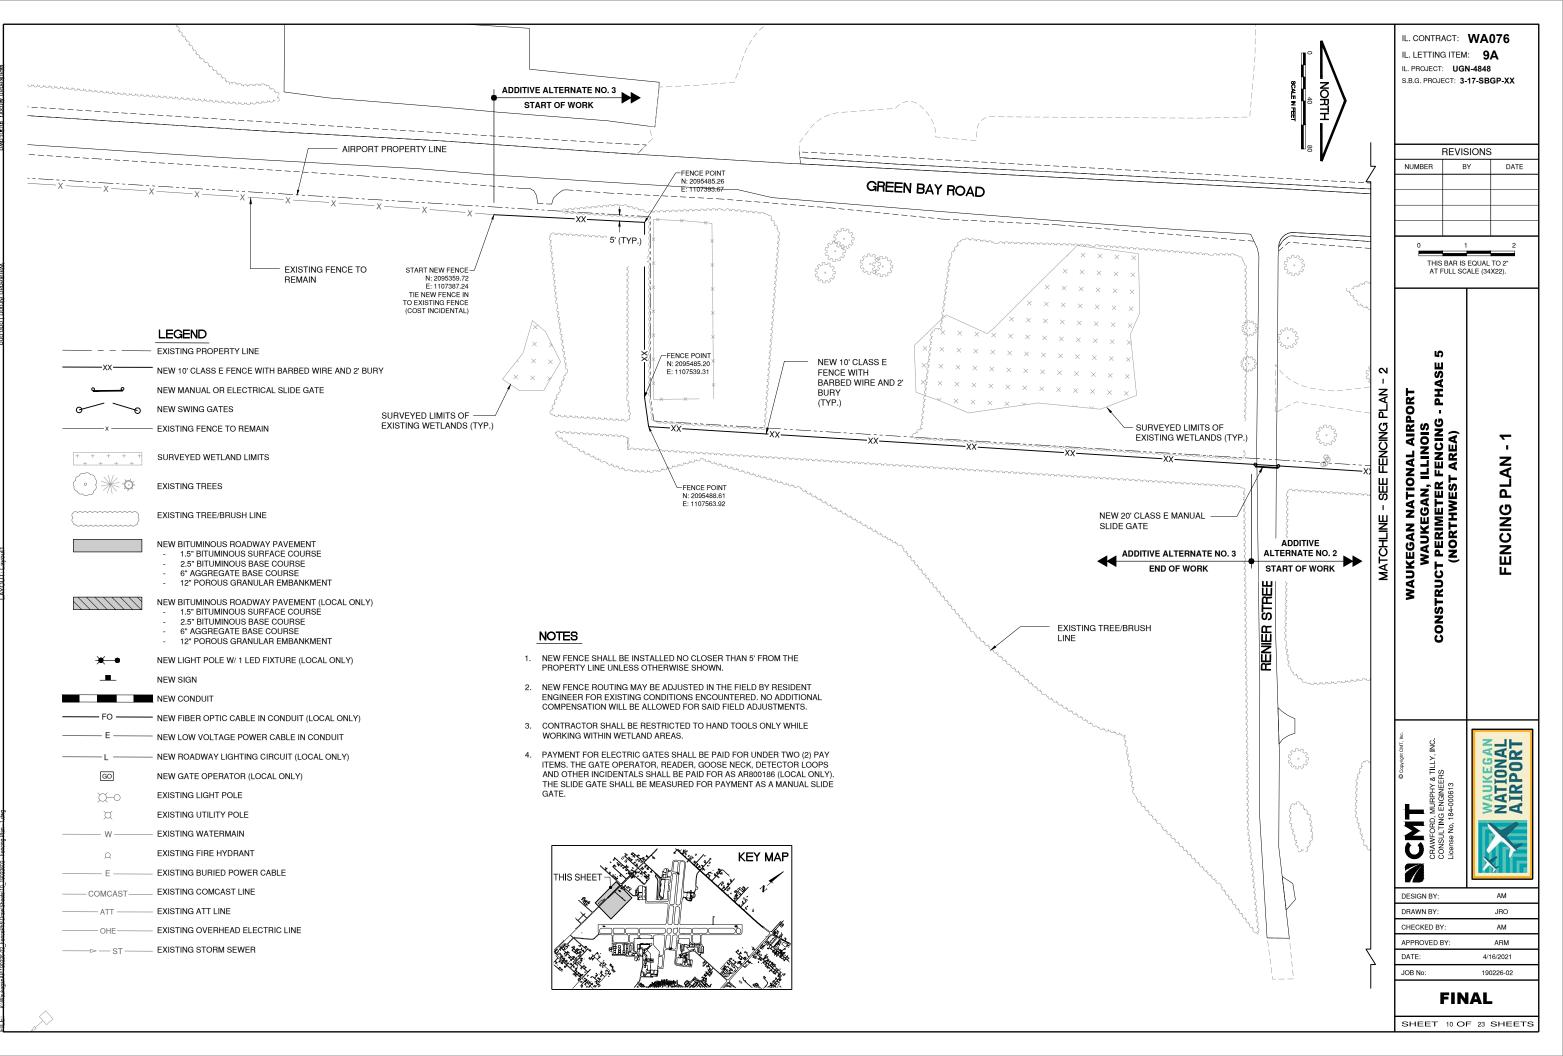



UPDATE BY: Jim Ohs

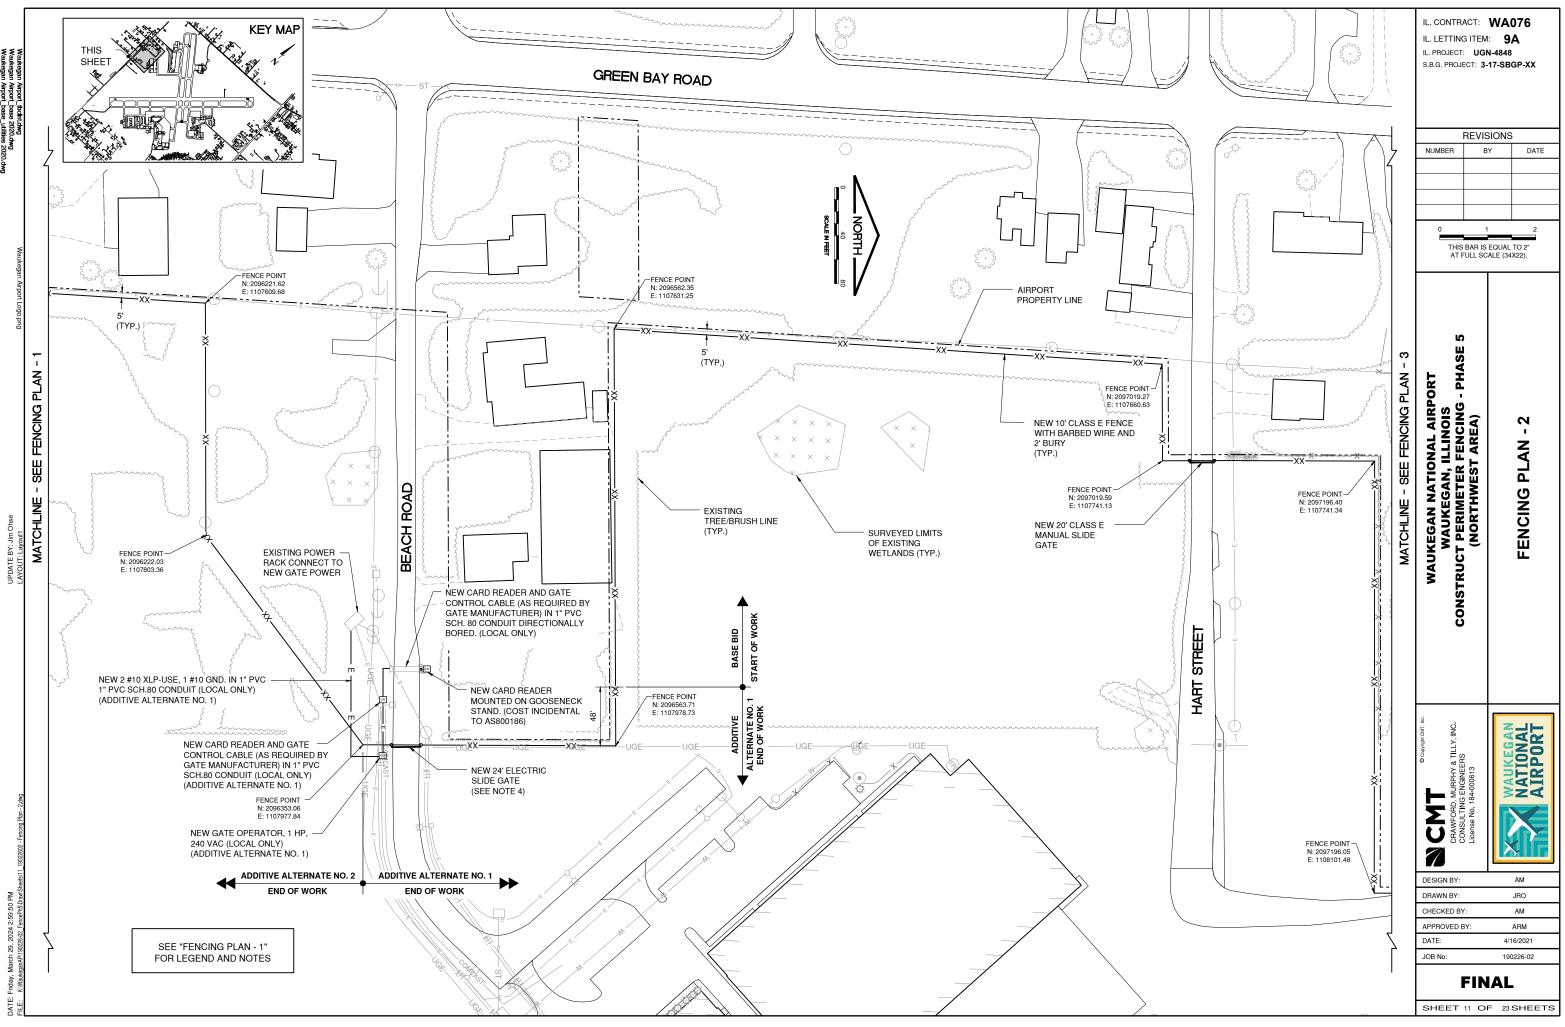


Waukegan Airport_tbcht.dwg Waukegan Airport_base 2020.dwg Waukegan Airport_base_utilities 2020.dwg

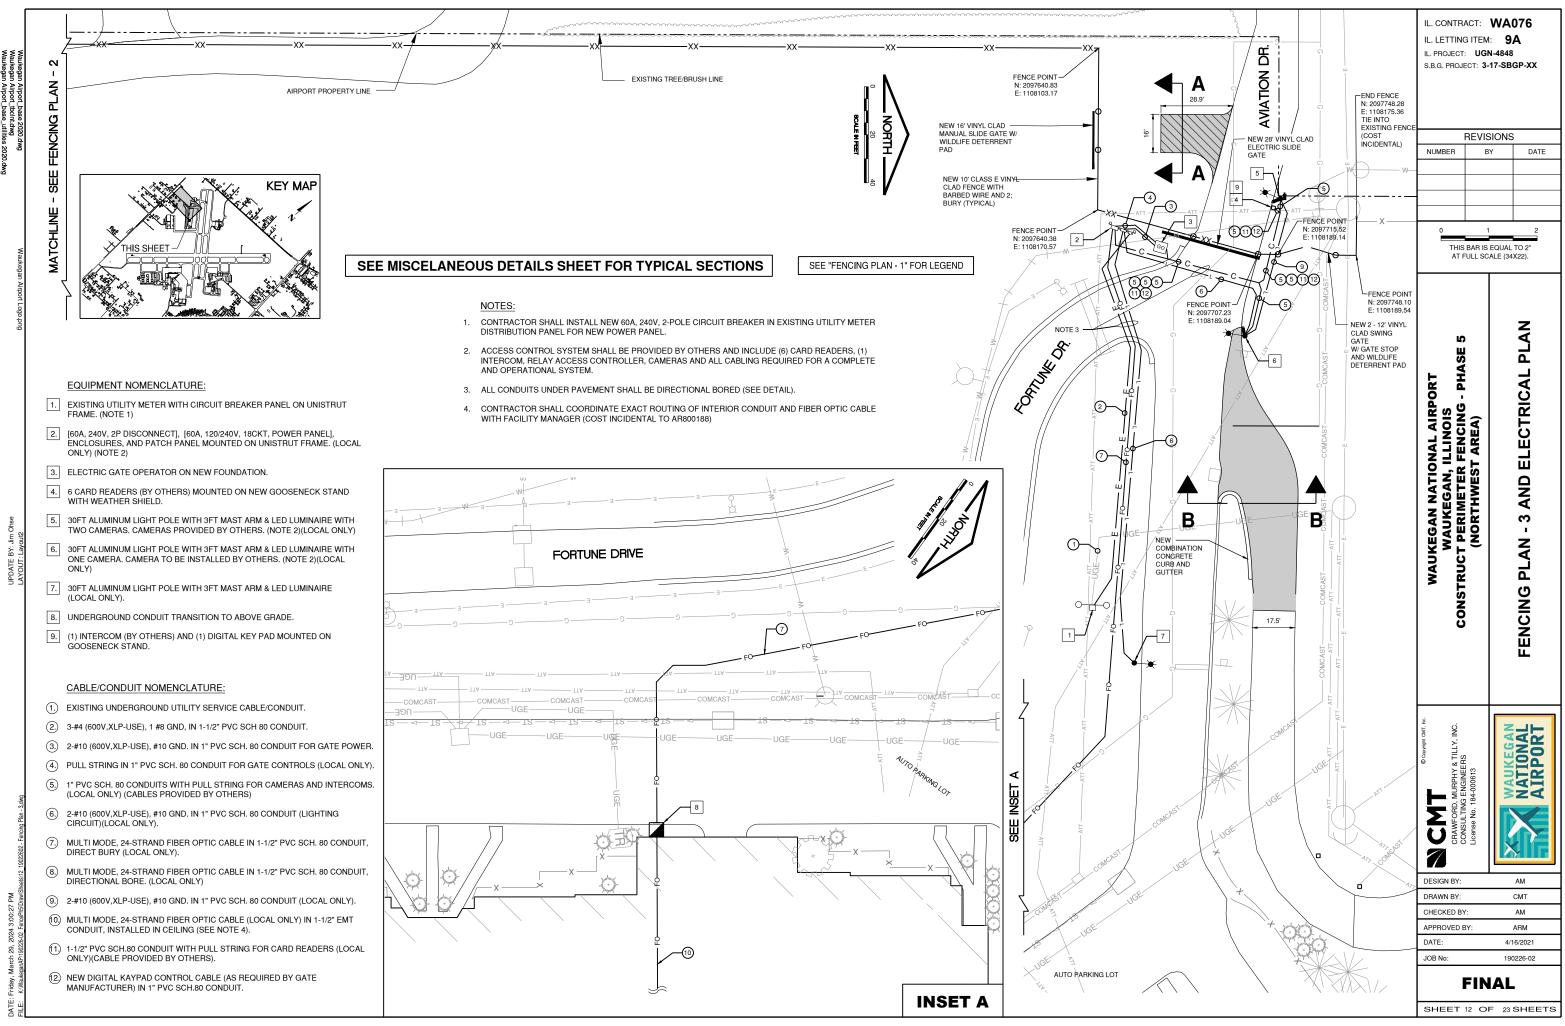

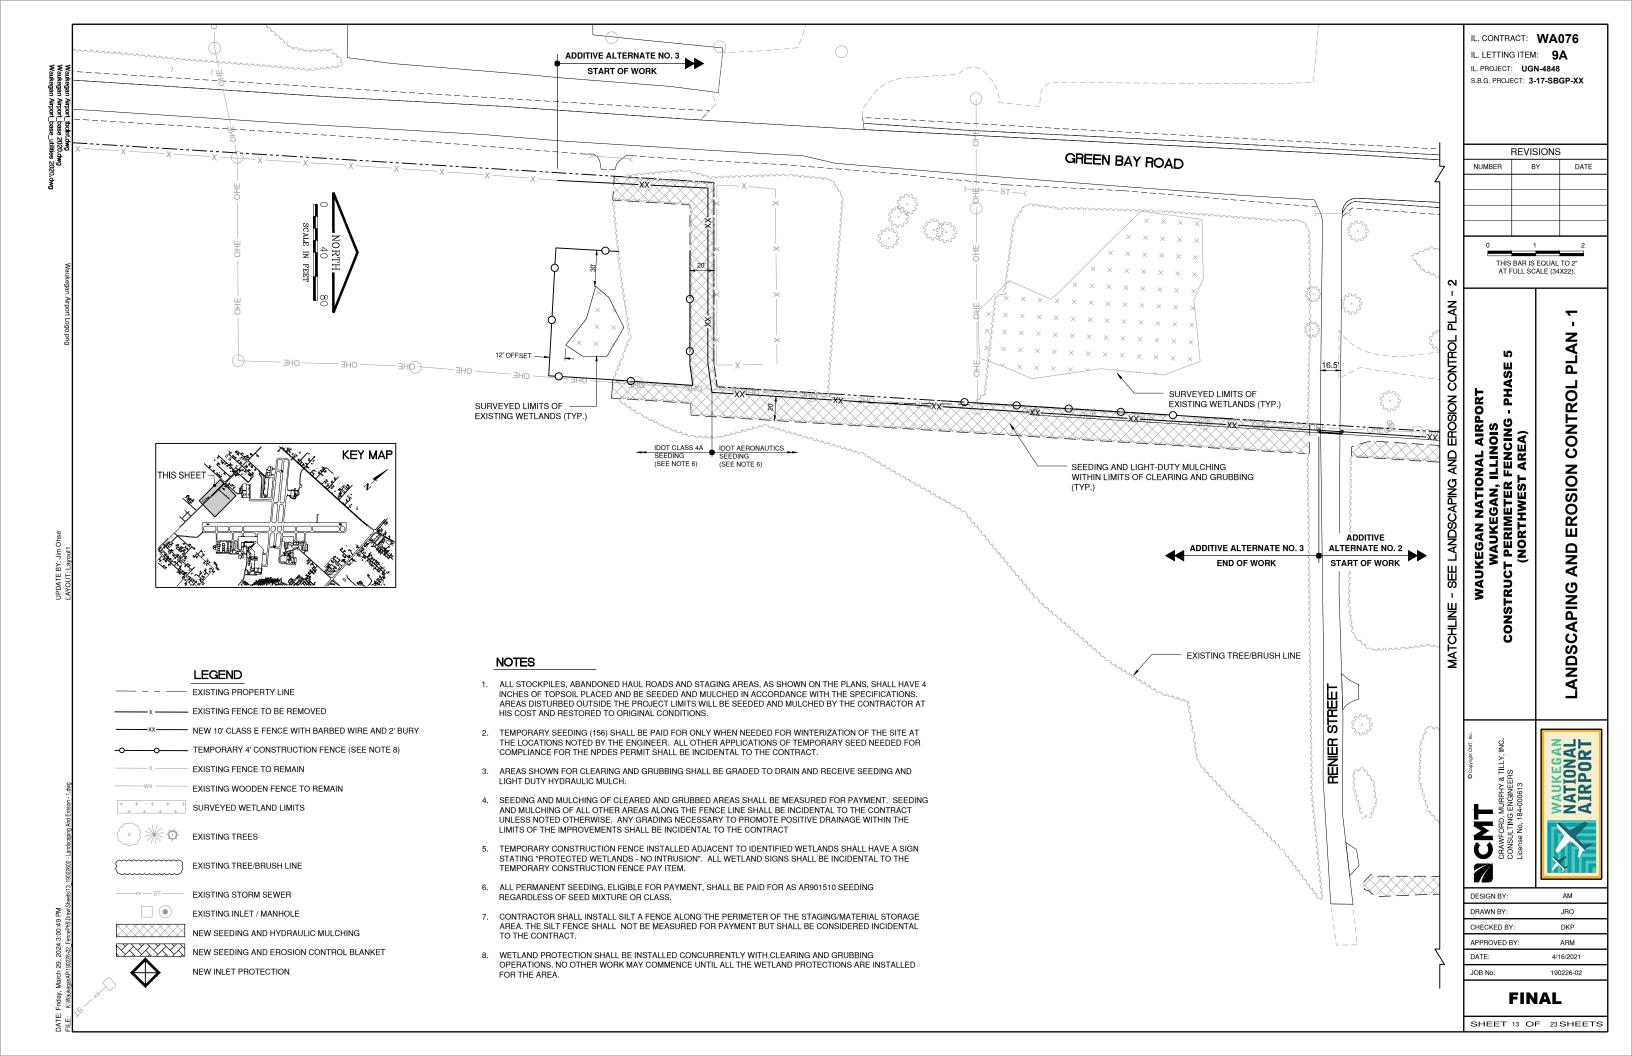

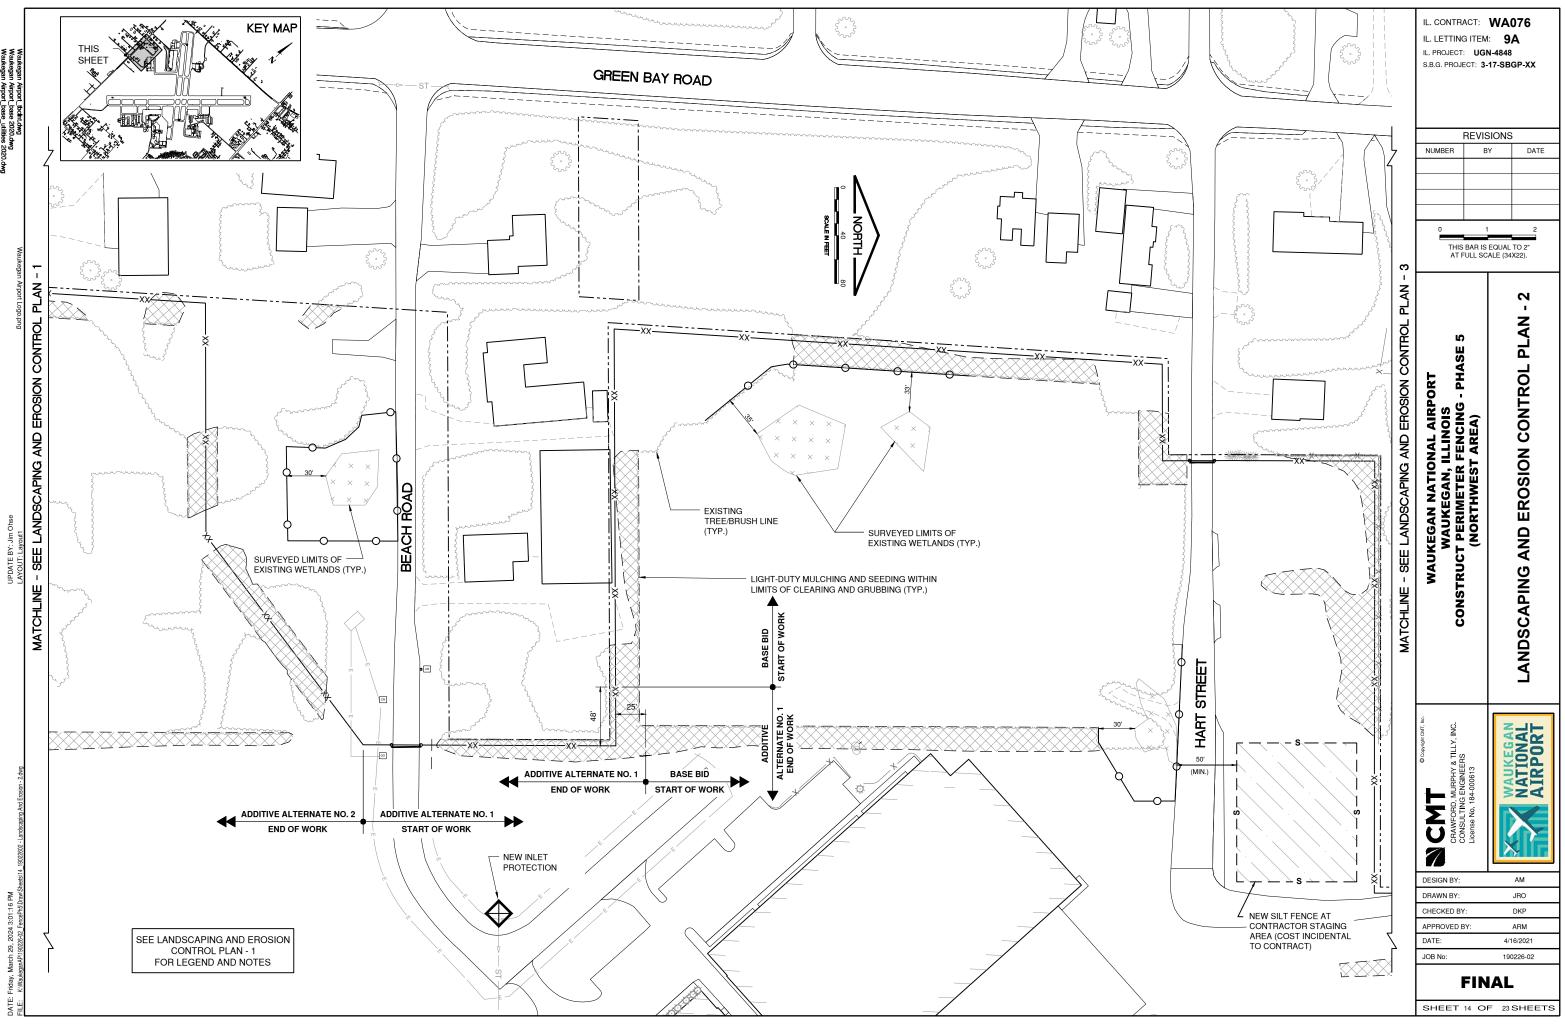

Waukegan Airport_tbcht.dwg Waukegan Airport_base 2020.dwg Waukegan Airport_base_utilities 2020.dwg

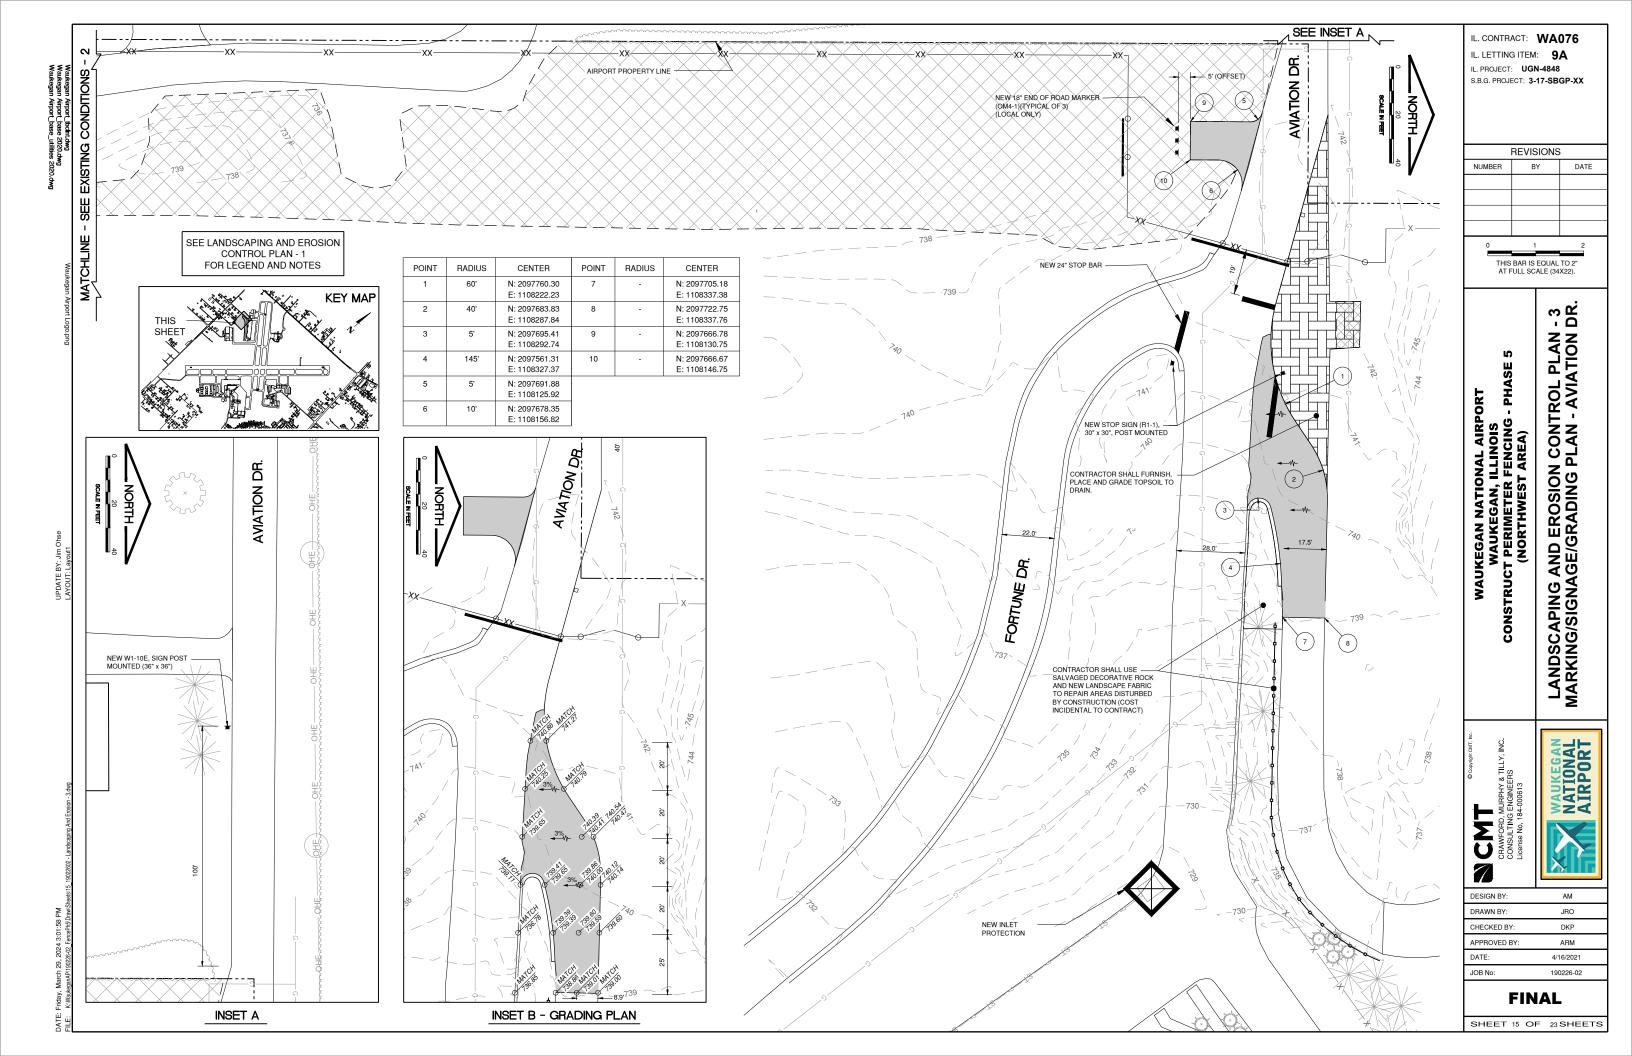

STORM WATER POLLUTION PREVENTION PLAN

THE FOLLOWING PLAN IS ESTABLISHED AND INCORPORATED IN THE PROJECT TO DIRECT THE CONTRACTOR IN THE PLACEMENT OF TEMPORARY EROSION CONTROL SYSTEMS AND TO PROVIDE A STORM WATER POLLUTION PREVENTION PLAN FOR COMPLIANCE WITH NPDES

THE PURPOSE OF THIS PLAN IS TO MINIMIZE EROSION WITHIN THE CONSTRUCTION SITE AND TO LIMIT SEDIMENTS FROM LEAVING THE SITE BY UTILIZING PROPER TEMPORARY EROSION CONTROL SYSTEMS AND PROVIDING GROUND COVER WITHIN A REASONABLE AMOUNT OF TIME

CERTAIN EROSION CONTROL FACILITIES SHALL BE INSTALLED BY THE CONTRACTOR AT THE BEGINNING OF CONSTRUCTION. OTHER ITEMS SHALL BE INSTALLED BY THE CONTRACTOR AS DIRECTED BY THE ENGINEER ON A CASE BY CASE SITUATION. DEPENDING ON THE CONTRACTOR'S SEQUENCE OF ACTIVITIES, TIME OF YEAR, AND EXPECTED WEATHER CONDITIONS.

THE CONTRACTOR SHALL INSTALL PERMANENT EROSION CONTROL SYSTEMS AND SEEDING WITHIN A TIMEERAME SPECIFIED THE CONTRACTOR STALL INSTALL FERMINATION FERSION CONTROL STOTEMS AND SEEDING WITH A TIME THRANE OF EXPLICIT HEREIN AND AS DIRECTED BY THE ENGINEER, THEREFORE MINIMIZING THE AMOUNT OF AREA SUSCEPTIBLE TO EROSION AND REDUCING THE AMOUNT OF TEMPORARY SEEDING, WHICH WILL BE THE CONTRACTOR'S COST. THE ENGINEER WILL DETERMINE IF ANY TEMPORARY EROSION CONTROL SYSTEMS SHOWN IN THE PLAN CAN BE DELETED AND IF ANY ADDITIONAL TEMPORARY EROSION CONTROL SYSTEMS, WHICH ARE NOT INCLUDED IN THIS PLAN, SHALL BE ADDED. THE CONTRACTOR SHALL PERFORM ALL WORK AS DIRECTED BY THE ENGINEER AND AS SHOWN ON THE PLANS.

SITE DESCRIPTION

THE FOLLOWING IS A DESCRIPTION OF THE CONSTRUCTION ACTIVITY WHICH IS THE SUBJECT OF THIS PLAN.

THIS PROJECT CONSISTS OF CONSTRUCTING A NEW 10' SECURITY FENCE WITH A 2' BURIED WILDLIFE FENCING. DRAINAGE CLEARING AND GRUBBING, INTERSECTION SECTION IMPROVEMENTS AT WAUKEGAN NATIONAL AIRPO

THE FOLLOWING IS A DESCRIPTION OF THE INTENDED SEQUENCE OF MAJOR ACTIVITIES WHICH WILL DISTURB SOILS FOR MAJOR PORTIONS OF THE CONSTRUCTION SITE, SUCH AS EXCAVATION AND GRADING

- 1. COMPLETE CLEARING AND GRUBBING.
- 2. INSTALL WETLAND PROTECTION FENCING
- 3. INSTALL AND MAINTAIN TEMPORARY EROSION CONTROL MEASURES.
- 4. REMOVE EXISTING FENCE.
- 5. CONSTRUCT TEMPORARY CONCRETE WASHOUT
- 6. INSTALL THE NEW FENCE POSTS AND DETERRENT FENCE EXCAVATION.
- INSTALL NEW FENCE IMPROVEMENTS.
- 8. REMOVE EXISTING PAVEMENT
- 9. EXCAVATION FOR NEW PAVEMENT.
- 10. INSTALL UNDERGROUND UTILITIES.
- 11. CONSTRUCT NEW HMA PAVEMENT
- 12. INSTALL NEW GATES
- 13. COMPLETE ELECTRICAL IMPROVEMENTS.
- 14. FINAL GRADING AND OTHER MISCELLANEOUS ITEMS.
- 15. PLACEMENT OF PERMANENT EROSION CONTROL, SUCH AS SEEDING AND BLANKET

AREA OF CONSTRUCTION SITE

THE TOTAL AREA OF THE CONSTRUCTION SITE IS ESTIMATED TO BE 8.5 ACRES OF WHICH 3.4 ACRES WILL BE DISTURBED BY EXCAVATION, GRADING, CLEARING AND GRUBBING AND OTHER ACTIVITIES.

HER REPORTS, STUDIES AND PLANS WHICH AID IN THE DEVELOPMENT OF THE STORM WATER POLLUTION PREVENTION PLAN AS REFERENCED DOCUMENTS

- INFORMATION OF THE SOILS AND TERRAIN WITHIN THE SITE WAS OBTAINED FROM TOPOGRAPHIC SURVEYS AND SOIL BORINGS THAT WERE UTILIZED FOR THE DEVELOPMENT OF THE PROPOSED TEMPORARY EROSION CONTROL SYSTEMS
- PROJECT PLAN DOCUMENTS, SPECIFICATION AND SPECIAL PROVISIONS, AND PLAN DRAWINGS INDICATING DRAINAGE PATTERNS AND APPROXIMATE SLOPES ANTICIPATED AFTER GRADING ACTIVITIES WERE UTILIZED FOR THE PROPOSED PLACEMENT OF THE TEMPORARY EROSION CONTROL SYSTEMS.

DRAINAGE TRIBUTARIES AND SENSITIVE AREAS RECEIVING RUNOFF FROM THIS CONSTRUCTION SITE

THE CONSTRUCTION LOCATED IN DES PLANES RIVER WATERSHED. THE SITE DRAINS THROUGH A SERIES OF OVERLAND FLOW ROUTES/STORM SEWER INTO THE SUBURBAN COUNTRY CLUB TRIBUTARY THAT OUTLET INTO ULTIMATELY THE DES PLAINES BIVER

SEDIMENTATION AND EROSION CONTROL NOTES

THE SOIL EROSION AND SEDIMENT CONTROL PRACTICES WILL BE INSPECTED WEEKLY AND AFTER 1/2 INCH OF RAIN OR MORE BY THE RESIDENT ENGINEER.

ALL SOIL EROSION AND SEDIMENT CONTROL PRACTICES ARE REFERENCED FROM THE ILLINOIS URBAN MANUAL. UNLESS OTHERWISE STATED.

THE DRAWINGS, SPECIFICATIONS AND SPECIAL PROVISIONS WILL ENSURE THAT EXISTING VEGETATION IS PRESERVED WHERE ATTAINABLE AND DISTUBBED PORTIONS OF THE SITE WILL BE STABILIZED. STABILIZATION PRACTICES INCLUDE SEEDING AND MULCHING AS DIRECTED BY THE ENGINEER. STABILIZATION MEASURES SHALL BE INITIATED AS SOON AS POSSIBLE IN PORTIONS OF THE SITE WHERE CONSTRUCTION ACTIVITIES HAVE TEMPORARILY OR PERMANENTLY CEASED, BUT IN NO CASE MORE THAN 7 DAYS AFTER THE CONSTRUCTION ACTIVITY IN THAT PORTION OF THE SITE HAS TEMPORARILY OR PERMANENTLY CEASED.

AS SOON AS REASONABLE ACCESS IS AVAILABLE TO ALL LOCATIONS WHERE WATER DRAINS AWAY FROM THE PROJECT, INLET PROTECTION AND PERIMETER SILT FENCE SHALL BE INSTALLED AS CALLED OUT IN THE PLANS OR AS DIRECTED BY THE ENGINEER

THIS PLAN HAS BEEN PREPARED TO COMPLY WITH THE PROVISIONS OF THE NPDES PERMIT NUMBER ILR10, ISSUED BY THE ILLINOIS ENVIRONMENTAL PROTECTION AGENCY FOR STORM WATER DISCHARGES FROM CONSTRUCTION SITE ACTIVITIES

DESCRIPTION OF STABILIZATION PRACTICES DURING CONSTRUCTION

DURING CONSTRUCTION, AREAS OUTSIDE THE CONSTRUCTION LIMITS AS OUTLINED PREVIOUSLY HEREIN SHALL BE PROTECTED THE CONTRACTOR SHALL NOT USE THIS AREA FOR STAGING (EXCEPT AS DESCRIBED ON THE PLANS AND DIRECTED BY THE ENGINEER), PARKING OF VEHICLES OR CONSTRUCTION EQUIPMENT, STORAGE OF MATERIALS, OR OTHER CONSTRUCTION BELATED ACTIVITIES.

- WITHIN THE CONSTRUCTION LIMITS, AREAS WHICH MAY BE SUSCEPTIBLE TO EROSION AS DETERMINED BY THE ENGINEER SHALL REMAIN UNDISTURBED UNTIL FULL SCALE CONSTRUCTION IS UNDERWAY TO PREVENT UNNECESSARY SOIL EROSION
- EARTH STOCKPILES SHALL BE TEMPORARILY SEEDED, AT THE CONTRACTORS EXPENSE, IF THEY ARE TO REMAIN UNUSED FOR MORE THAN FOURTEEN DAYS
- AS CONSTRUCTION PROCEEDS, THE CONTRACTOR SHALL INSTITUTE THE FOLLOWING AS DIRECTED BY THE ENGINEER: 2
- A. PLACE TEMPORARY EROSION CONTROL FACILITIES AT LOCATIONS SHOWN ON THE PLANS
- B. EXCAVATED AREAS AND EMBANKMENT AREAS SHALL BE PERMANENTLY SEEDED IMMEDIATELY AFTER FINAL GRADING. IF PORARILY SEEDED, AT THE CONTRACTOR'S COST, IF NO CONSTRUCTION ACTIVITY IN THE AREA IS PLANNED FOR SEVEN DAYS
- CONSTRUCTION EQUIPMENT SHALL BE STORED AND FUELED ONLY AT DESIGNATED LOCATIONS. ALL NECESSARY MEASURES SHALL BE TAKEN TO CONTAIN ANY FUEL OR POLLUTANT IN ACCORDANCE WITH EPA WATER QUALITY REGULATIONS. LEAKING EQUIPMENT OR SUPPLIES SHALL BE IMMEDIATELY REPAIRED OR REMOVED FROM THE SITE
- SEDIMENT COLLECTED DURING CONSTRUCTION OF THE VARIOUS TEMPORARY EROSION CONTROL SYSTEMS SHALL BE DISPOSED OF ON SITE ON A REGULAR BASIS AS DIRECTED BY THE ENGINEER. THE COST OF THIS MAINTENANCE SHALL BE INCLUDED IN THE UNIT BID PRICE FOR UNCLASSIFIED EXCAVATION AND EROSION CONTROL ITEMS.
- THE TEMPORARY EROSION CONTROL SYSTEMS SHALL BE REMOVED AS DIRECTED BY THE ENGINEER AFTER USE IS NO LONGER NEDED OR NO LONGER FUNCTIONING. THE COST OF THIS REMOVAL SHALL BE INCLUDED IN THE UNIT BID PRICE FOR VARIOUS TEMPORARY EROSION CONTROL PAY ITEMS.

DESCRIPTION OF STRUCTURAL PRACTICES AFTER FINAL GRADING

TEMPORARY EROSION CONTROL SYSTEMS SHALL BE LEFT IN PLACE WITH PROPER MAINTENANCE UNTIL PERMANENT EROSION CONTROL IS IN PLACE AND WORKING PROPERLY AND ALL PROPOSED TURF AREAS ARE SEEDED AND ESTABLISHED

ONCE PERMANENT EROSION CONTROL SYSTEMS AS PROPOSED IN THE PLANS ARE FUNCTIONAL AND ESTABLISHED, TEMPORARY ITEMS SHALL BE REMOVED, CLEANED UP, AND DISTURBED TURF RESEEDED.

MAINTENANCE AFTER CONSTRUCTION

CONSTRUCTION IS COMPLETE AFTER FINAL ACCEPTANCE BY THE ILLINOIS DIVISION OF AERONAUTICS. MAINTENANCE UP TO THIS DATE WILL BE REQUIRED BY THE CONTRACTOR

CONTRACTORS

- 1. THE STORM WATER POLITION PREVENTION PLAN MUST CLEARLY IDENTIFY FOR EACH MEASURE IDENTIFIED IN THE PLAN THE CONTRACTORS OR SUBCONTRACTORS THAT WILL IMPLEMENT THE MESURE. ALL CONTRACTORS AND SUBCONTRACTORS AND SUBCONTRACTORS IDENTIFIED IN THE PLAN MUST SIGN A COPY OF THE CERTIFICATION STATEMENT IN PARAGRAPH 2 BELOW IN ACCORDANCE WITH PART VI.G (SIGNATORY REQUIREMENTS) OF THIS PERMIT, ALL CERTIFICATIONS MUST BE INCLUDED IN THE STORM WATER POLLUTION PREVENTION PLAN EXCEPT FOR OWNERS THAT ARE ACTING AS
- CERTIFICATION STATEMENT, ALL CONTRACTORS AND SUBCONTRACTORS IDENTIFIED IN A STORM WATER POLLUTION PREVENTION PLAN IN ACCORDANCE WITH PARAGRAPH 1 ABOVE SHALL SIGN A COPY OF THE FOLLOWING CERTIFICATION STATEMENT BEFORE CONDUCTING ANY PROFESSIONAL SERVICE AT THE SITE IDENTIFIED IN THE STORM WATER POLI UTION PREVENTION PLAN
 - I CERTIFY UNDER PENALTY OF LAW THAT I UNDERSTAND THE TERMS AND CONDITIONS OF THE GENERAL NATIONAL POLI UTANT DISCHARGE FLIMINATION SYSTEM (NPDES) PERMIT (1) B10) THAT AUTHORIZES THE STORM WATER DISCHARGES ASSOCIATED WITH INDUSTRIAL ACTIVITY FROM THE CONSTRUCTION SITE IDENTIFIED AS PART OF THIS

THE CERTIFICATION MUST INCLUDE THE NAME AND TITLE OF THE PERSON PROVIDING THE SIGNATURE IN ACCORDANCE WITH PART VI.G OF THIS PERMIT: THE NAME, ADDRESS AND TELEPHONE NUMBER OF THE CONTRACTING FIRM; THE ADDRESS (OR OTHER IDENTIFYING DESCRIPTION) OF THE SITE: AND THE DATE THE CERTIFICATION IS MADE.

CONTRACTOR CERTIFICATION STATEMENT

THIS CERTIFICATION STATEMENT IS A PART OF THE STORM WATER POLILITION PREVENTION PLAN FOR THE PROJECT DESCRIBED BELOW IN ACCORDANCE WITH NPDES PERMIT NO. ILR10 ISSUED BY THE ILLINOIS ENVIRONMENTAL PROTECTION AGENC

MARKED: CONSTRUCT PERIMETER FENCING - PHASE 5 (NORTHWEST AREA)

PROJECT INFORMATION

ROUTE: WAUKEGAN NATIONAL AIRPORT

PROJECT NUMBER: UGN-4848 SECTION: 31 CONTRACT NUMBER: 3-17-SBGP-156/152

COUNTY: LAKE

I CERTIEV UNDER PENALTY OF LAW THAT I UNDERSTAND THE TERMS AND CONDITIONS OF THE GENERAL NATIONAL POLITION DISCHARGE ELIMINATION SYSTEM (NPDES) PERMIT (ILENIO) THAT LONDERSTAND CONDITIONS OF THE GENERAL INATIONAL POLIDION DISCHARGE ELIMINATION SYSTEM (NPDES) PERMIT (ILENIO) THAT AUTHORIZES THE STORM WATER DISCHARGES ASSOCIATED WITH INDUSTRIAL ACTIVITY FROM THE CONSTRUCTION SITE IDENTIFIED AS PART OF THIS CERTIFICATION.

SIGNATURE: DATE: TITLE: PRINTED NAME:

NAME OF FIRM:

STREET ADDRESS:

CITY, STATE, ZIP: PHONE NUMBER:

THE INFORMATION WITHIN THIS BOX SHALL BE COMPLETED BY THE CONTRACTOR AFTER THE AWARD OF THE CONTRACT TO OBTAIN THE REQUIRED NPDES PERMIT FROM IEPA. COMPLETION OF THIS IS A CONTRACT REQUIREMENT

ADDITIONAL NOTES

- THE OWNER FOR REVIEW AND INCLUSION INTO SWPPP.
- 2. STORMWATER STRUCTURES IS PROHIBITED.
- TO THE CONTRACT.

LAKE COUNTY STORMWATER MANAGEMENT COMMISSION SOIL EROSION AND SEDIMENT CONTROL CONSTRUCTION NOTES

- DISTURBANCE OF UPLAND AREAS.
- INSPECTIONS AND DOCUMENTATION SHALL BE PERFORMED, AT A MINIMUN
- GRADING
- OR LIQUID EQUIVALENT PRECIPITATION.
- APPROPRIATE SOIL EROSION AND SEDIMENT CONTROL MEASURES

- PLACED IN FLOOD PRONE AREAS OR WETLANDS AND DESIGNATED BUFFERS
- ENFORCEMENT OFFICE
- L.
- APPROPRIATE SEDIMENT CONTROL MEASURE
- REQUIRED BY THE ENFORCEMENT OFFICER.

- GOVERNING AGENCY.

PRIOR TO COMMENCING DEWATERING ACTIVITIES AND LAND DISTURBING ACTIVITIES IN AREAS OTHER THAN THIGH TO COMMENSION DEVELOPMENT AND CALIFORNIA AND A COMPACT AND A COMPA

DURING DEWATERING OPERATION, WATER SHALL BE PUMPED FROM A SUMP PIT INTO SEDIMENT BASINS OR SILT TRAPS OR OTHER APPROVED BMP. COSTS OF SUMP PITS, SEDIMENT BASINS AND SILT TRAPS AND OTHER BMP ARE INCIDENTAL TO THE DEWATERING PAY ITEM. DEWATERING DIRECTLY INTO FIELD TILES OR

3 LINEESS OTHERWISE INDICATED ALL VEGETATIVE AND STRUCTURAL EROSION AND SEDIMENT CONTROL PRACTICES SHALL BE CONSTRUCTED ACCORDING TO MINIMUM STANDARDS AND SPECIFICATIONS IN THE ILLINOIS URBAN MANUAL CURRENT EDITION FOUND AT ILLINOISMANUAL.ORG.

4 WINTER SHUTDOWN SHALL BE ADDRESSED FABLY IN THE FALL GROWING SEASON SO THAT SLOPES AND OTHER BARE EARTH AREAS MAY BE STABILIZED WITH TEMPORARY AND OR PERMANENT VEGETATIVE COVER FOR PROPER EROSION AND SEDIMENT CONTROL. TEMPORARY SEEDING (156) SHALL BE PAID FOR ONLY WHEN NEEDED FOR WINTERIZATION OF THE SITE AT THE LOCATIONS NOTED BY THE ENGINEER. ALL OTHER APPLICATIONS OF TEMPORARY SEED NEEDED FOR COMPLIANCE FOR THE NPDES PERMIT SHALL BE INCIDENTAL

A. SEDIMENT CONTROL MEASURES SHALL BE INSTALLED PRIOR TO THE COMMENCEMENT OF HYDROLOGIC

B. FOR THOSE DEVELOPMENTS THAT REQUIRE A DESIGNATED EROSION CONTROL INSPECTOR (DECI),

UPON COMPLETION OF SEDIMENT AND RUNOFF CONTROL MEASURES (INCLUDING PERIMETER CONTROLS AND DIVERSIONS), PRIOR TO PROCEEDING WITH ANY OTHER EARTH DISTURBANCE OR

AFTER EVERY SEVEN (7) CALENDAR DAYS OR STORM EVENT WITH GREATER THAN 0.5 INCH OF RAINFALL

C. SOIL DISTURBANCE SHALL BE CONDUCTED IN SUCH A MANNER AS TO MINIMIZE EROSION. IF STRIPPING CLEARING, GRADING, OR LANDSCAPING ARE TO BE DONE IN PHASES, THE PERMITTEE SHALL PLAN FOR

A STABILIZED MAT OF CRUSHED STONE MEETING IDOT GRADATION CA 1 UNDERLAIN WITH FILTER FABRIC AND IN ACCORDANCE WITH THE ILLINOIS URBAN MANUAL, OR OTHER APPROPRIATE MEASURE(S) AS APPROVED BY THE ENFORCEMENT OFFICER, SHALL BE INSTALLED AT ANY POINT WHERE TRAFFIC WILL BE ENTERING OR LEAVING A CONSTRUCTION SITE. SEDIMENT OR SOIL REACHING AN IMPROVED PUBLIC RIGHT OF WAY STREET, ALLEY OR PARKING AREA SHALL BE REMOVED BY SCRAPING OR STREET CLEANING AS ACCUMULATIONS WARBANT AND TRANSPORTED TO A CONTROLLED SEDIMENT DISPOSAL AREA.

E. TEMPORARY DIVERSIONS SHALL BE CONSTRUCTED AS NECESSARY TO DIRECT ALL RUNOFF FROM HYDROLOGICALLY DISTURBED AREAS TO AN APPROPRIATE SEDIMENT TRAP OR BASIN

DISTURBED AREAS SHALL BE STABILIZED WITH TEMPORARY OR PERMANENT MEASURES WITHIN SEVEN (7) CALENDAR DAYS FOLLOWING THE END OF ACTIVE HYDROLOGIC DISTURBANCE OR REDISTURBANCE.

G. ALL STOCKPILES SHALL HAVE APPROPRIATE MEASURES TO PREVENT EROSION, STOCKPILES SHALL NOT BE

H SLOPES STEEPER THAN 3H11V SHALL BE STABILIZED WITH APPROPRIATE MEASURESAS APPROVED BY THE

APPROPRIATE EROSION CONTROL BLANKET SHALL BE INSTALLED ON ALL INTERIOR DETENTION BASIN SIDE SLOPES BETWEEN THE NORMAL WATER LEVEL AND HIGH WATER LEVEL

J. STORM SEWERS THAT ARE OR WILL BE FUNCTIONING DURING CONSTRUCTION SHALL BE PROTECTED BY AN


IF DEWATERING SERVICES ARE USED, ADJOINING PROPERTIES AND DISCHARGE LOCATIONS SHALL BE PROTECTED FROM FROSION AND SEDIMENTATION, DISCHARGES SHALL BE ROUTED THROUGH AN APPROVED. ANIONIC POLYMER DEWATERING SYSTEM OR A SIMILAR MEASURE AS APPROVED BY THE ENFORCEMENT OFFICER. DEWATERING SYSTEMS SHOULD BE INSPECTED DAILY DURING OPERATIONAL PERIODS. THE ENFORCEMENT OFFICER. OR APPROVED REPRESENTATIVE, MUST BE PRESENT AT THE COMMENCEMENT OF DEWATEBING ACTIVITIES IF INSTALLED SOIL EBOSION AND SEDIMENT CONTROL MEASURES DO NOT MINIMIZE SEDMENT LEAVING THE DEVELOPMENT SITE, ADDITIONAL MEASURES SUCH AS ANIONIC POLYMERS OR FILTRATION SYSTEMS MAY BE REQUIRED BY THE ENFORCEMENT OFFICER.


IF INSTALLED SOIL EROSION AND SEDIMENT CONTROL MEASURES DO NOT MINIMIZE SEDIMENT LEAVING THE DEVELOPMENT SITE, ADDITIONAL MEASURES SUCH AS ANIONIC POLYMERS OR FILTRATION SYSTEMS MAY BE

M. ALL TEMPORARY AND PERMANENT EROSION CONTROL MEASURES MUST BE MAINTAINED AND REPAIRED AS NEEDED. THE PROPERTY OWNER SHALL BE ULTIMATELY RESPONSIBLE FOR MAINTENANCE AND REPAIR.


ALL TEMPORARY SEDIMENT CONTROL MEASURES SHALL BE REMOVED WITHIN 30 DAYS AFTER FINAL SITE STABILIZATION IS ACHIEVED OR AFTER THE TEMPORARY MEASURES ARE NO LONGER NEEDED.

O. THE EBOSION CONTROL MEASURES INDICATED ON THE PLANS ARE THE MINIMUM REQUIREMENTS, ADDITIONAL MEASURES MAY BE REQUIRED, AS DIRECTED BY THE ENGINEER, ENFORCEMENT OFFICER, OR OTHER




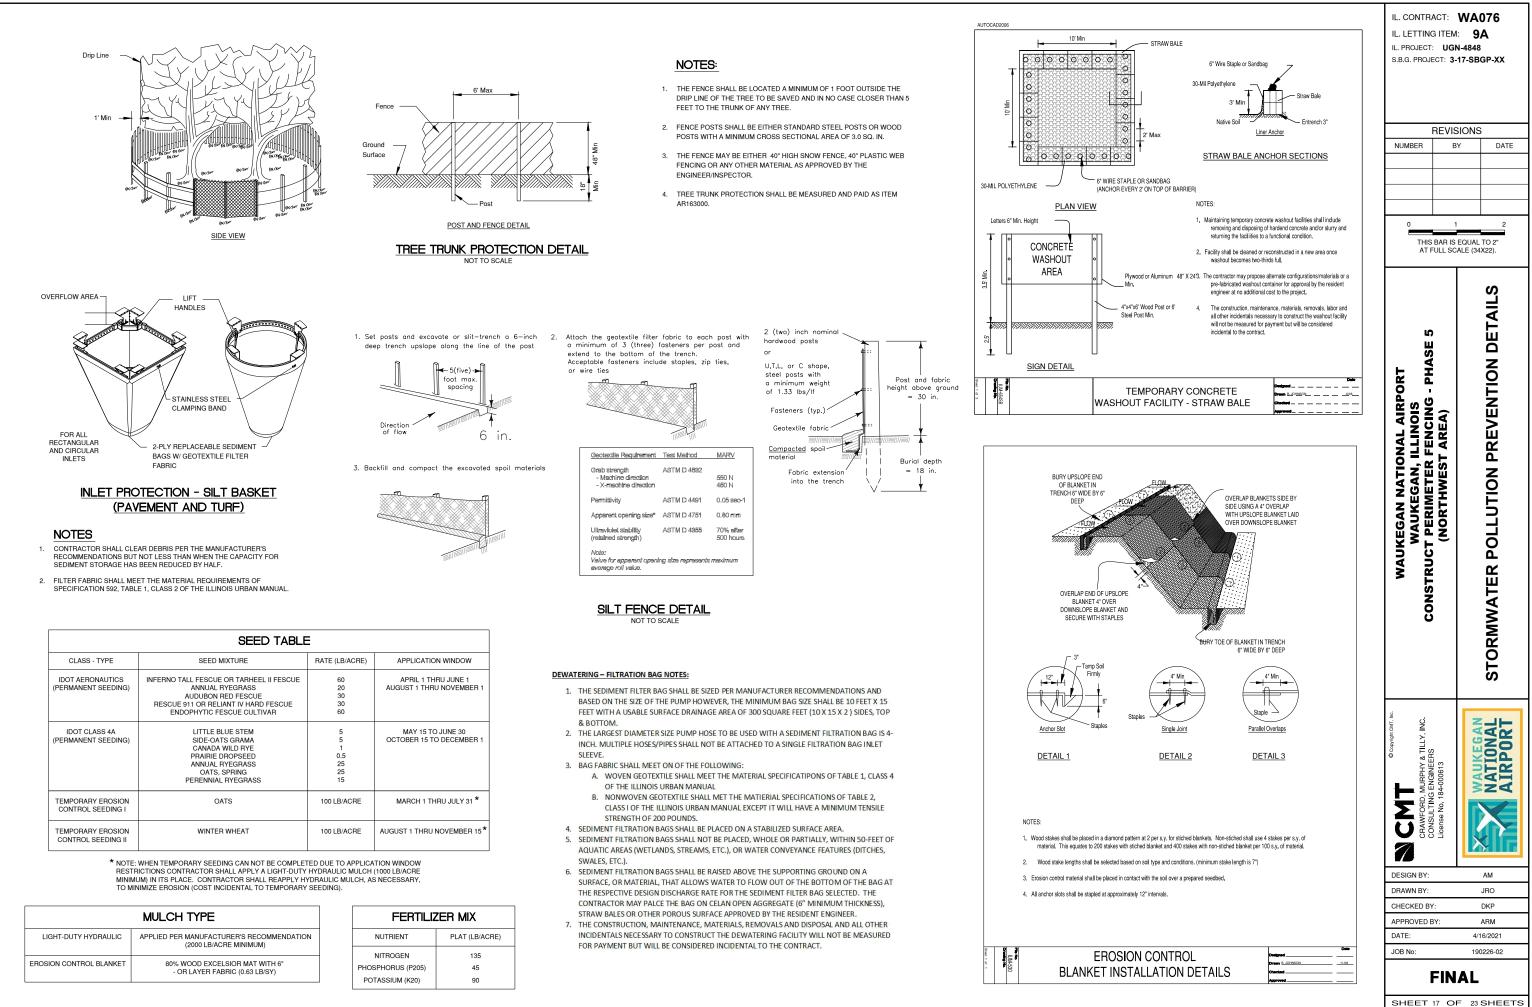


UPDATE

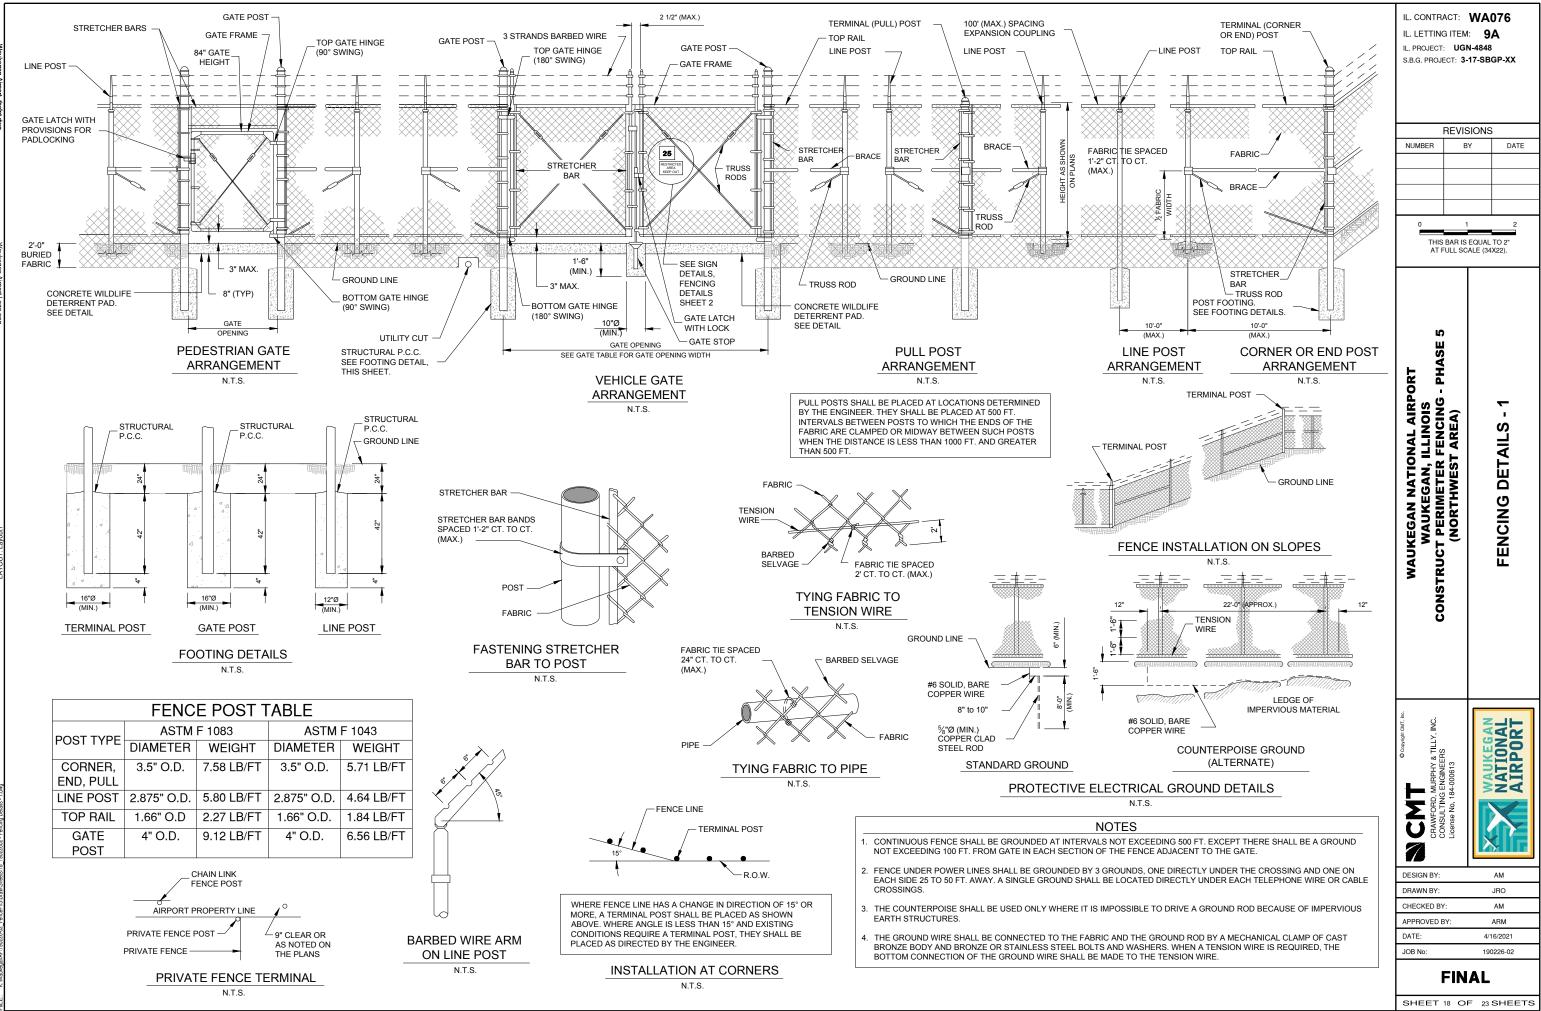


UPDATE BY: Jim Of LAVOLIT- Lavourt

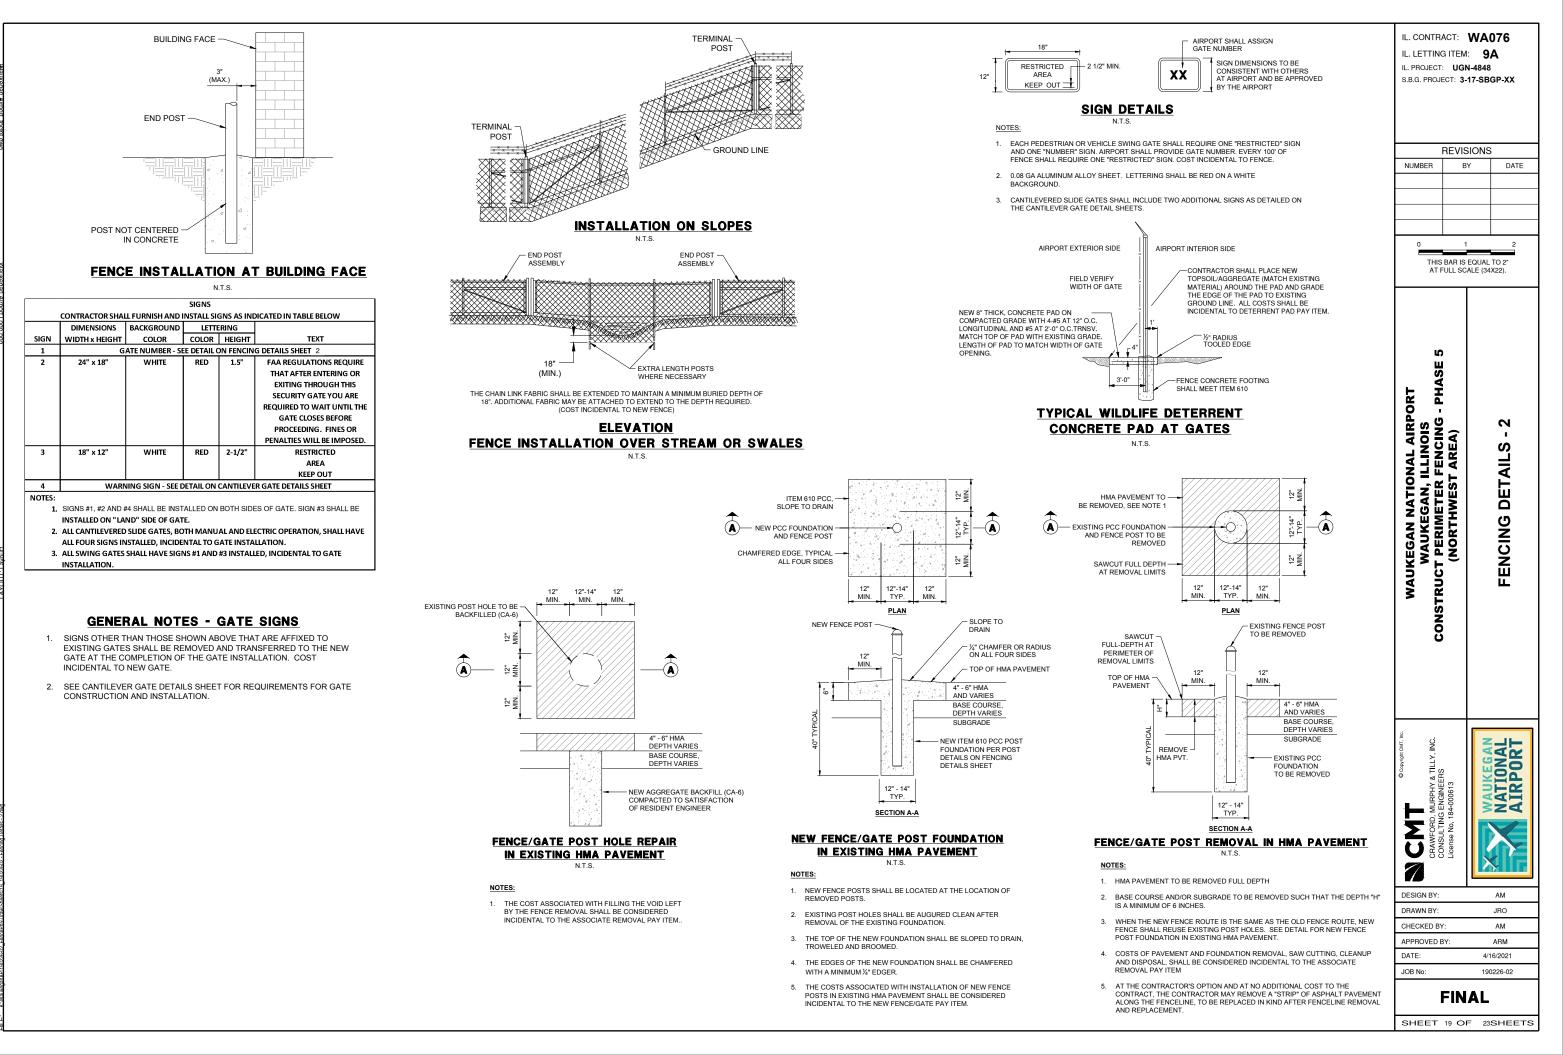


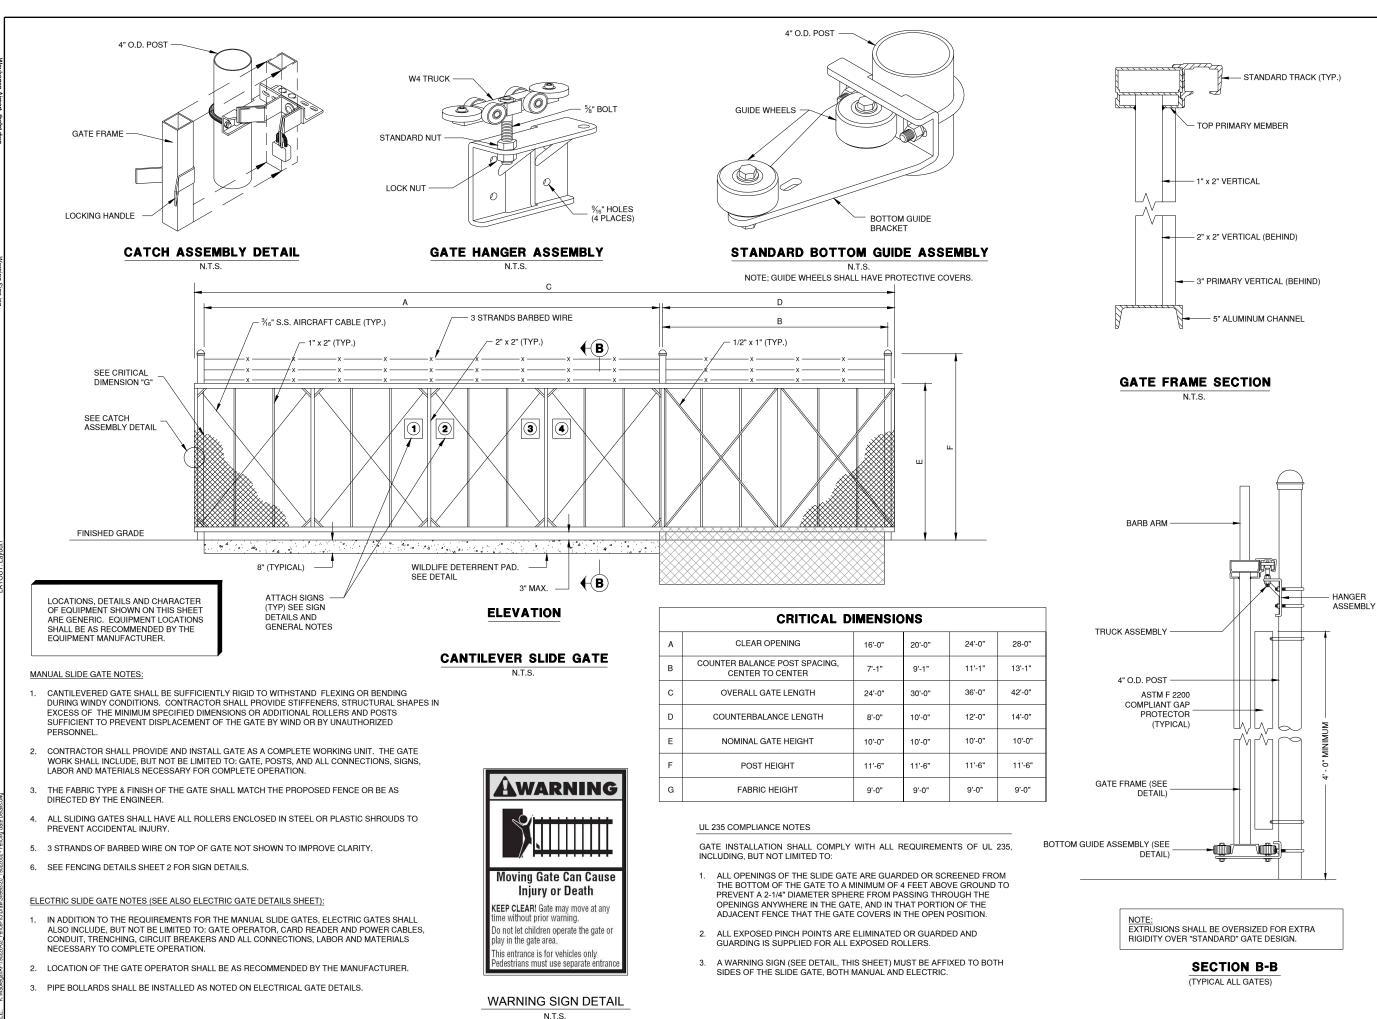

gan Airport Logo.png

UPDATE BY: Jim Ohs



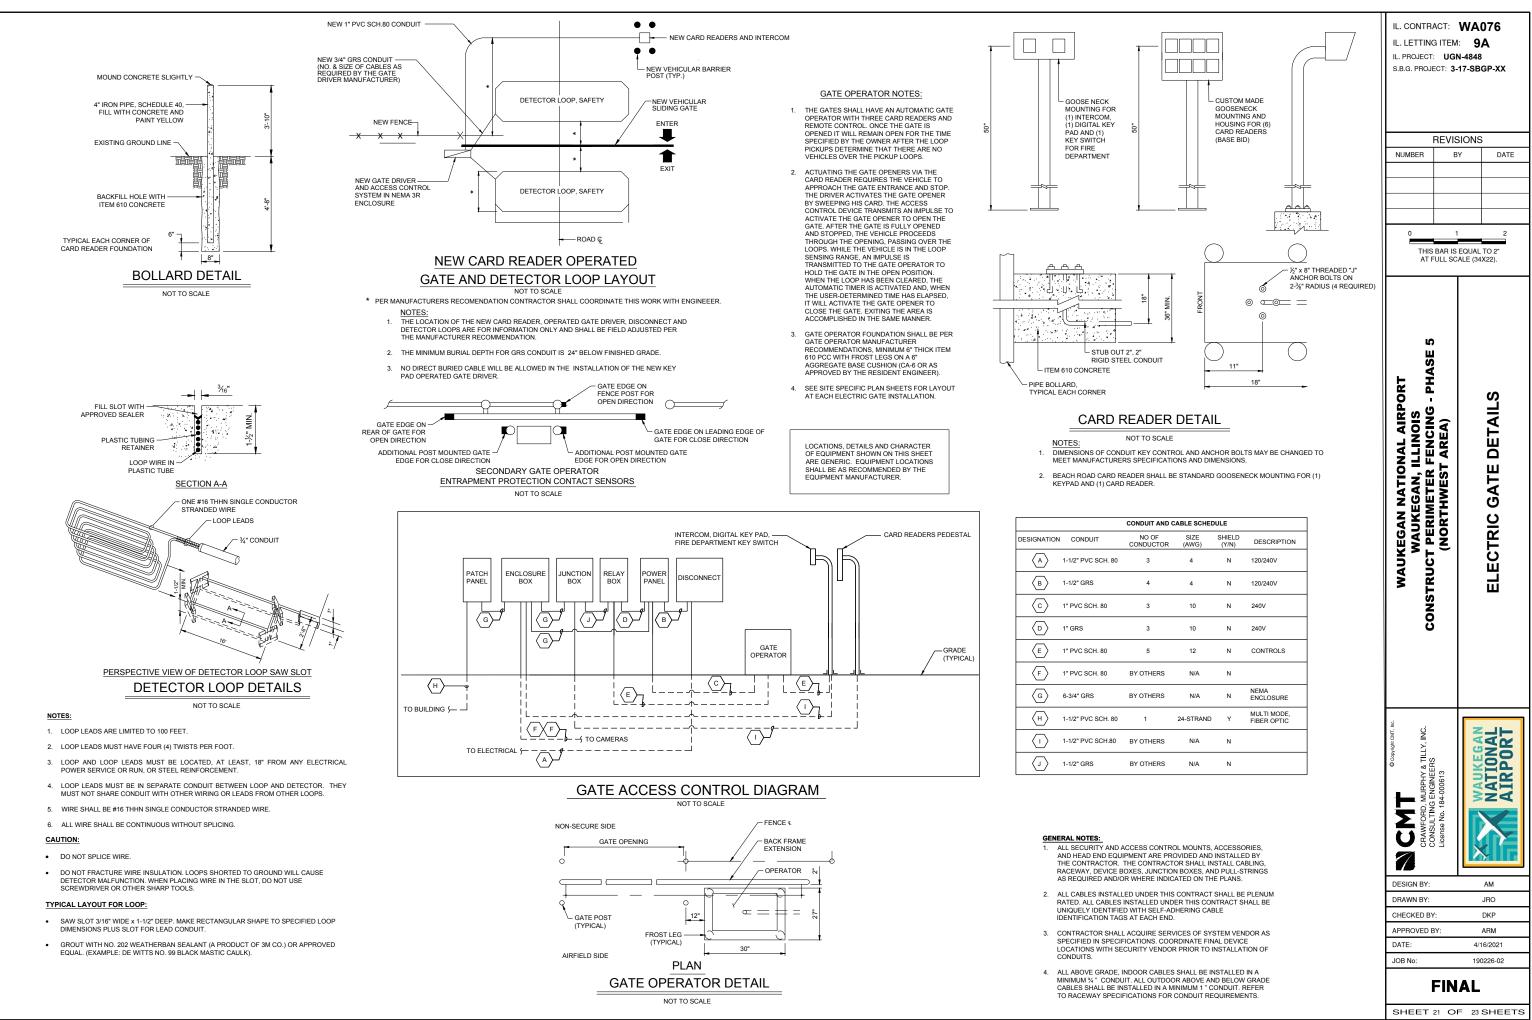


CONDUIT AND CABLE SCHEDULE							
NO OF CONDUCTOR	SIZE (AWG)	SHIELD (Y/N)	DESCRIPTION				
3	4	Ν	120/240V				
4	4	Ν	120/240V				
3	10	Ν	240V				
3	10	Ν	240V				
5	12	Ν	CONTROLS				
BY OTHERS	N/A	Ν					
BY OTHERS	N/A	Ν	NEMA ENCLOSURE				
1	24-STRAND	Y	MULTI MODE, FIBER OPTIC				
BY OTHERS	N/A	Ν					
BY OTHERS	N/A	Ν					


PANEL DESIGNATION: PP-2 LOCATION: OUTDOOR MFR & TYPE: SQUARE D, OR EQUIV.

NOTES

- 1. ALL EQUIPMENT SHOWN IS NEW, UNLESS OTHERWISE NOTED.
- 2. ALL CIRCUIT BREAKERS SHALL BE GFCI.
- ALL EXPOSED CONDUIT SHALL BE RIGID GALVANIZED STEEL 3. AND TRANSITION UNDERGROUND TO PVC SCH. 80, UNLESS OTHERWISE NOTED.
- 4. CONDUITS SHALL BE SECURED TO UNISTRUT FRAME WITH CONDUIT CLAMP.

	VOLTS: 120/240V				м		CUD	ACE			BUS RATI	
	PHASE: 1				MOUNTING: SURFACE ENCL RATING: NEMA 3R						BUS RATI	40 (A
		WIRE: 3			LING	LIVATING.	HL H	4		MA	AIN CIRCUIT	BRE
CKT		BREAKER	LOAD	USAGE	HASE AM	PS	POLE	PI	HASE AM	s	USAGE	L
NO.	LOAD	SIZE	AMPS	FACTOR	A	В	NO.		A	В	FACTOR	AI
1	CONVENIENCE RECEPTACLE	20A/1P	1.8	0.05	1.5		1	2	0.875		0.5	1
3	TVSS	20A/1P				0.09	3	4		0.875	0.5	1
5	SPARE	20A/1P			0		5	6	0.68		0.1	
7	SPARE	20A/1P				0	7	8		0.68	0.1	6
9	SPARE	20A/1P			0		9	10	0			
11	SPARE	20A/1P				0	11	12		0		
13	SPARE	20A/1P			0		13	14	0			
15	SPARE	20A/1P				0	15	16		0		
17	SPARE	20A/1P			0		17	18	0			
	SECTION TOTAL:				1.5	0.09			1.555	1.555		
									A	В	_	
					PHASE	TOTALA	MPS:		3.055	1.645		
									A	В		
					PH	ASE TOTA	LVA:		366.6	197.4		



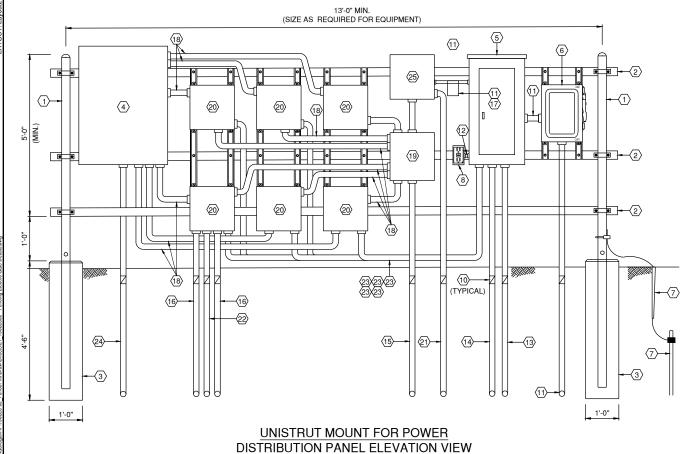


NOT TO SCALE

EQUIPMENT NOMENCLATURE

- $\langle 1 \rangle$ 3" GRS CONDUIT PEDESTAL SUPPORT WITH END CAPS
- 2 12 GAUGE GALVANIZED STEEL UNITSTRUT
- (3) 12" DIA. x 4'-6" DEEP CONCRETE FOUNDATION
- 4 12 PORT PATCH PANEL, 24" x 24" x 12" NEMA 3R WITH BACK PANEL.
- 5 POWER PANEL "PP-2", 60A, 120/240V, 1-PHASE, NEMA 3R WITH 60A MAIN CIRCUIT BREAKER
- 6 NON-FUSED DISCONNECT, 60A, 240V, 2-POLE, NEMA 3R.
- 1/C #6 GROUNDING ELECTRODE CONDUCTOR IN 1" PVC $\langle 7 \rangle$ SCH.40 CONDUIT, EXOTHERMIC WELDED TO 3/4" DIA. x 10'-0" LONG GROUND ROD.
- CONVENIENCE OUTLET, 20A, 120V, DUPLEX GFCI RECEPTACLE IN WEATHERPROOF ENCLOSURE. $\langle 8 \rangle$
 - (9) 6-FT WIDE, 4-FT DEEP, 4-INCH THICK CONCRETE SLAB
 - (10) PVC TO GRS CONDUIT ADAPTER
 - (11) 3-#4 XLP-USE, 1-#8 GND. IN 1-1/2" CONDUIT.
- (12) 2-#12 XLP-USE, 1-#10 GND. IN 3/4" CONDUIT
- (13) 2-#10 XLP-USE, 1-#10 GND. IN 1-1/2" CONDUIT TO GATE OPERATOR.
- (14) 2-#10 XLP-USE, 1-#10 GND. IN 1-1/2" CONDUIT TO OUTDOOR LIGHTS.
- $\left< \underline{15} \right> \ \ \mbox{PULL STRING IN 1-1/2" CONDUIT TO CARD READER}$
- (16) PULL STRING IN 1" CONDUIT TO CAMERA
- (17) TVSS IN NEMA 3R ENCLOSURE
- 18 PULL STRING IN 1" CONDUIT
- (19) JUNCTION BOX 12" X 12" X 12" NEMA 3R ENCLOSURE WITH BACK PANEL
- 20 12" X 12" X 12" NEMA 3R ENCLOSURE WITH BACK PANEL
- PULL STRING IN 1" CONDUIT TO GATE OPERATOR 21
- 22 PULL STRING IN 1" CONDUIT TO INTERCOM
- 23 PULL STRING IN 3/4" CONDUIT
- 24> 24 PAIR MULTI-MODE FIBER OPTIC CABLE IN 1-1/2" CONDUIT
- **25** GATE OPERATOR RELAY BOX, 12" x 12" x 12" NEMA 3R ENCLOSURE WITH BACK PANEL (RELAYS TO BE PROVIDED BY OTHERS)

ENTRANCE INTO BUILDING. RGS, UNLESS OTHERWISE NOTED. (COST INCIDENTAL TO AR800188)

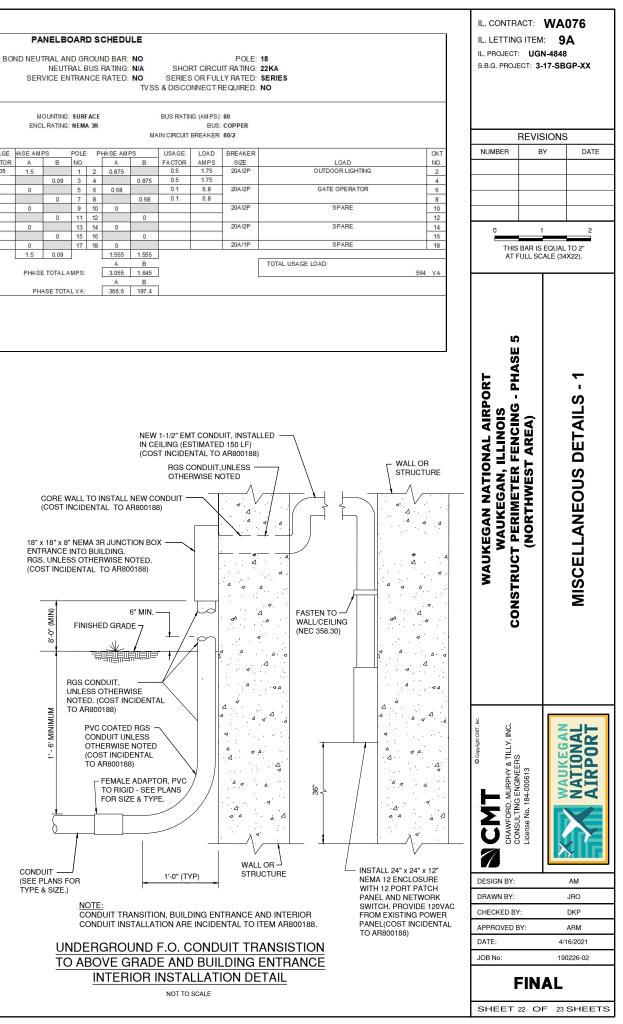

UPDATE

