



Illinois Department of Transportation

Office of Intermodal Project Implementation / Division of Aeronautics
1 Langhorne Bond Drive / Springfield, Illinois 62707-8415

June 2, 2026

SUBJECT: Central Illinois Regional Airport
Bloomington, Illinois
McLean County
Illinois Project Number: BMI-5258
AIP Project Number: 3-17-0006-TBD
Contract No. BL074
Item No. 06A, June 12, 2026 Letting
Addendum B

NOTICE TO PROSPECTIVE BIDDERS

Attached is an addendum to the plans or proposal. This addendum involves revised and/or added material.

Reason for Addendum:

Revised Plan Sheets and Specifications

To All Plan Holders:

This addendum forms a part of the bidding and contract documents and modifies the original bidding documents dated May 1, 2026

Plan Changes:

Sheet 3

REVISE Summary of Quantities to revise the pay item unit.

Sheet 49

ADD note to clarify location on Temporary markings.

Sheet 50

ADD note to clarify location on Temporary markings.

Special Provisions Changes:

Section 80-02

REVISE the second sentence to the following:

"The Contractor is expected to commence project operations within **10** days of the NTP date."

Schedule of Prices Changes:

N/A

Prime contractors must utilize the enclosed material when preparing their bid and must include any changes to the Schedule of Prices in their bid.

Questions on this addendum may be directed to Dillon Ruholl of Crawford, Murphy & Tilly at 217-572-1069.

Path: K:\Bloomington\Ap\21008501-00_RehabRwy1120\Draw\Sheets\Phase 2\21008520-PH2-GI002.dwg
Date: Tuesday, June 2, 2026 10:24:30 AM

ITEM NO.	ITEM DESCRIPTION	UNIT	TOTAL QTY
AW108065	RGL CABLE	FOOT	4650
AW108706	1/C #6 COUNTERPOISE	FOOT	4200
AW110102	DUCT MARKER - IN PAVEMENT	EACH	17
AW125565	SPLICE CAN	EACH	9
AW125740	RUNWAY GUARD LIGHT	EACH	8
AW125906	REMOVE SPLICE CAN	EACH	4
AW125946	ADJUST SPLICE CAN	EACH	5
AW150510	ENGINEER'S FIELD OFFICE	L SUM	1
AW150520	MOBILIZATION	L SUM	1
AW150550	CONSTRUCTION ACCESS	L SUM	1
AW150552	RESTORE CONSTRUCTION ACCESS	L SUM	1
AW152451	SHOULDER EMBANKMENT	CU YD	2150
AW152515	SUBGRADE UNDERCUT	CU YD	1200
AW156510	SILT FENCE	FOOT	1450
AW156520	INLET PROTECTION	EACH	12
AW209618	CRUSHED AGGREGATE BASE COURSE - 18"	SQ YD	10500
AW401010	CONTRACTOR QUALITY CONTROL PROGRAM	L SUM	1
AW401610	BITUMINOUS SURFACE COURSE	TON	10330
AW401620	BIT. SURFACE COURSE, LEVELING	TON	1800
AW401630	BITUMINOUS SURFACE TEST SECTION	EACH	1
AW403610	BITUMINOUS BASE COURSE	TON	6350
AW403630	BITUMINOUS BASE TEST SECTION	EACH	1
AW401640	BITUMINOUS PAVEMENT GROOVING	SQ YD	33000
AW401655	BUTT JOINT CONSTRUCTION	SQ YD	3375
AW401900	REMOVE BITUMINOUS PAVEMENT	SQ YD	10250
AW602510	BITUMINOUS PRIME COAT	GALLON	3550
AW603510	BITUMINOUS TACK COAT	GALLON	12560
AW620520	PAVEMENT MARKING - WATERBORNE	SQ FT	50300
AW620525	PAVEMENT MARKING - BLACK BORDER	SQ FT	12600
AW620545	PAVEMENT MARKING - WATERBORNE SPHPs	SQ FT	575
AW620900	PAVEMENT MARKING REMOVAL	SQ FT	650
AW705526	6" PERFORATED UNDERDRAIN W/ SOCK	FOOT	1250
AW705546	6" NONPERFORATED UNDERDRAIN	FOOT	170
AW705635	UNDERDRAIN COLLECTION STRUCTURE	EACH	2
AW705645	UNDERDRAIN CONNECTION	EACH	2
AW705900	REMOVE UNDERDRAIN	FOOT	1100
AW705904	REMOVE UNDERDRAIN CLEANOUT	EACH	3
AW705944	ADJUST UNDERDRAIN CLEANOUT	EACH	7
AW801523	ADJUST BASE MOUNTED LIGHT IN TURF	EACH	30
AW801524	ADJUST BASE MOUNTED LIGHT IN PAVEMENT	EACH	33
AW801529	BITUMINOUS PAVEMENT MILLING - 0.75" TO 4" VAR. DEPTH	SQ YD	28750
AW801533	REMOVE SURFACE SENSOR	EACH	2
AW801536	DUST CONTROL	L SUM	1
AW801537	REMOVE AND REPLACE AIRFIELD SIGN	EACH	4
AW801538	BITUMINOUS PAVEMENT MILLING - 1"	SQ YD	2800
AW801539	REMOVE BITUMINOUS ROAD	SQ YD	1450
AW801540	SPARE PARTS	EACH	8
AW801541	CRUSHED AGG BASE COURSE - 10"	SQ YD	1500
AW901510	SEEDING	ACRE	9.4
AW904510	SODDING	SQ YD	2200
AW908515	HEAVY-DUTY HYDRAULIC MULCH	ACRE	9.4

CONTRACT TIME (CALENDAR DAYS)
BASE BID 206



License No. 184-000613
CONSULTANTS

100% FINAL
MAY 1, 2026

REHABILITATE RUNWAY 11/29:
PHASE 2 CONSTRUCTION

OWNER





CENTRAL ILLINOIS REGIONAL
AIRPORT AUTHORITY
CENTRAL ILLINOIS REGIONAL
AIRPORT
BLOOMINGTON, ILLINOIS


	06/02/26	ADDENDUM B
MARK	DATE	DESCRIPTION
AIP PROJ. NO. 3-17-0006-TBD		
IL PROJ. NO. BMI-5258		
CMT PROJECT NO: 21008501.20		
CAD DWG FILE: 21008520-PH2-GI002.DWG		
DESIGNED BY: DJR		
DRAWN BY: DPA		
CHECKED BY: MJD		
APPROVED BY: EMH		
COPYRIGHT:		

SHEET TITLE

SUMMARY OF QUANTITIES



OWNER




MARK	DATE	DESCRIPTION
------	------	-------------

SHEET TITLE

CM102

SHEET 50 OF 70

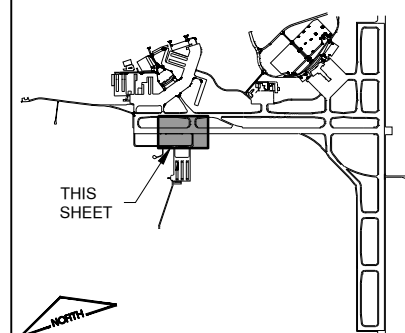

Section 80 Execution and Progress

80-01 Subletting of contract. The Owner will not recognize any subcontractor on the work. The Contractor shall at all times when work is in progress be represented either in person, by a qualified superintendent, or by other designated, qualified representative who is duly authorized to receive and execute orders of the Resident Project Representative (RPR).

The Contractor shall perform, with his organization, an amount of work equal to at least **51** percent of the total contract cost.

Should the Contractor elect to assign their contract, said assignment shall be concurred in by the surety, shall be presented for the consideration and approval of the Owner, and shall be consummated only on the written approval of the Owner.

The Contractor shall provide copies of all subcontracts to the RPR 14 days prior to being utilized on the project. As a minimum, the information shall include the following:

- Subcontractor's legal company name.
- Subcontractor's legal company address, including County name.
- Principal contact person's name, telephone and fax number.
- Complete narrative description, and dollar value of the work to be performed by the subcontractor.
- Copies of required insurance certificates in accordance with the specifications.
- Minority/ non-minority status.

80-02 Notice to proceed (NTP). The Owners notice to proceed will state the date on which contract time commences. The Contractor is expected to commence project operations within **10** days of the NTP date. The Contractor shall notify the RPR at least 72 hours in advance of the time contract operations begins. The Contractor shall not commence any actual operations prior to the date on which the notice to proceed is issued by the Owner.

80-03 Execution and progress. Unless otherwise specified, the Contractor shall submit their coordinated construction schedule showing all work activities for the RPR's review and acceptance at least 10 days prior to the start of work. The Contractor's progress schedule, once accepted by the RPR, will represent the Contractor's baseline plan to accomplish the project in accordance with the terms and conditions of the Contract. The RPR will compare actual Contractor progress against the baseline schedule to determine that status of the Contractor's performance. The Contractor shall provide sufficient materials, equipment, and labor to guarantee the completion of the project in accordance with the plans and specifications within the time set forth in the proposal.

If the Contractor falls significantly behind the submitted schedule, the Contractor shall, upon the RPR's request, submit a revised schedule for completion of the work within the contract time and modify their operations to provide such additional materials, equipment, and labor necessary to meet the revised schedule. Should the execution of the work be discontinued for any reason, the Contractor shall notify the RPR at least 24 hours in advance of resuming operations.
